



Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
								Nov	Dec	Jan	
DC-HYP-FINAL-6 Hyperscale D		399	399	0%	05-Jan-26	15-Jul-27	0				
DC-HYP-FINAL-6.1 Project Man		30	30	0%	05-Jan-26	13-Feb-26	85				
DC-HYP-FINAL-6.1.1 Project Manage		11	11	0%	05-Jan-26	19-Jan-26	44				
PM-001	Notice to Proceed	0	0	0%	05-Jan-26		0				
PM-010	Project Kick-Off Meeting	1	1	0%	05-Jan-26	05-Jan-26	0				
PM-020	Establish Project Organizati	5	5	0%	06-Jan-26	12-Jan-26	49				
PM-030	Establish Project Managem	10	10	0%	06-Jan-26	19-Jan-26	44				
DC-HYP-FINAL-6.1.2 Project Control		30	30	0%	05-Jan-26	13-Feb-26	25				
PC-010	Develop Project Controls Pl	5	5	0%	05-Jan-26	09-Jan-26	25				
PC-020	Develop Detailed Baseline	15	15	0%	12-Jan-26	30-Jan-26	25				
PC-030	Baseline Schedule Review	5	5	0%	02-Feb-26	06-Feb-26	25				
PC-040	Baseline Schedule Approva	5	5	0%	09-Feb-26	13-Feb-26	25				
PC-050	Baseline Programme Appro	0	0	0%		13-Feb-26	25				
DC-HYP-FINAL-6.1.3 HSE Managem		18	18	0%	05-Jan-26	28-Jan-26	45				
HSE-010	Develop Project HSE Plan	10	10	0%	05-Jan-26	16-Jan-26	45				
HSE-020	HSE Plan Review	5	5	0%	19-Jan-26	23-Jan-26	45				
HSE-030	HSE Plan Approval	3	3	0%	26-Jan-26	28-Jan-26	45				
DC-HYP-FINAL-6.1.4 Quality Manage		18	18	0%	05-Jan-26	28-Jan-26	97				
QA-010	Develop Project Quality Pla	10	10	0%	05-Jan-26	16-Jan-26	97				
QA-020	Quality Plan Review	5	5	0%	19-Jan-26	23-Jan-26	97				
QA-030	Quality Plan Approval	3	3	0%	26-Jan-26	28-Jan-26	97				
DC-HYP-FINAL-6.1.5 Contract & Corr		10	10	0%	06-Jan-26	19-Jan-26	44				
COM-010	Establish Contract Administ	5	5	0%	06-Jan-26	12-Jan-26	44				
COM-020	Establish Change and Vari	5	5	0%	13-Jan-26	19-Jan-26	44				
COM-030	Establish Payment and Co	5	5	0%	13-Jan-26	19-Jan-26	44				
COM-040	Establish Commercial Rep	5	5	0%	13-Jan-26	19-Jan-26	44				
DC-HYP-FINAL-6.1.6 Stakeholder & I		20	20	0%	06-Jan-26	02-Feb-26	34				
INT-010	Develop Stakeholder Regis	5	5	0%	06-Jan-26	12-Jan-26	34				
INT-020	Develop Interface Register	10	10	0%	13-Jan-26	26-Jan-26	34				
INT-030	Establish Interface Manage	5	5	0%	27-Jan-26	02-Feb-26	34				
INT-040	Establish Communication a	5	5	0%	13-Jan-26	19-Jan-26	44				
DC-HYP-FINAL-6.2 Design & Ei		90	90	0%	06-Jan-26	11-May-26	134				
DC-HYP-FINAL-6.2.1 Design Manage		71	71	0%	06-Jan-26	14-Apr-26	153				


Actual Level of Effort Remaining Work
 Actual Work Critical Remainin...

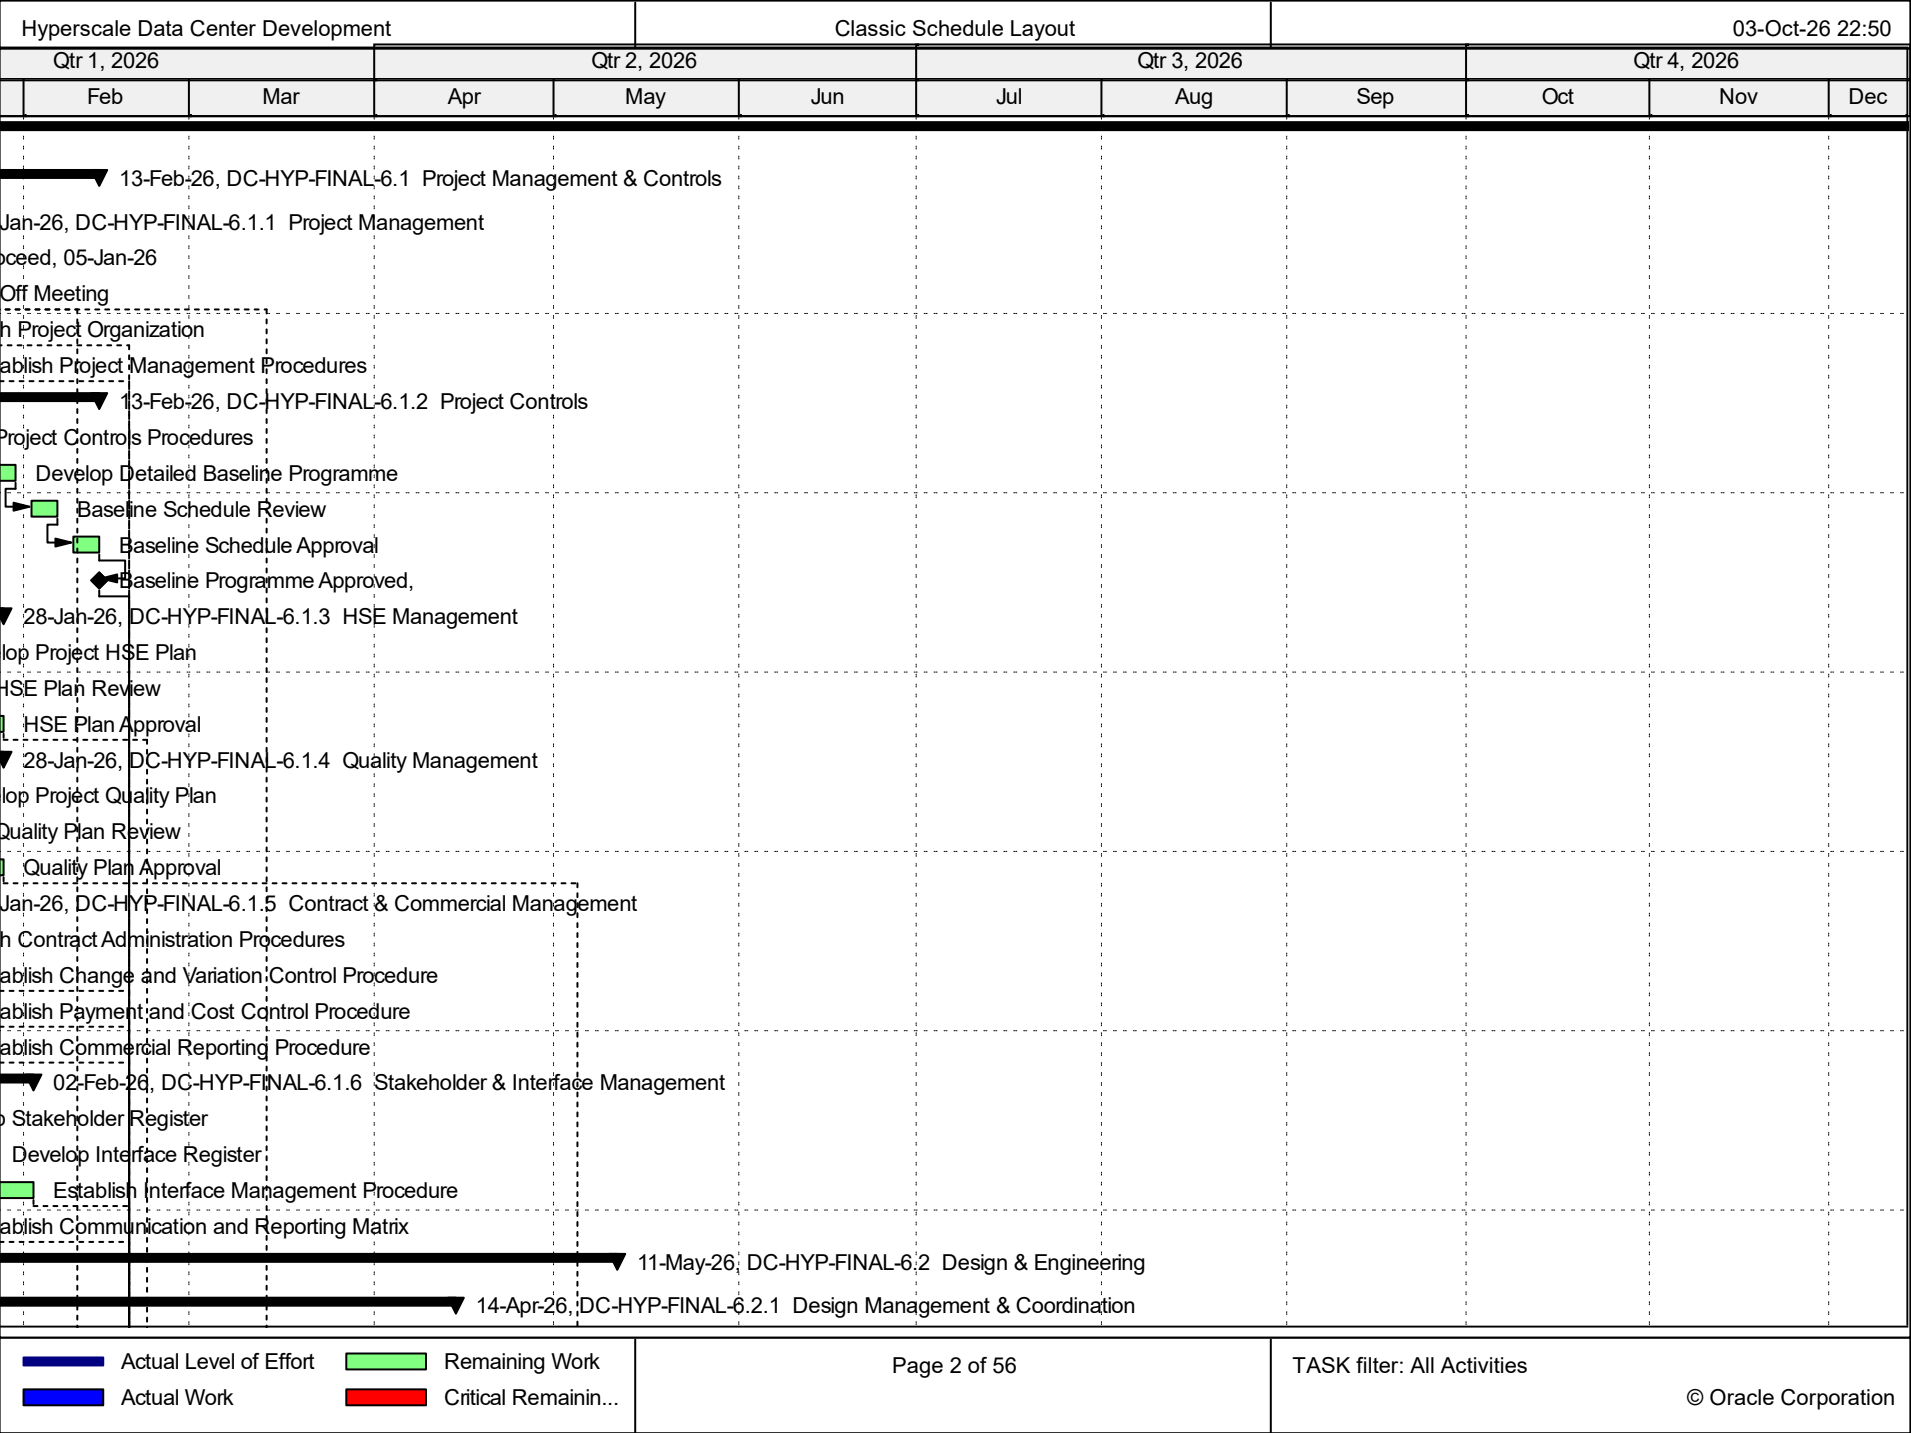

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
								Nov	Dec	Jan	
 DM-010	Establish Design Manager	5	5	0%	06-Jan-26	12-Jan-26	0				Establis
 DM-020	Establish Design Deliverabl	3	3	0%	08-Jan-26	12-Jan-26	174				Establis
 DM-030	Establish Design Responsil	3	3	0%	08-Jan-26	12-Jan-26	174				Establis
 DM-040	Develop Design Coordinati	5	5	0%	13-Jan-26	19-Jan-26	174				De
 DM-050	Conduct Multidiscipline Des	40	40	0%	20-Jan-26	16-Mar-26	174				
 DM-060	Design Coordination Comp	0	0	0%		14-Apr-26	153				
 DC-HYP-FINAL-6.2.2 Civil & Structur		45	45	0%	13-Jan-26	16-Mar-26	64				
 CIV-010	Develop Civil and Structura	5	5	0%	13-Jan-26	19-Jan-26	10				De
 CIV-020	Develop Site Grading and I	10	10	0%	20-Jan-26	02-Feb-26	89				
 CIV-030	Develop Foundation Design	15	15	0%	20-Jan-26	09-Feb-26	84				
 CIV-040	Develop Main Structural Fræ	20	20	0%	20-Jan-26	16-Feb-26	10				
 CIV-050	Develop Equipment Found:	10	10	0%	24-Feb-26	09-Mar-26	64				
 CIV-060	Civil and Structural Design I	5	5	0%	10-Mar-26	16-Mar-26	64				
 CIV-070	Civil and Structural Design /	0	0	0%		16-Mar-26	64				
 DC-HYP-FINAL-6.2.3 Architectural De		30	30	0%	13-Jan-26	23-Feb-26	94				
 ARC-010	Develop Architectural Desig	5	5	0%	13-Jan-26	19-Jan-26	0				De
 ARC-020	Develop Data Hall Layout	10	10	0%	20-Jan-26	02-Feb-26	15				
 ARC-030	Develop Technical Room Li	10	10	0%	20-Jan-26	02-Feb-26	0				
 ARC-040	Develop Building Envelope	15	15	0%	20-Jan-26	09-Feb-26	99				
 ARC-050	Develop Internal Partition a	10	10	0%	03-Feb-26	16-Feb-26	94				
 ARC-060	Architectural Design Review	5	5	0%	17-Feb-26	23-Feb-26	94				
 ARC-070	Architectural Design Approv	0	0	0%		23-Feb-26	94				
 DC-HYP-FINAL-6.2.4 Electrical Desig		52	52	0%	13-Jan-26	25-Mar-26	0				
 ELE-D-01	Develop Electrical Design C	5	5	0%	13-Jan-26	19-Jan-26	0				De
 ELE-D-02	Develop Electrical Load Scl	10	10	0%	20-Jan-26	02-Feb-26	0				
 ELE-D-03	Develop MV Distribution De	15	15	0%	10-Feb-26	02-Mar-26	10				
 ELE-D-04	Develop Transformer Desig	10	10	0%	03-Feb-26	16-Feb-26	20				
 ELE-D-05	Develop Generator System	10	10	0%	03-Feb-26	16-Feb-26	20				
 ELE-D-06	Develop LV Distribution De:	15	15	0%	03-Feb-26	23-Feb-26	0				
 ELE-D-07	Develop UPS and Battery S	15	15	0%	03-Feb-26	23-Feb-26	0				
 ELE-D-08	Develop Busway and Data	15	15	0%	24-Feb-26	16-Mar-26	0				
 ELE-D-09	Develop Earthing and Light	10	10	0%	17-Feb-26	02-Mar-26	10				
 ELE-D-10	Electrical Design Review	7	7	0%	17-Mar-26	25-Mar-26	0				
 ELE-D-11	Electrical Design Approved	0	0	0%		25-Mar-26	0				


 Actual Level of Effort  Remaining Work
 Actual Work  Critical Remainin...

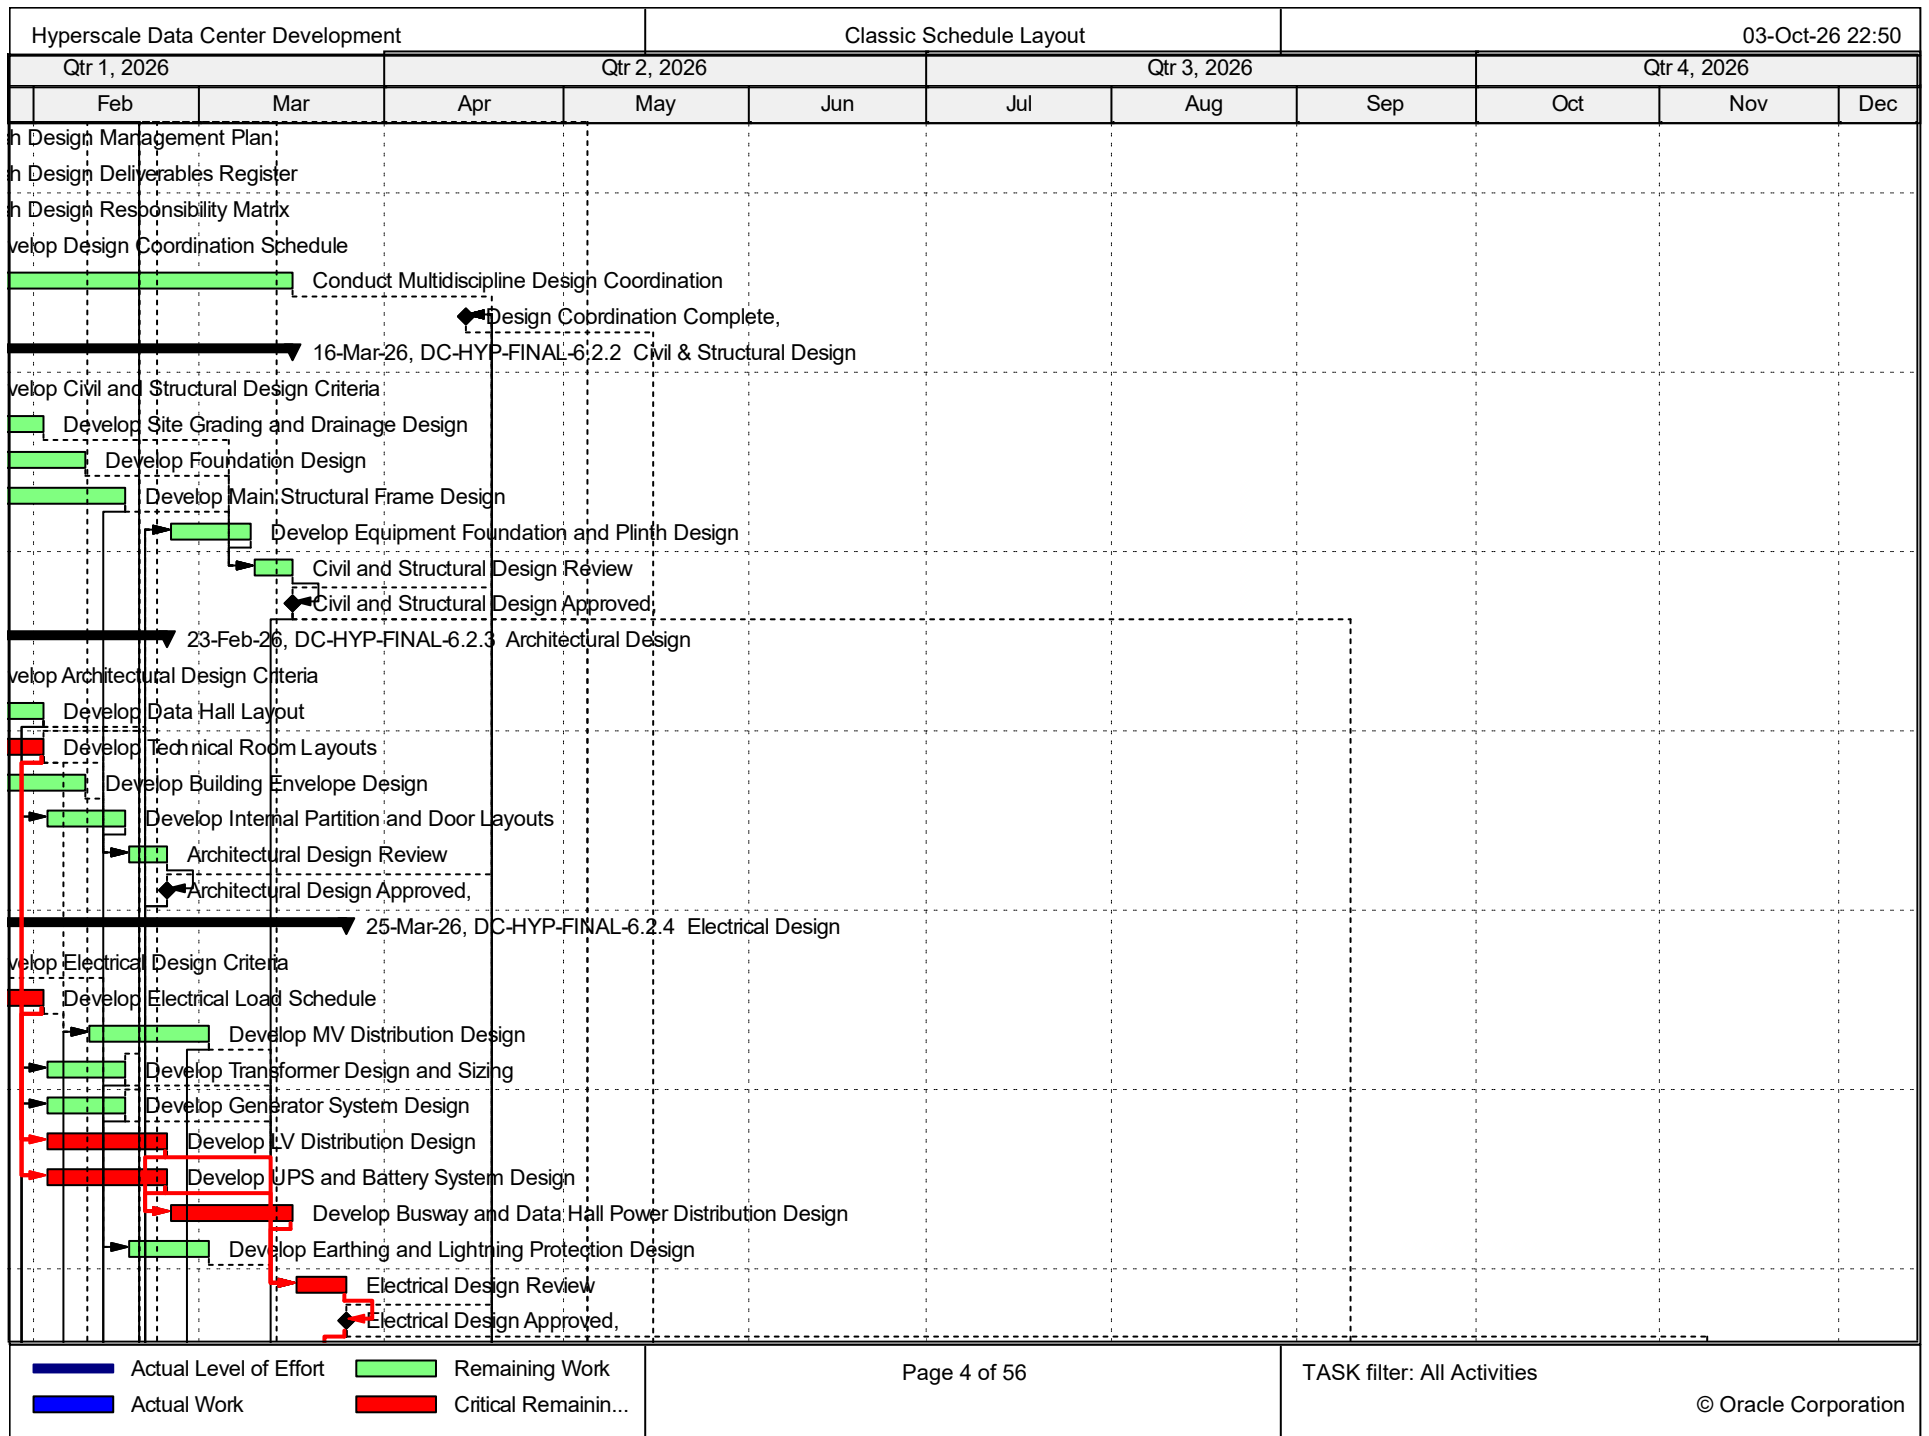

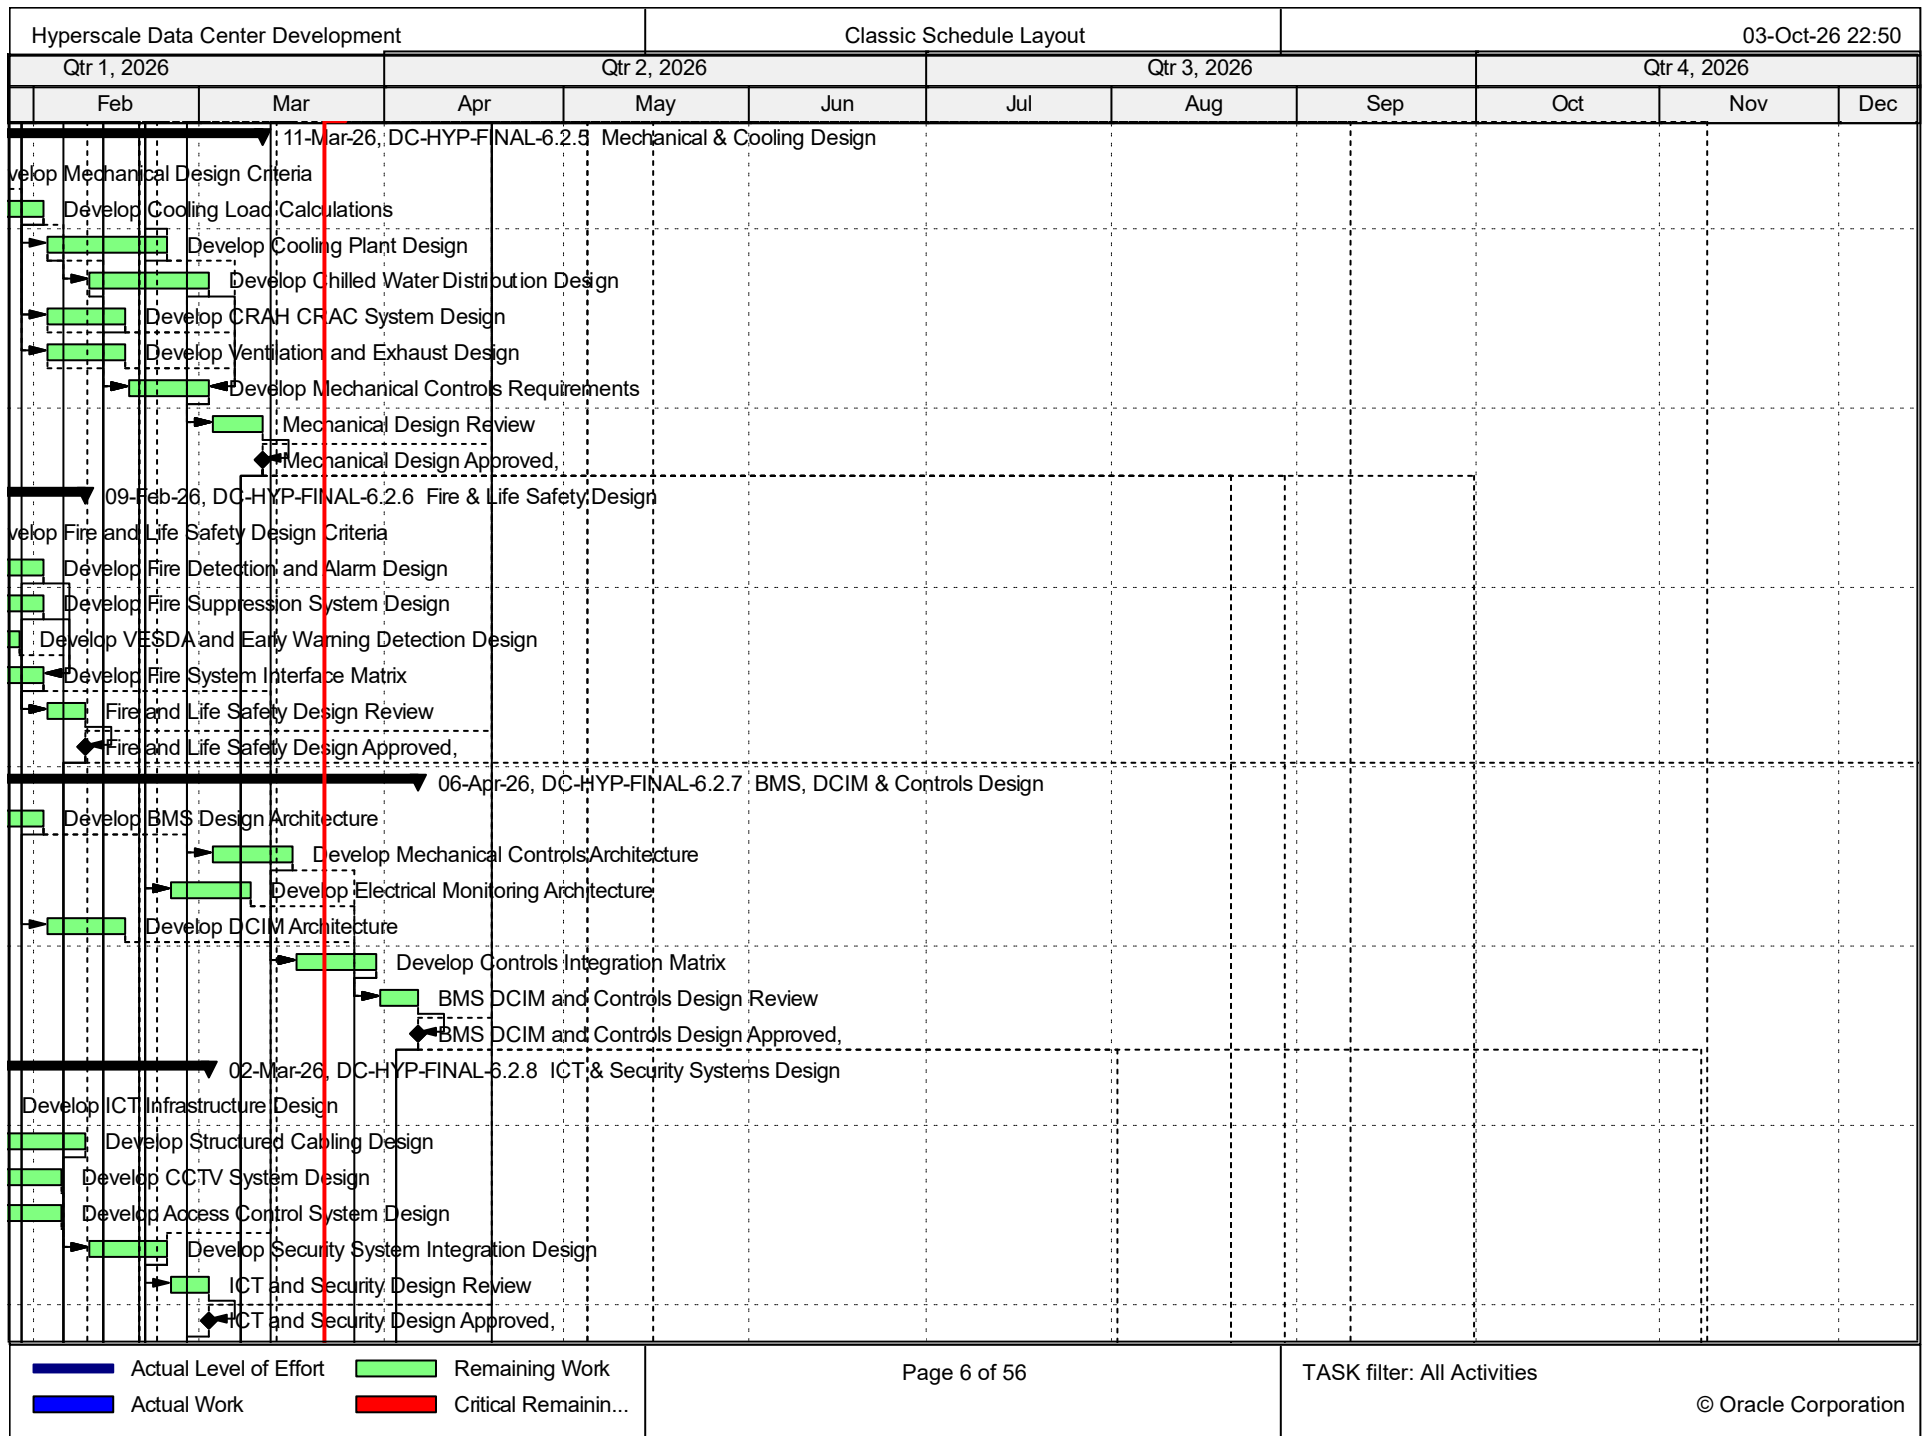

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
								Nov	Dec	Jan	
<											


 Actual Level of Effort  Remaining Work
 Actual Work  Critical Remainin...

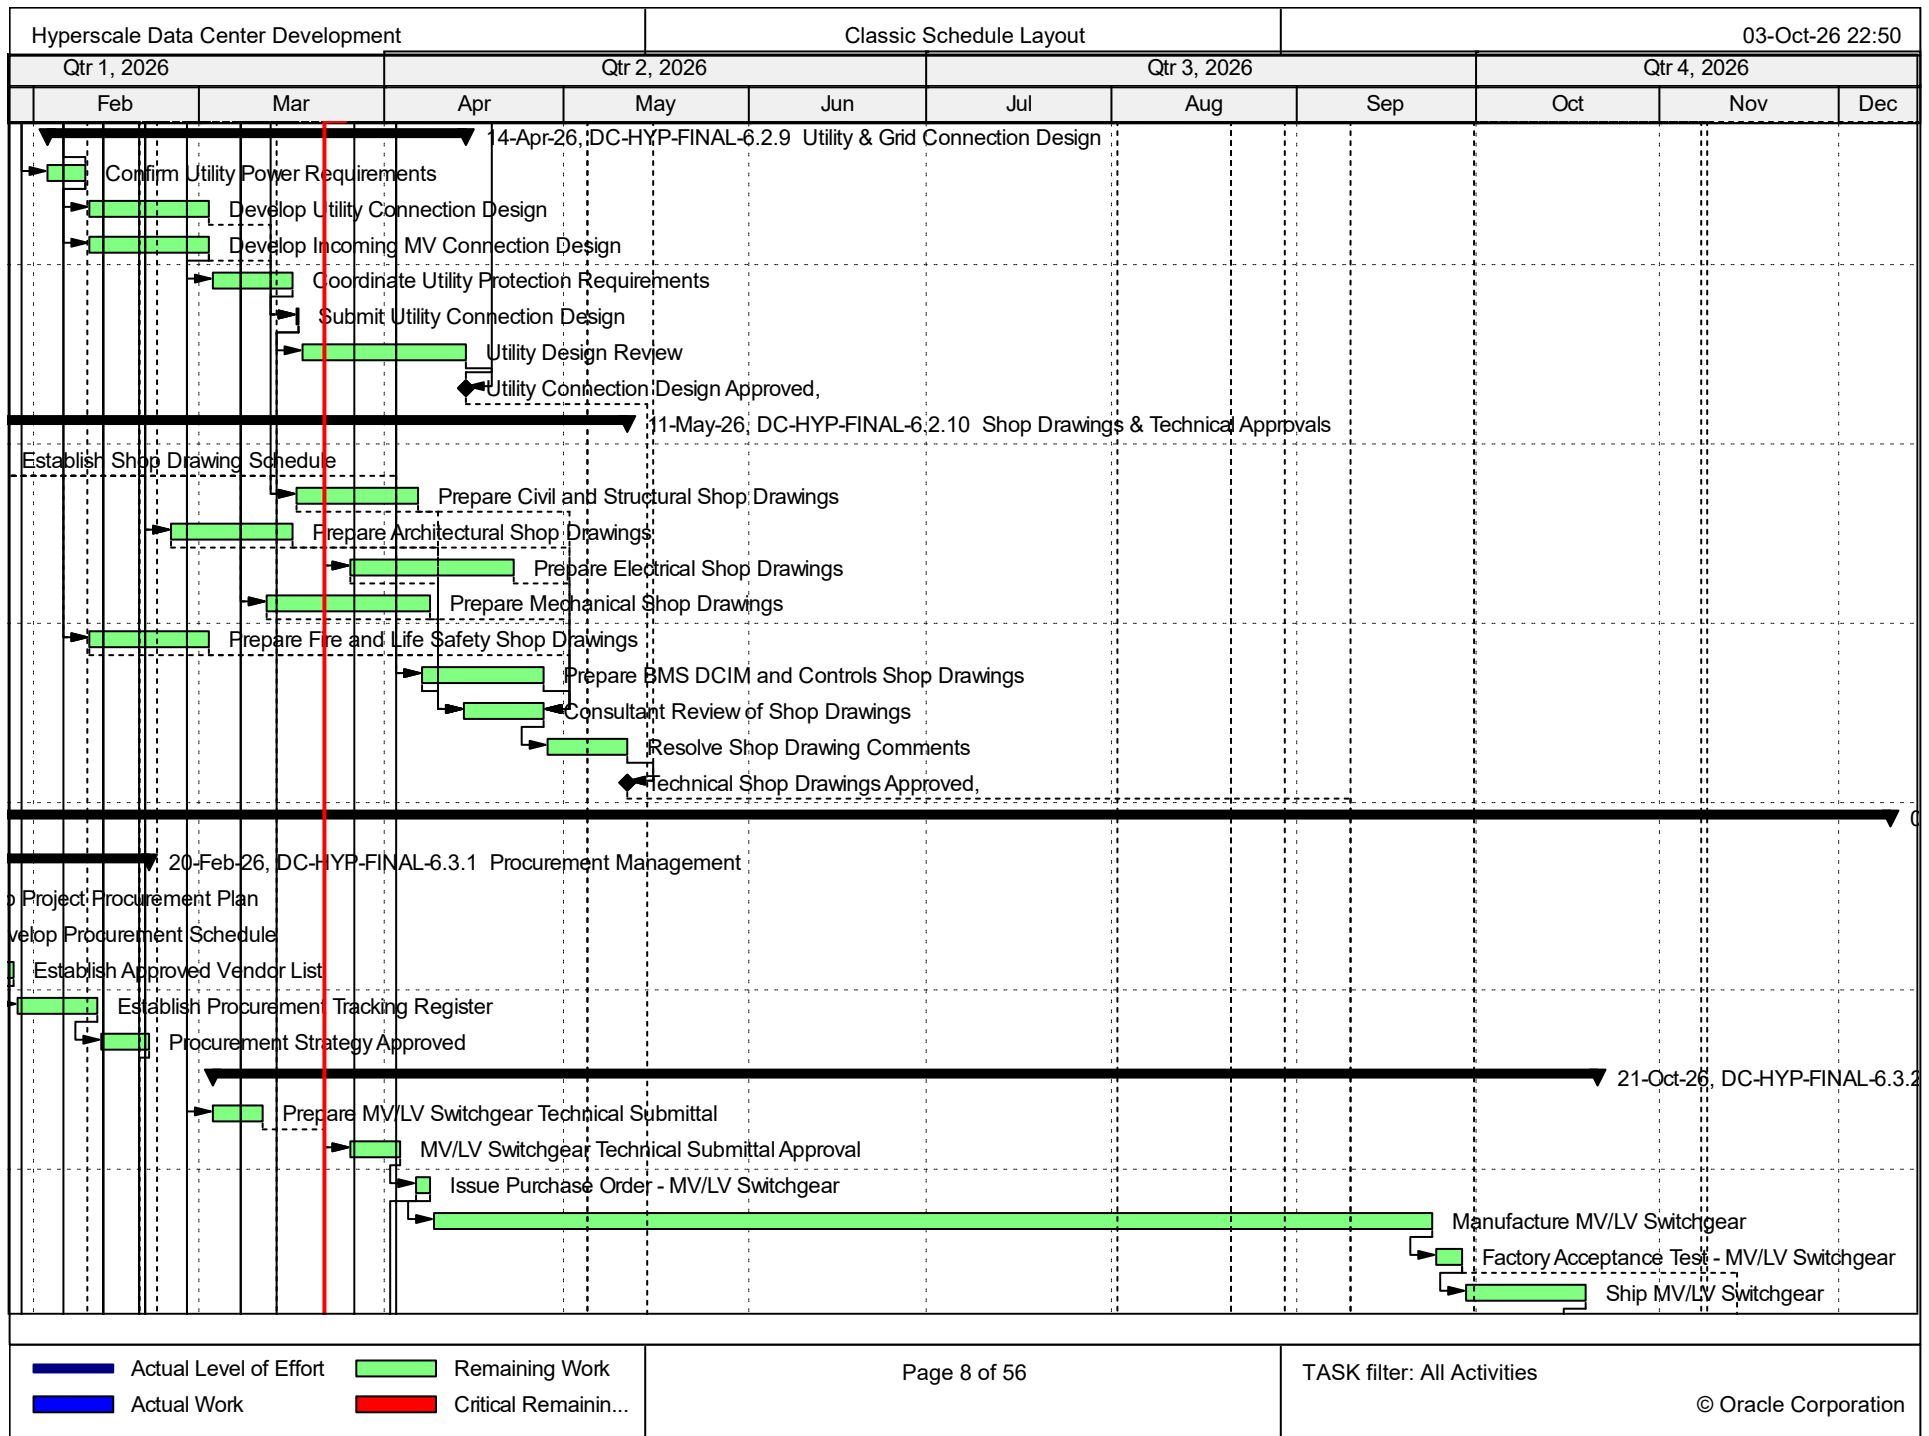

Page 8 of 56

TASK filter: All Activities

© Oracle Corporation

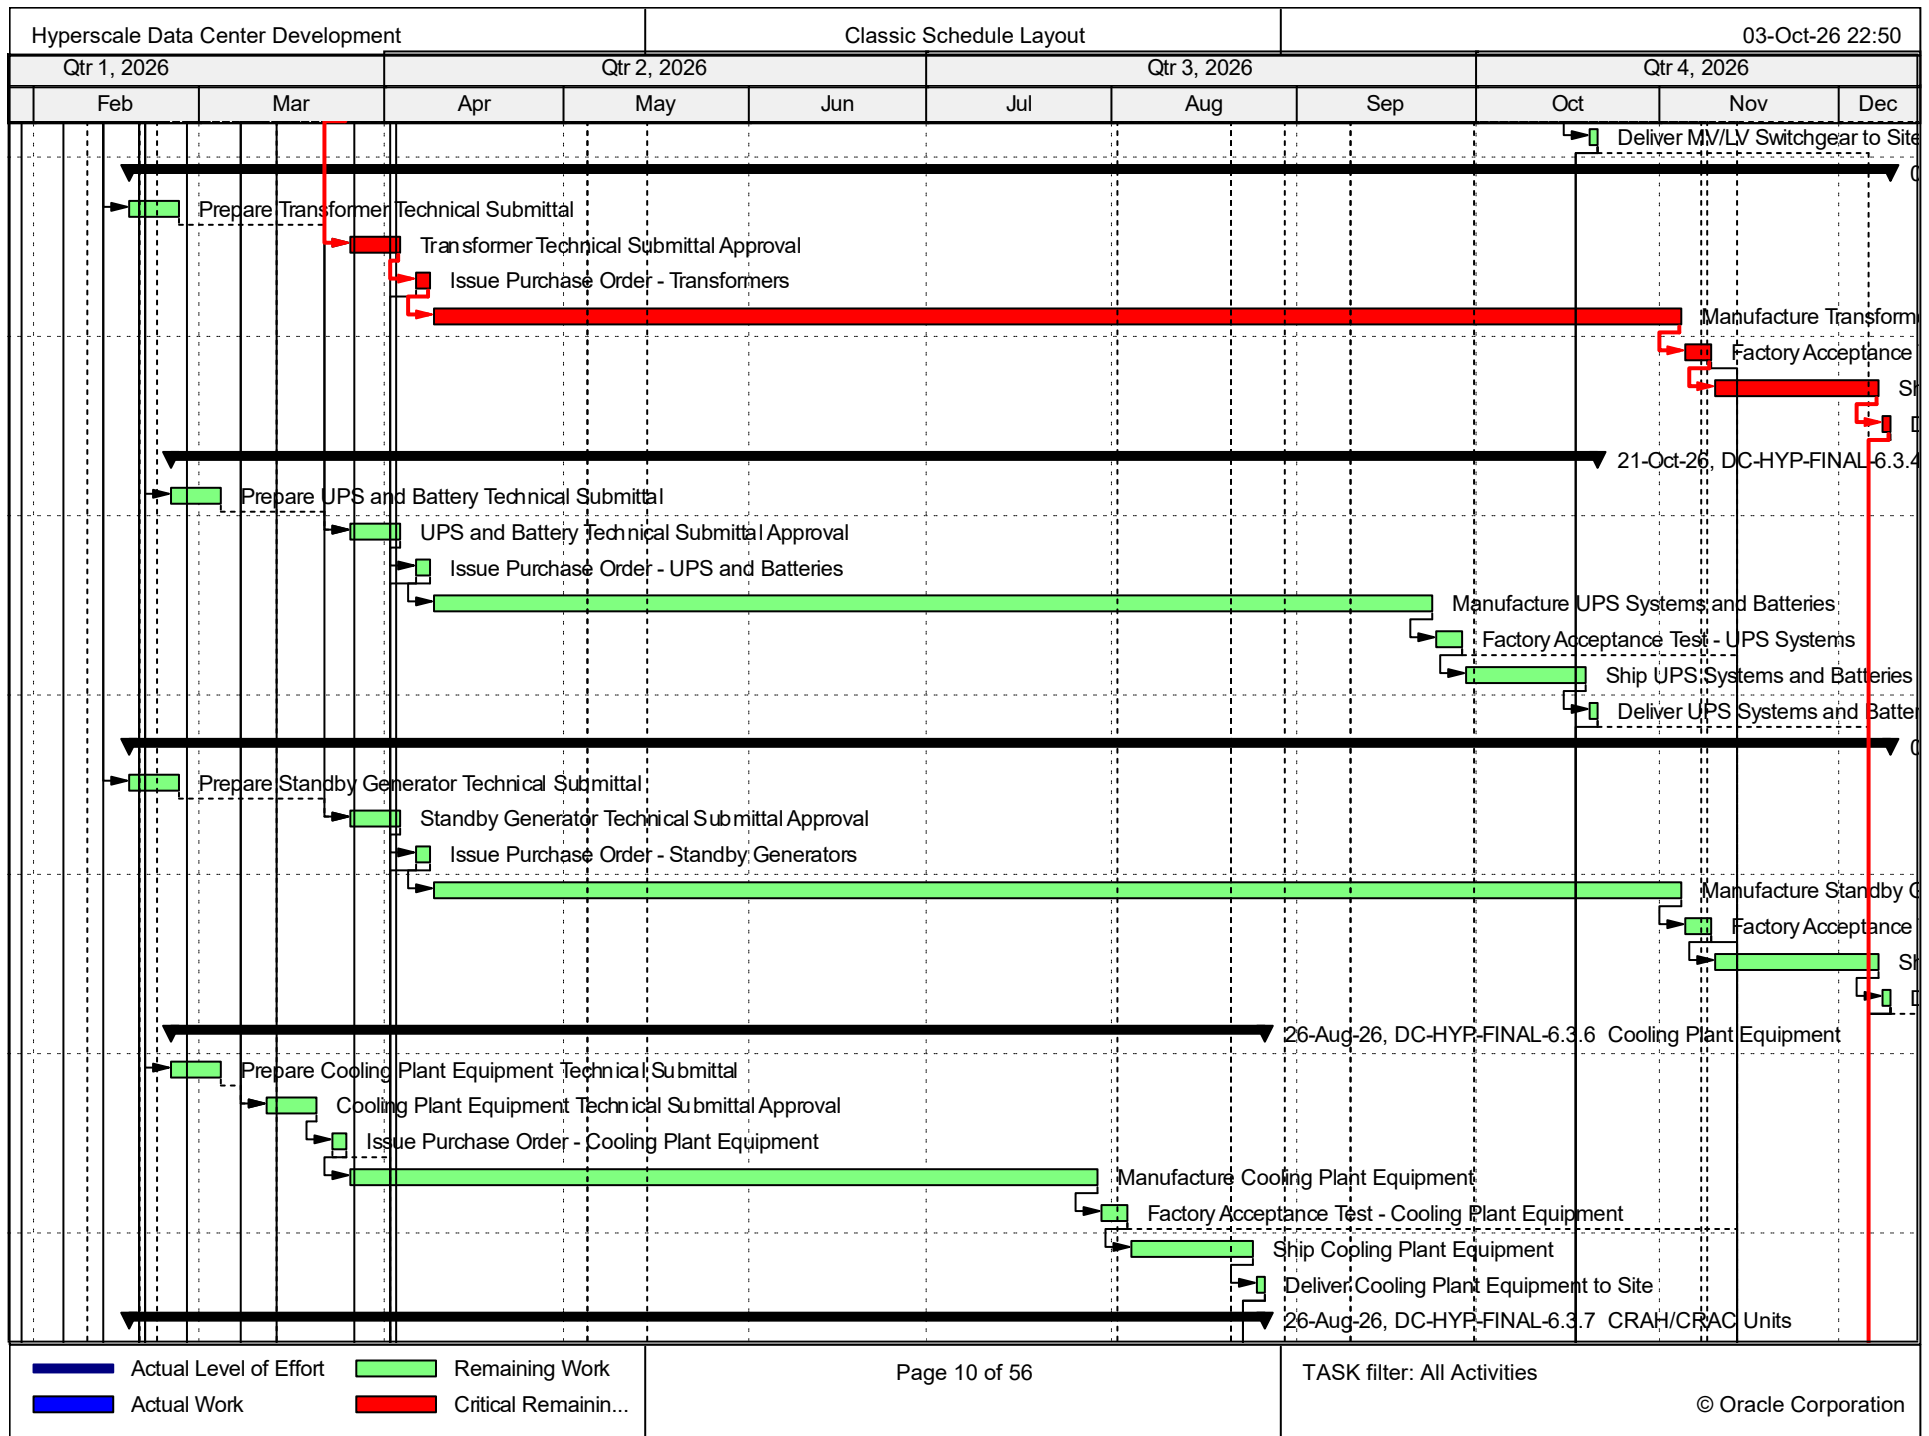

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
■ CRAH-010	Prepare CRAH/CRAC Test	7	7	0%	17-Feb-26	25-Feb-26	62			
■ CRAH-020	CRAH/CRAC Technical Su	7	7	0%	12-Mar-26	20-Mar-26	52			
■ CRAH-030	Issue Purchase Order - CR.	3	3	0%	23-Mar-26	25-Mar-26	52			
■ CRAH-040	Manufacture CRAH/CRAC	90	90	0%	26-Mar-26	29-Jul-26	52			
■ CRAH-050	Factory Acceptance Test - C	3	3	0%	30-Jul-26	03-Aug-26	52			
■ CRAH-060	Ship CRAH/CRAC Units	15	15	0%	04-Aug-26	24-Aug-26	52			
■ CRAH-070	Deliver CRAH/CRAC Units	2	2	0%	25-Aug-26	26-Aug-26	52			
■ DC-HYP-FINAL-6.3.8	Fire & Life Safe	90	90	0%	03-Feb-26	08-Jun-26	144			
■ FLS-P-010	Prepare Fire and Life Safet	5	5	0%	03-Feb-26	09-Feb-26	144			
■ FLS-P-020	Fire and Life Safety Equipm	7	7	0%	10-Feb-26	18-Feb-26	144			
■ FLS-P-030	Issue Purchase Order - Fire	3	3	0%	19-Feb-26	23-Feb-26	144			
■ FLS-P-040	Manufacture Fire and Life S	60	60	0%	24-Feb-26	18-May-26	144			
■ FLS-P-050	Factory Testing - Fire and Li	3	3	0%	19-May-26	21-May-26	144			
■ FLS-P-060	Ship Fire and Life Safety Et	10	10	0%	22-May-26	04-Jun-26	144			
■ FLS-P-070	Deliver Fire and Life Safety	2	2	0%	05-Jun-26	08-Jun-26	144			
■ DC-HYP-FINAL-6.3.9	BMS, DCIM & C	92	92	0%	31-Mar-26	05-Aug-26	82			
■ BMS-P-01	Prepare BMS DCIM and C	5	5	0%	31-Mar-26	06-Apr-26	82			
■ BMS-P-02	BMS DCIM and Controls E	7	7	0%	07-Apr-26	15-Apr-26	82			
■ BMS-P-03	Issue Purchase Order - BM	3	3	0%	16-Apr-26	20-Apr-26	82			
■ BMS-P-04	Configure and Manufacture	60	60	0%	21-Apr-26	13-Jul-26	82			
■ BMS-P-05	Factory Testing - BMS DCIM	5	5	0%	14-Jul-26	20-Jul-26	82			
■ BMS-P-06	Ship BMS DCIM and Contr	10	10	0%	21-Jul-26	03-Aug-26	82			
■ BMS-P-07	Deliver BMS DCIM and Co	2	2	0%	04-Aug-26	05-Aug-26	82			
■ DC-HYP-FINAL-6.3.10	ICT & Security	60	60	0%	24-Feb-26	18-May-26	240			
■ ICT-P-010	Prepare ICT and Security E	5	5	0%	24-Feb-26	02-Mar-26	240			
■ ICT-P-020	ICT and Security Equipmer	5	5	0%	03-Mar-26	09-Mar-26	240			
■ ICT-P-030	Issue Purchase Order - ICT	3	3	0%	10-Mar-26	12-Mar-26	240			
■ ICT-P-040	Procure ICT and Security E	30	30	0%	13-Mar-26	23-Apr-26	240			
■ ICT-P-050	Factory Configuration and 1	5	5	0%	24-Apr-26	30-Apr-26	240			
■ ICT-P-060	Ship ICT and Security Equi	10	10	0%	01-May-26	14-May-26	240			
■ ICT-P-070	Deliver ICT and Security Ec	2	2	0%	15-May-26	18-May-26	240			
■ DC-HYP-FINAL-6.3.11	Architectural &	63	63	0%	24-Feb-26	21-May-26	94			
■ ABM-010	Prepare Architectural Materi	5	5	0%	24-Feb-26	02-Mar-26	94			
■ ABM-020	Architectural Materials Subr	5	5	0%	03-Mar-26	09-Mar-26	94			

■ Actual Level of Effort

■ Actual Work


■ Remaining Work

■ Critical Remainin...

Page 11 of 56

TASK filter: All Activities

© Oracle Corporation

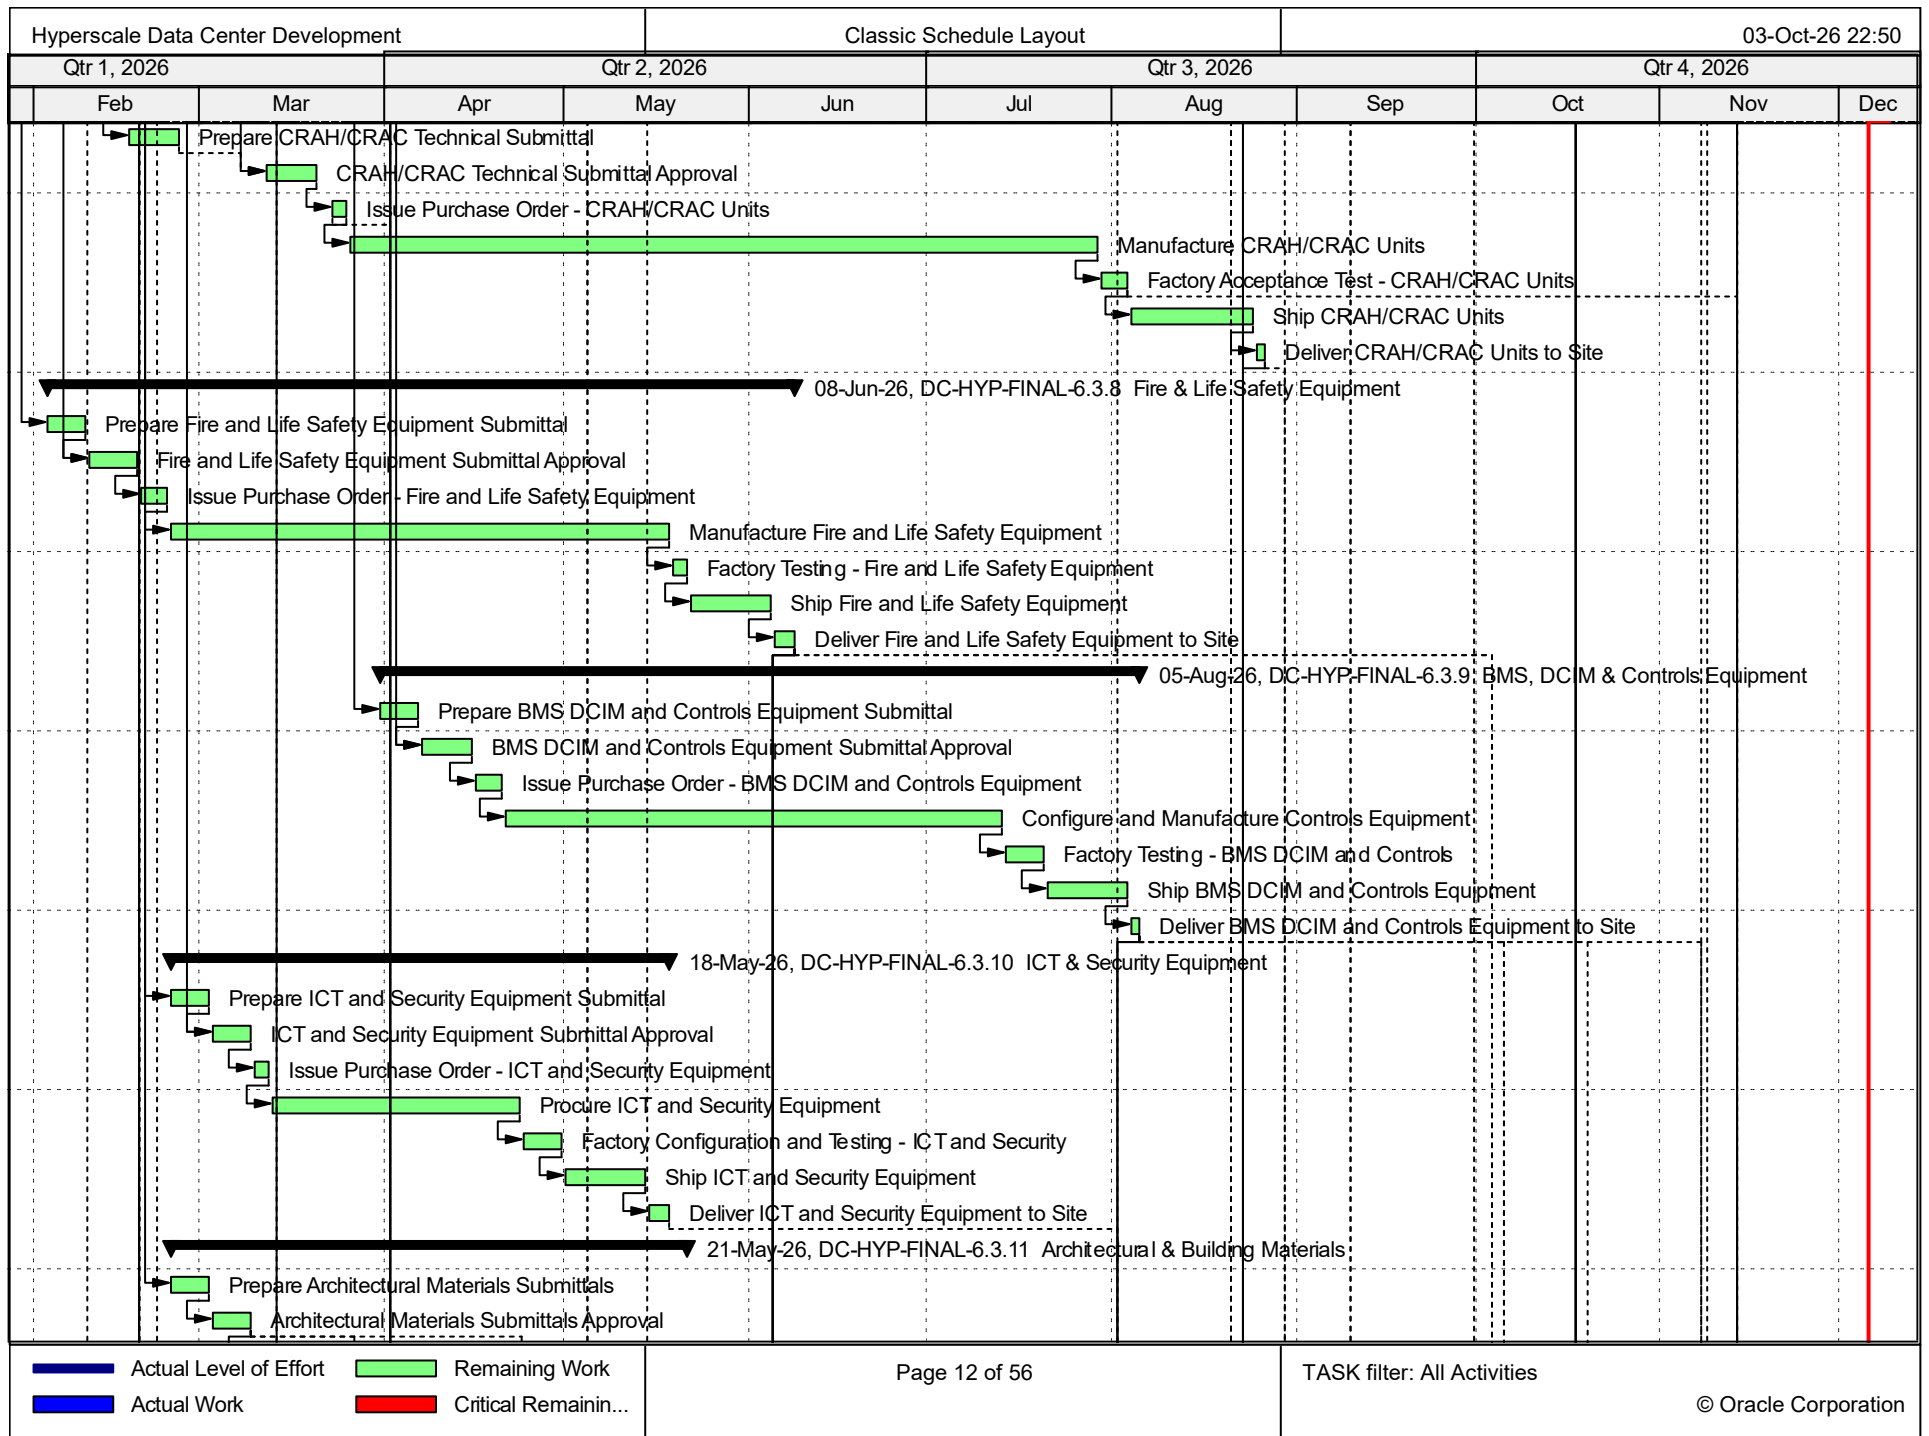

Page 12 of 56

TASK filter: All Activities

© Oracle Corporation

Hyperscale Data Center Development			Classic Schedule Layout				03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
ABM-030	Procure Roofing and Water	15	15	0%	10-Mar-26	30-Mar-26	94			
ABM-040	Procure External Cladding I	20	20	0%	31-Mar-26	27-Apr-26	94			
ABM-050	Procure Doors Louvers and	15	15	0%	28-Apr-26	18-May-26	94			
ABM-060	Deliver Architectural Materie	3	3	0%	19-May-26	21-May-26	94			
DC-HYP-FINAL-6.3.12	Long-Lead Eq	186	186	0%	23-Feb-26	09-Nov-26	54			
LLE-010	Identify Long-Lead Equipm	5	5	0%	23-Feb-26	27-Feb-26	130			
LLE-020	Establish Long-Lead Equipm	5	5	0%	02-Mar-26	06-Mar-26	130			
LLE-030	Confirm Required-on-Site C	5	5	0%	09-Mar-26	13-Mar-26	130			
LLE-040	Monitor Vendor Engineering	90	90	0%	06-Apr-26	07-Aug-26	115			
LLE-050	Monitor FAT and Shipping F	5	5	0%	10-Aug-26	14-Aug-26	115			
LLE-060	Long-Lead Equipment Deliv	0	0	0%		09-Nov-26	54			
DC-HYP-FINAL-6.4	Enabling &	138	138	0%	06-Jan-26	16-Jun-26	269			
DC-HYP-FINAL-6.4.1	Mobilization &	34	34	0%	06-Jan-26	14-Feb-26	30			
MOB-010	Mobilize Project Team to Si	5	5	0%	06-Jan-26	10-Jan-26	54			
MOB-020	Establish Site Offices and V	5	5	0%	12-Jan-26	16-Jan-26	54			
MOB-030	Install Temporary Site Fenci	5	5	0%	12-Jan-26	16-Jan-26	54			
MOB-040	Establish Temporary Storang	5	5	0%	12-Jan-26	16-Jan-26	54			
MOB-050	Establish Site Security and	5	5	0%	12-Jan-26	16-Jan-26	54			
MOB-060	Site Mobilization Complete	0	0	0%	14-Feb-26	14-Feb-26	30			
DC-HYP-FINAL-6.4.2	Surveying & Se	13	13	0%	14-Feb-26	02-Mar-26	89			
SUR-010	Establish Survey Control Pc	3	3	0%	14-Feb-26	17-Feb-26	30			
SUR-020	Conduct Existing Site Topo	5	5	0%	18-Feb-26	23-Feb-26	30			
SUR-030	Verify Existing Site Levels a	2	2	0%	24-Feb-26	25-Feb-26	30			
SUR-040	Set Out Main Building Foot	3	3	0%	26-Feb-26	28-Feb-26	89			
SUR-050	Set Out External Infrastruct	3	3	0%	26-Feb-26	28-Feb-26	89			
SUR-060	Survey and Setting Out Co	0	0	0%	02-Mar-26	02-Mar-26	89			
DC-HYP-FINAL-6.4.3	Site Clearance	27	27	0%	26-Feb-26	30-Mar-26	30			
SCP-010	Clear Existing Vegetation a	7	7	0%	26-Feb-26	05-Mar-26	30			
SCP-020	Remove Existing Surface M	5	5	0%	06-Mar-26	11-Mar-26	30			
SCP-030	Remove or Divert Existing	7	7	0%	12-Mar-26	19-Mar-26	30			
SCP-040	Strip and Stockpile Topsoil	5	5	0%	20-Mar-26	25-Mar-26	30			
SCP-050	Prepare Site for Earthworks	3	3	0%	26-Mar-26	28-Mar-26	30			
SCP-060	Site Clearance Complete	0	0	0%	30-Mar-26	30-Mar-26	30			

Actual Level of Effort

Actual Work

Remaining Work


Critical Remainin...

Page 13 of 56


TASK filter: All Activities


© Oracle Corporation

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
</										

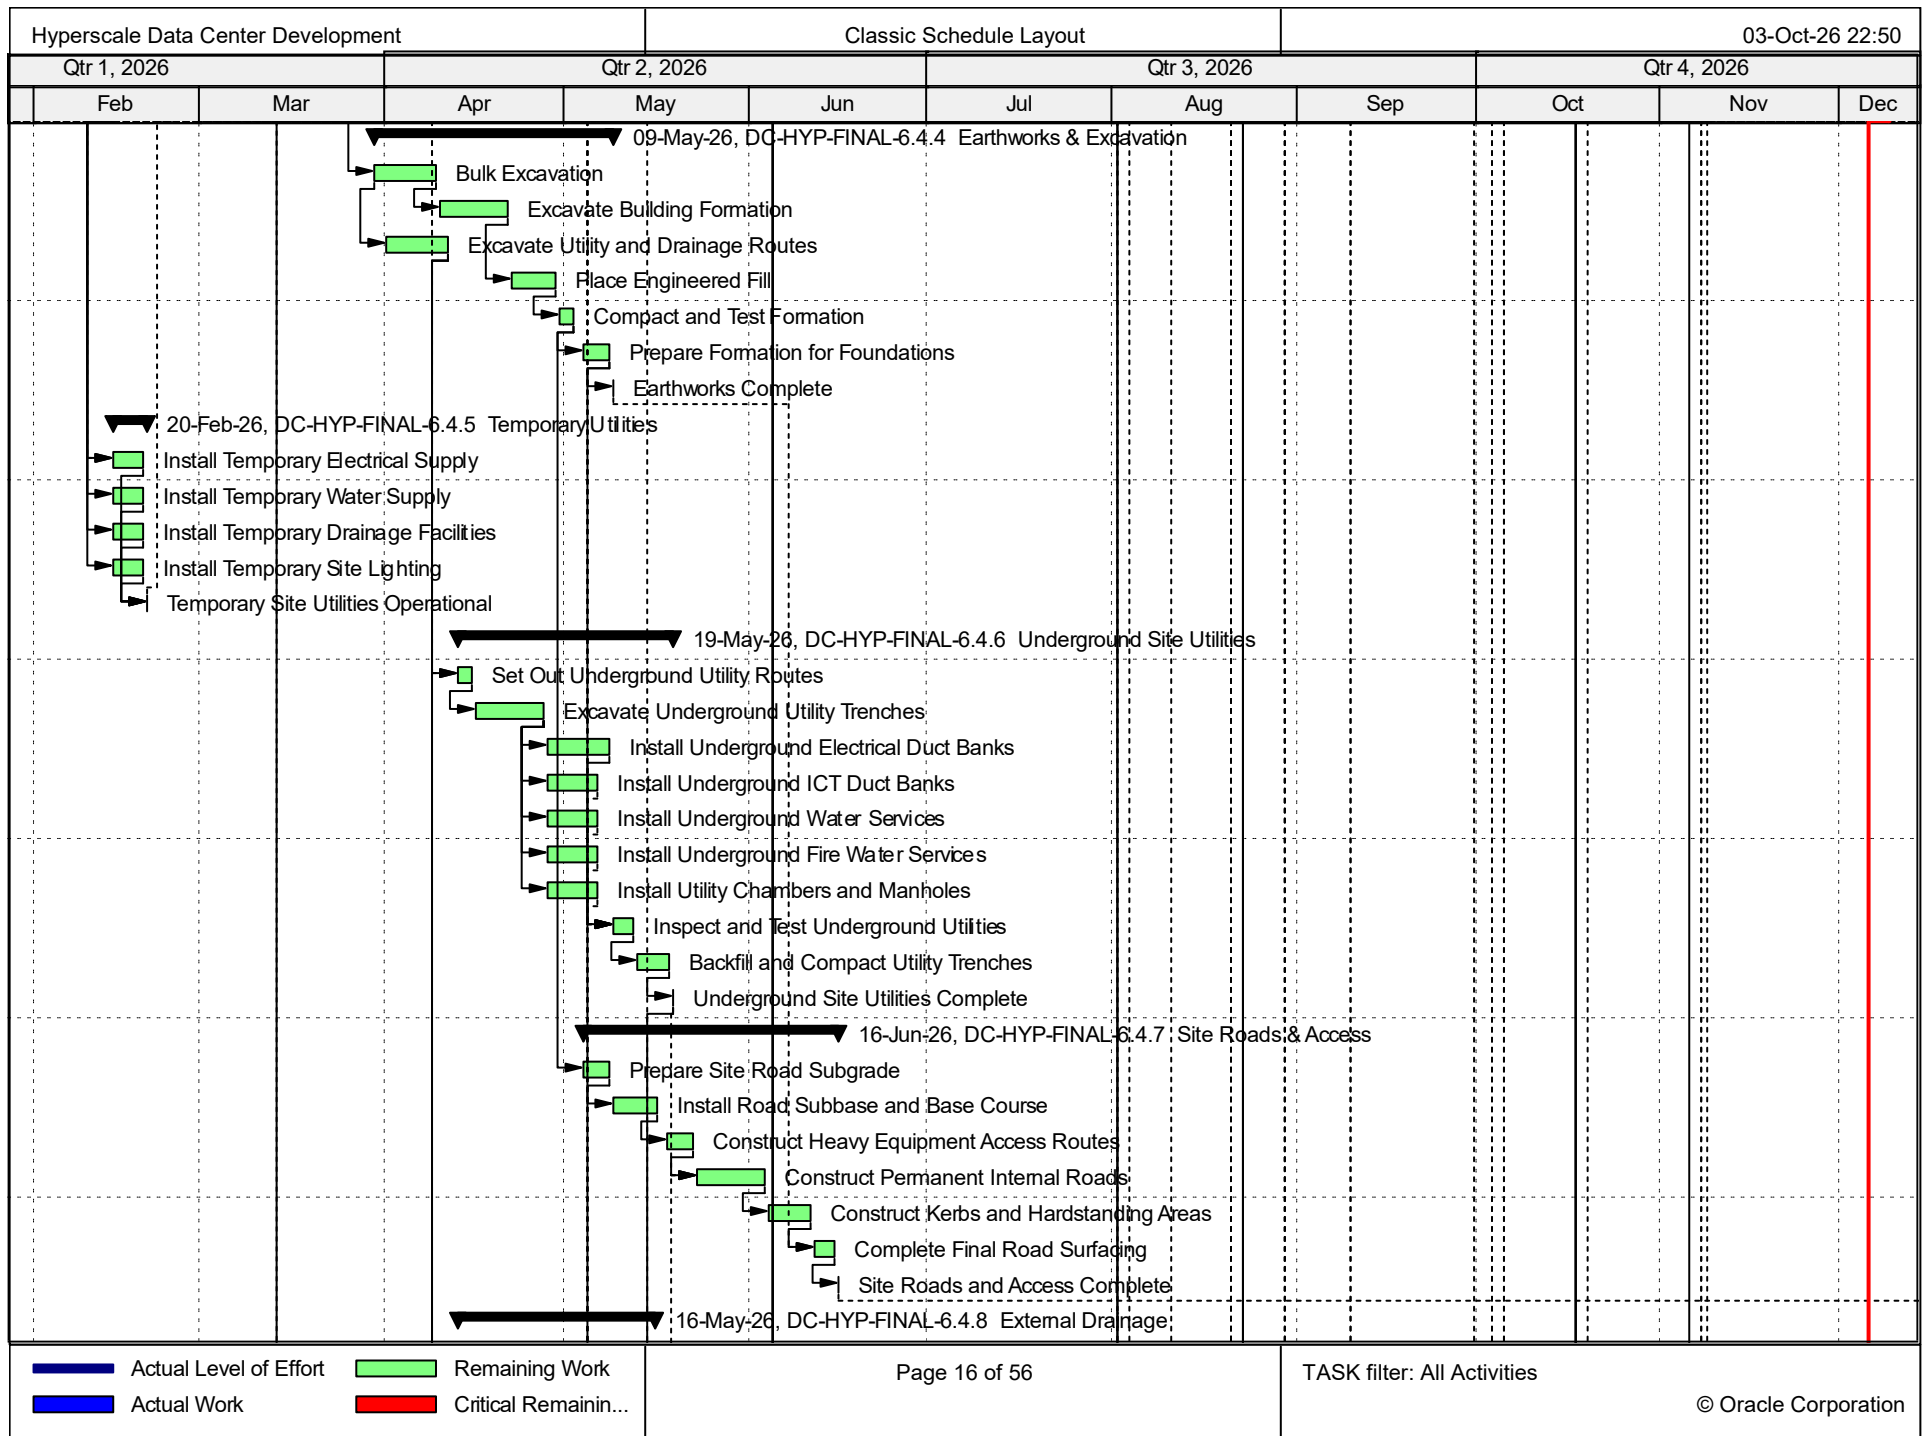

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID		Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
									Nov	Dec	Jan

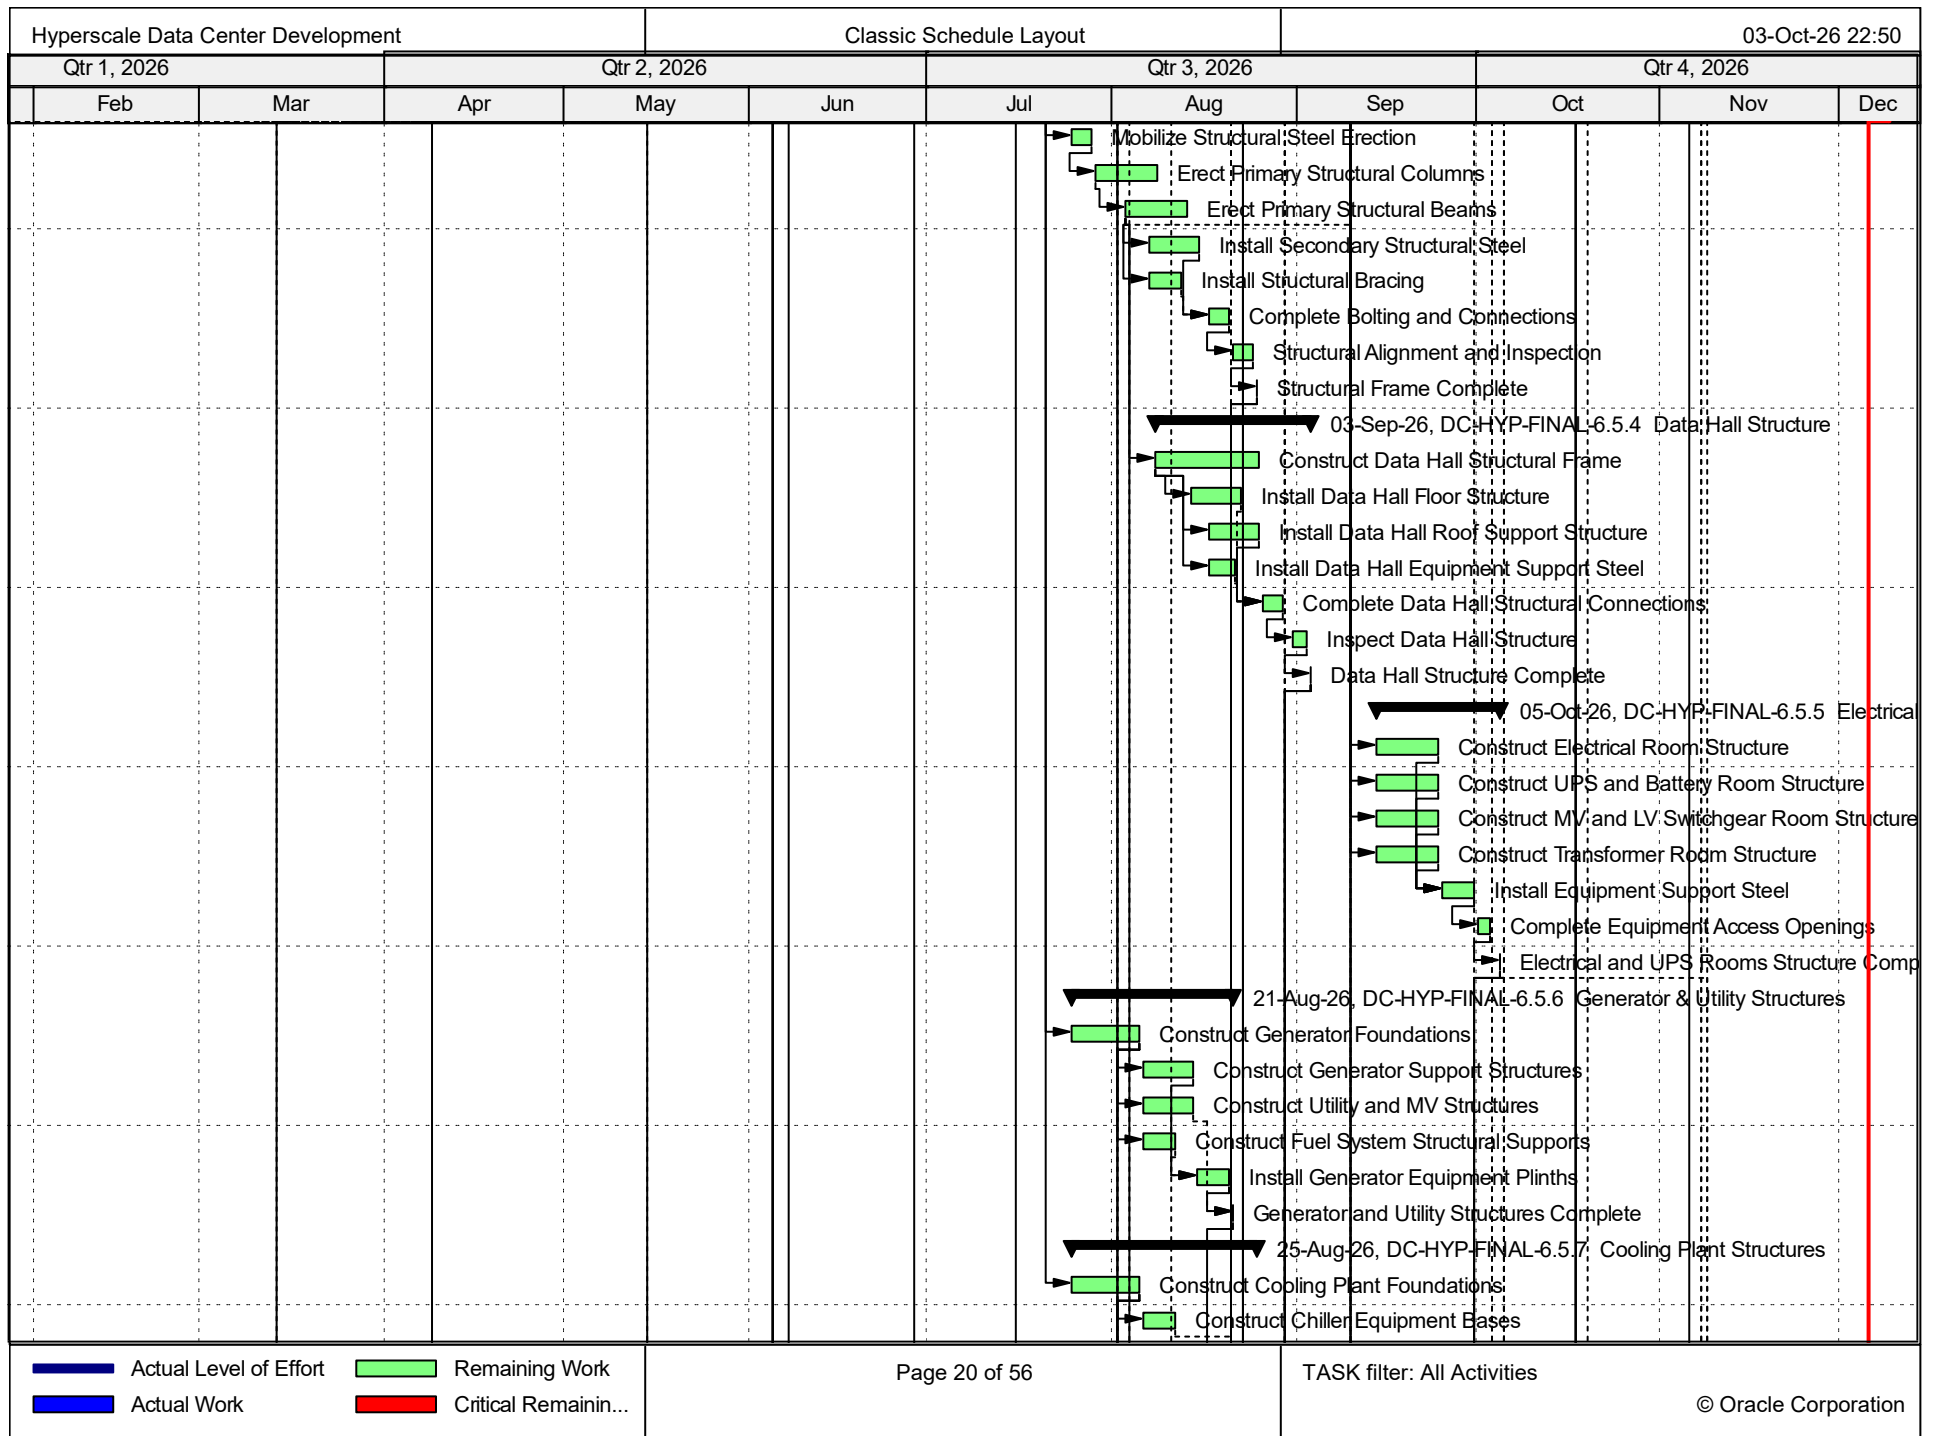

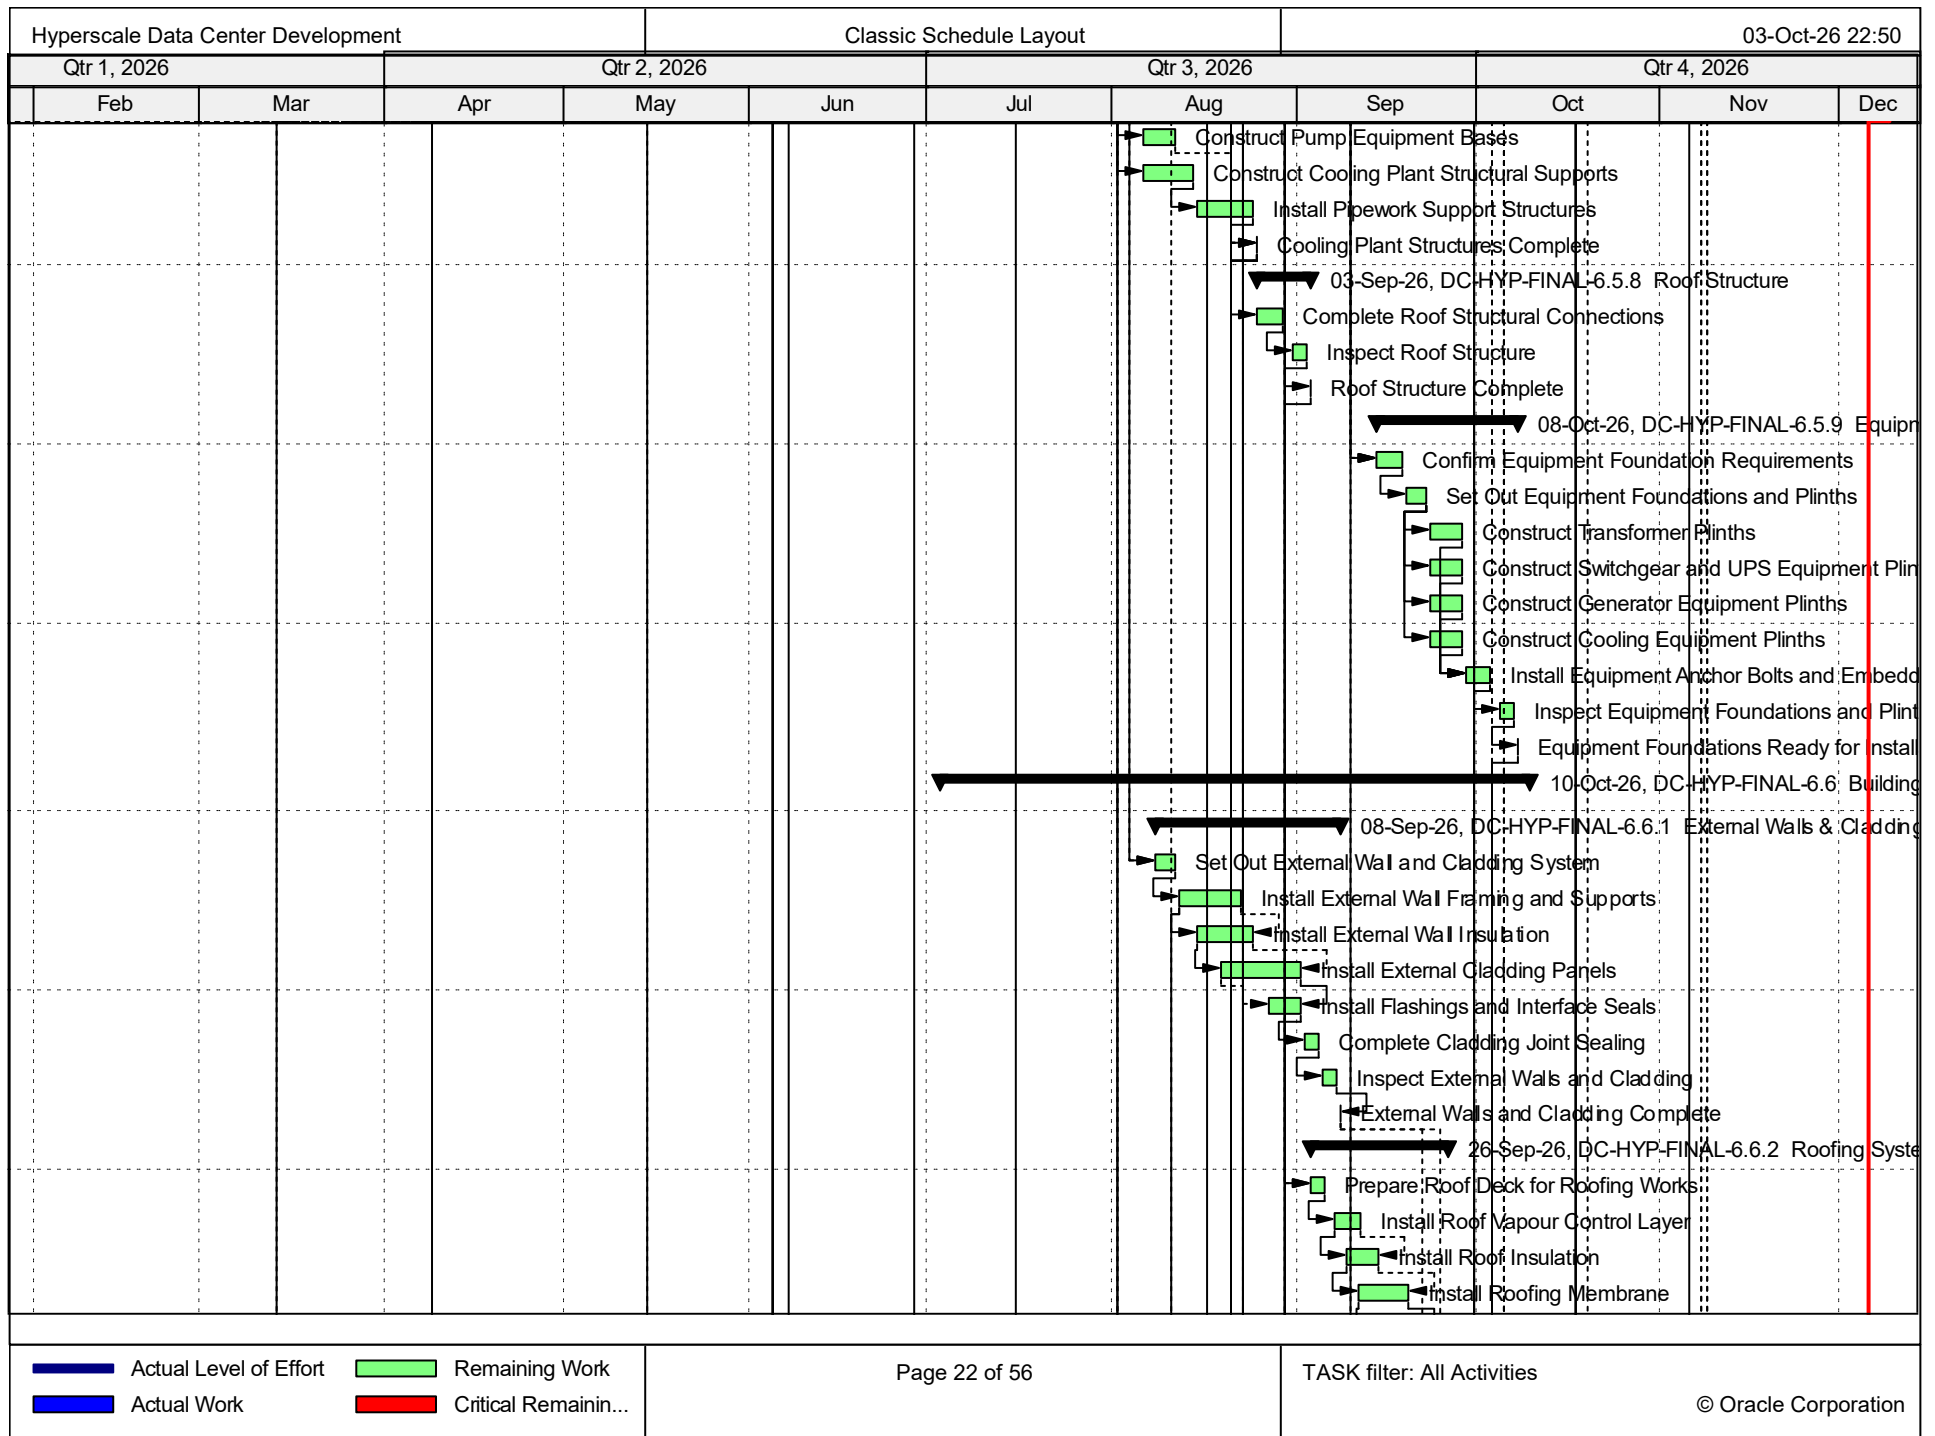

Hyperscale Data Center Development			Classic Schedule Layout				03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
ENV-030	Perform External Wall Water	3	3	0%	29-Sep-26	01-Oct-26	30			
ENV-040	Inspect Doors Louvers and	2	2	0%	29-Sep-26	30-Sep-26	31			
ENV-050	Rectify Building Envelope L	5	5	0%	02-Oct-26	07-Oct-26	30			
ENV-060	Complete Final Building En	2	2	0%	08-Oct-26	09-Oct-26	30			
ENV-070	Building Weather-Tight	0	0	0%	10-Oct-26	10-Oct-26	30			
DC-HYP-FINAL-6.7 Electrical S		244	244	0%	13-Apr-26	21-Jan-27	2			
DC-HYP-FINAL-6.7.1 Utility / MV Pow		35	35	0%	19-May-26	27-Jun-26	137			
MV-010	Set Out MV Power Infrastru	2	2	0%	19-May-26	20-May-26	137			
MV-020	Install MV Cable Duct Bank	15	15	0%	21-May-26	06-Jun-26	137			
MV-030	Install MV Cable Chambers	10	10	0%	27-May-26	06-Jun-26	137			
MV-040	Install Incoming MV Cables	10	10	0%	08-Jun-26	18-Jun-26	137			
MV-050	Terminate Incoming MV Ca	5	5	0%	19-Jun-26	24-Jun-26	137			
MV-060	Test Incoming MV Cable S	3	3	0%	25-Jun-26	27-Jun-26	137			
MV-070	MV Power Infrastructure Re	0	0	0%		27-Jun-26	137			
DC-HYP-FINAL-6.7.2 MV Switchgear		29	29	0%	10-Oct-26	12-Nov-26	26			
MVSG-01	Prepare MV Switchgear Ro	3	3	0%	10-Oct-26	13-Oct-26	35			
MVSG-02	Receive and Inspect MV S	2	2	0%	22-Oct-26	23-Oct-26	26			
MVSG-03	Position and Install MV Swi	5	5	0%	24-Oct-26	29-Oct-26	26			
MVSG-04	Assemble MV Switchgear S	5	5	0%	30-Oct-26	04-Nov-26	26			
MVSG-05	Install MV Switchgear Conti	5	5	0%	02-Nov-26	06-Nov-26	29			
MVSG-06	Terminate MV Power Cable	5	5	0%	05-Nov-26	10-Nov-26	26			
MVSG-07	Complete MV Switchgear In	2	2	0%	11-Nov-26	12-Nov-26	26			
MVSG-08	MV Switchgear Ready for F	0	0	0%		12-Nov-26	26			
DC-HYP-FINAL-6.7.3 Transformers		66	66	0%	08-Oct-26	23-Dec-26	0			
TRI-010	Prepare Transformer Areas	3	3	0%	08-Oct-26	10-Oct-26	53			
TRI-020	Receive and Inspect Transf	2	2	0%	10-Dec-26	11-Dec-26	0			
TRI-030	Position Transformers on Pl	3	3	0%	12-Dec-26	15-Dec-26	0			
TRI-040	Install Transformer Ancillary	5	5	0%	16-Dec-26	21-Dec-26	0			
TRI-050	Complete MV Transformer	3	3	0%	16-Dec-26	18-Dec-26	2			
TRI-060	Complete LV Transformer C	3	3	0%	16-Dec-26	18-Dec-26	0			
TRI-070	Complete Transformer Inst	2	2	0%	22-Dec-26	23-Dec-26	0			
TRI-080	Transformers Ready for Pre	0	0	0%		23-Dec-26	0			
DC-HYP-FINAL-6.7.4 Standby Gener		111	111	0%	21-Aug-26	28-Dec-26	23			

Actual Level of Effort

Actual Work

Remaining Work

Critical Remainin...


Page 25 of 56

TASK filter: All Activities

© Oracle Corporation



Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50				
Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			
Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
07 22-Sep-26, DC-HYP-FINAL-6.8.1 Cooling Plant Prepare Cooling Plant Area for Installation Install Cooling Plant Equipment Supports Install Cooling Plant Main Headers Install Cooling Plant Valves and Accessories Install Cooling Plant Electrical Interfaces Install Cooling Plant Controls Interfaces Inspect Cooling Plant Installation Cooling Plant Ready for Pre-Commissioning, 21-Sep-26, DC-HYP-FINAL-6.8.2 Chillers / Heat R Prepare Chiller and Heat Rejection Equipment Areas Receive and Inspect Chillers and Heat Rejection Equipment Position Chillers on Equipment Bases Position Heat Rejection Equipment Install Chiller Mechanical Connections Install Heat Rejection Equipment Connections Install Electrical and Controls Connections Complete Chiller Installation Inspection Chillers and Heat Rejection Equipment Ready for P 15-Sep-26, DC-HYP-FINAL-6.8.3 Pumps & Pumping S Prepare Pump Bases for Installation Receive and Inspect Pumps Install Primary Cooling Pumps Install Secondary Cooling Pumps Install Pump Suction and Discharge Connections Install Pump Electrical Connections Install Pump Controls and Instrumentation Inspect Pumping System Installation Pumping Systems Ready for Pre-Commissioning, 04-Nov-26, DC-HYP-FI												
Actual Level of Effort Actual Work			Remaining Work Critical Remainin...			Page 32 of 56			TASK filter: All Activities			© Oracle Corporation

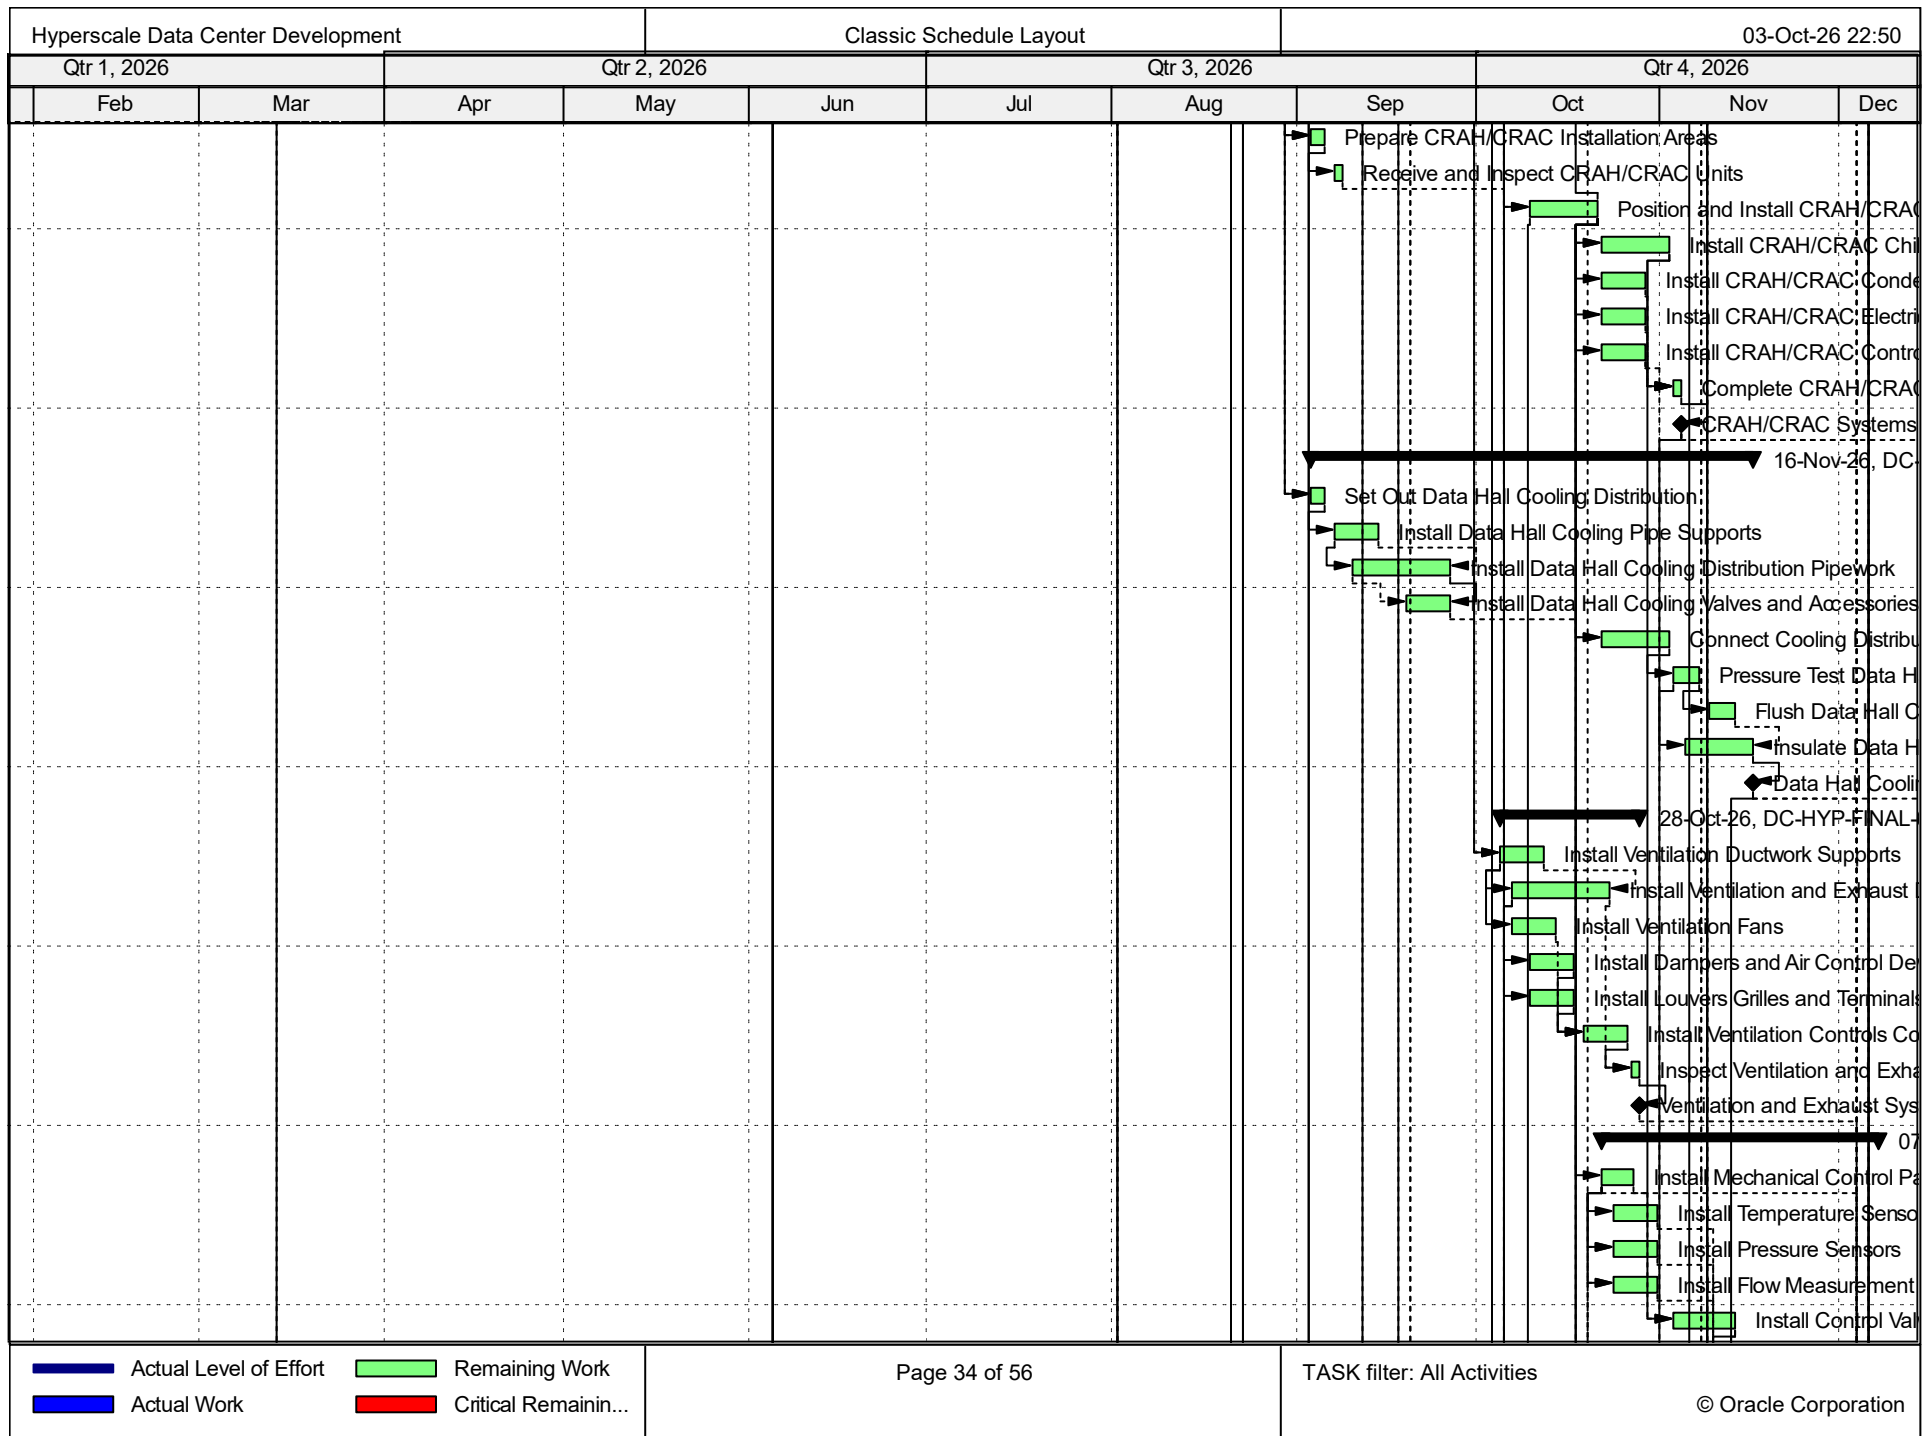

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
	MCI-060 Complete Mechanical Cont	10	10	0%	14-Nov-26	25-Nov-26	30			
	MCI-070 Complete BMS Interface C	7	7	0%	26-Nov-26	03-Dec-26	30			
	MCI-080 Inspect Mechanical Control	3	3	0%	04-Dec-26	07-Dec-26	30			
	MCI-090 Mechanical Controls Ready	0	0	0%		07-Dec-26	30			
	DC-HYP-FINAL-6.8.9 Water Treatmen	20	20	0%	25-Aug-26	16-Sep-26	111			
	WTM-010 Prepare Water Treatment E	3	3	0%	25-Aug-26	27-Aug-26	111			
	WTM-020 Install Water Treatment Equ	5	5	0%	28-Aug-26	02-Sep-26	111			
	WTM-030 Install Chemical Dosing Sys	5	5	0%	03-Sep-26	08-Sep-26	111			
	WTM-040 Install Cooling System Mak	5	5	0%	03-Sep-26	08-Sep-26	111			
	WTM-050 Install Water Treatment Inst	5	5	0%	31-Aug-26	04-Sep-26	114			
	WTM-060 Complete Electrical and Co	5	5	0%	09-Sep-26	14-Sep-26	111			
	WTM-070 Inspect Water Treatment ar	2	2	0%	15-Sep-26	16-Sep-26	111			
	WTM-080 Water Treatment and Make	0	0	0%		16-Sep-26	111			
	DC-HYP-FINAL-6.8.10 Mechanical An	49	49	0%	07-Sep-26	02-Nov-26	71			
	MCA-010 Install Mechanical Equipme	7	7	0%	22-Oct-26	29-Oct-26	71			
	MCA-020 Install Condensate Drainag	7	7	0%	22-Oct-26	29-Oct-26	71			
	MCA-030 Install Mechanical Equipme	5	5	0%	07-Sep-26	11-Sep-26	112			
	MCA-040 Complete Mechanical Equi	5	5	0%	14-Oct-26	19-Oct-26	80			
	MCA-050 Complete Mechanical Plan	5	5	0%	07-Sep-26	11-Sep-26	112			
	MCA-060 Complete Mechanical Insta	3	3	0%	30-Oct-26	02-Nov-26	71			
	MCA-070 Mechanical Systems Install	0	0	0%		02-Nov-26	71			
	DC-HYP-FINAL-6.8.4 Chilled Water D	38	38	0%	25-Aug-26	07-Oct-26	93			
	CHW-010 Set Out Chilled Water Pipe	3	3	0%	25-Aug-26	27-Aug-26	42			
	CHW-020 Install Chilled Water Pipe S	10	10	0%	28-Aug-26	08-Sep-26	42			
	CHW-030 Install Main Chilled Water F	15	15	0%	01-Sep-26	17-Sep-26	42			
	CHW-040 Install Chilled Water Branch	15	15	0%	07-Sep-26	23-Sep-26	42			
	CHW-050 Install Chilled Water Valves	7	7	0%	16-Sep-26	23-Sep-26	42			
	CHW-060 Pressure Test Chilled Water	7	7	0%	24-Sep-26	01-Oct-26	42			
	CHW-070 Flush and Clean Chilled We	5	5	0%	02-Oct-26	07-Oct-26	42			
	CHW-080 Install Chilled Water Pipe Ir	10	10	0%	26-Sep-26	07-Oct-26	93			
	CHW-090 Chilled Water Distribution R	0	0	0%		07-Oct-26	93			
	DC-HYP-FINAL-6.9 Fire & Life S	218	218	0%	09-Jun-26	17-Feb-27	63			
	DC-HYP-FINAL-6.9.1 Fire Detection &	118	118	0%	09-Jun-26	23-Oct-26	65			

Actual Level of Effort

Actual Work


Remaining Work

Critical Remainin...


Page 35 of 56

TASK filter: All Activities

© Oracle Corporation

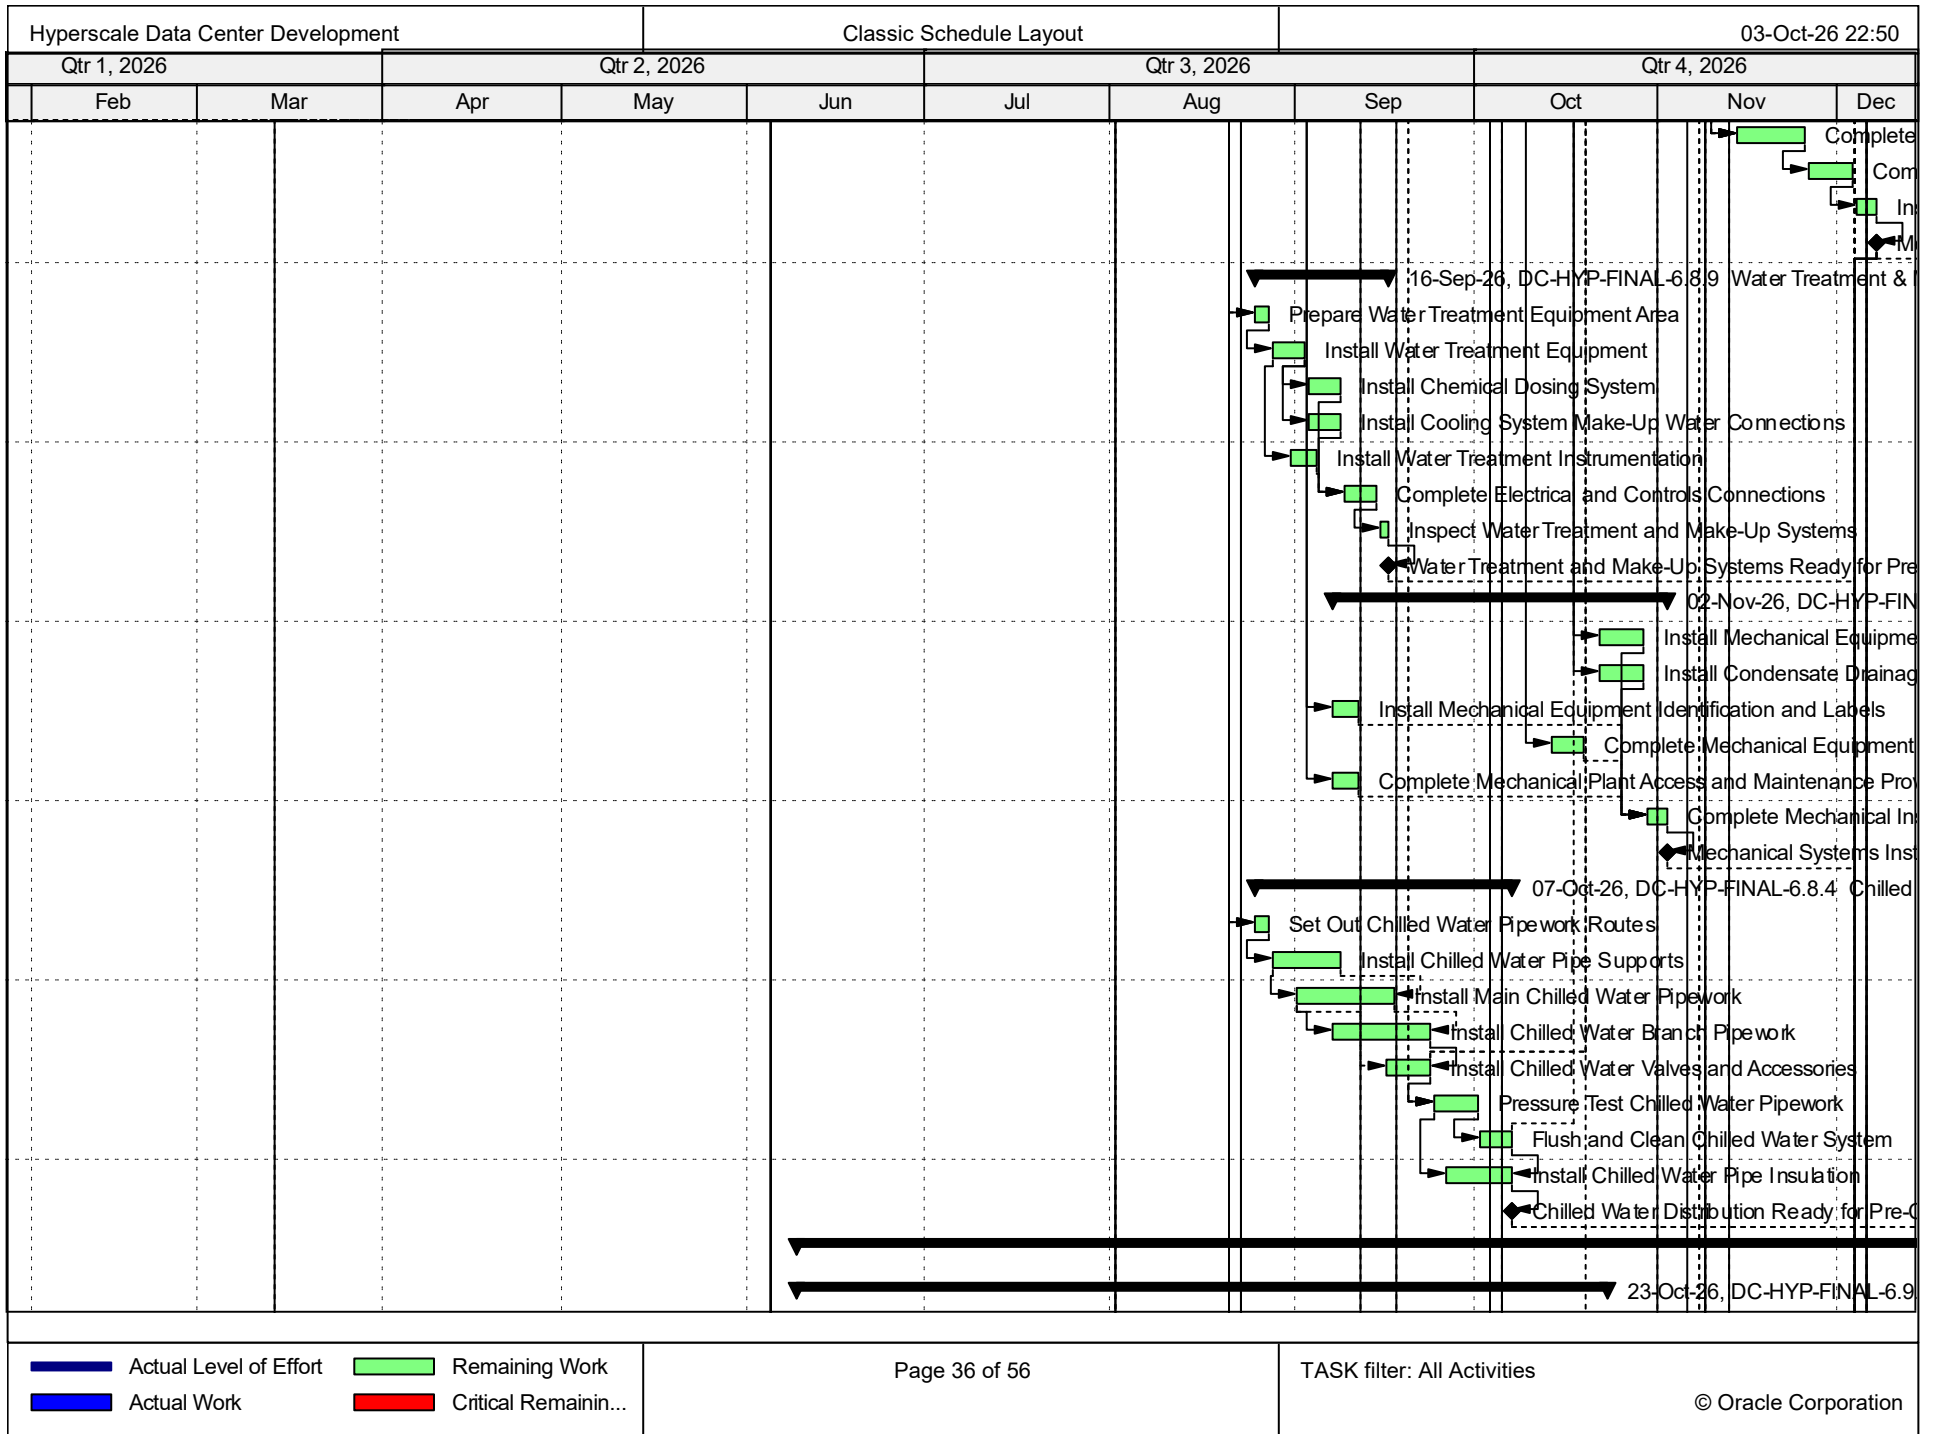

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID		Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
									Nov	Dec	Jan

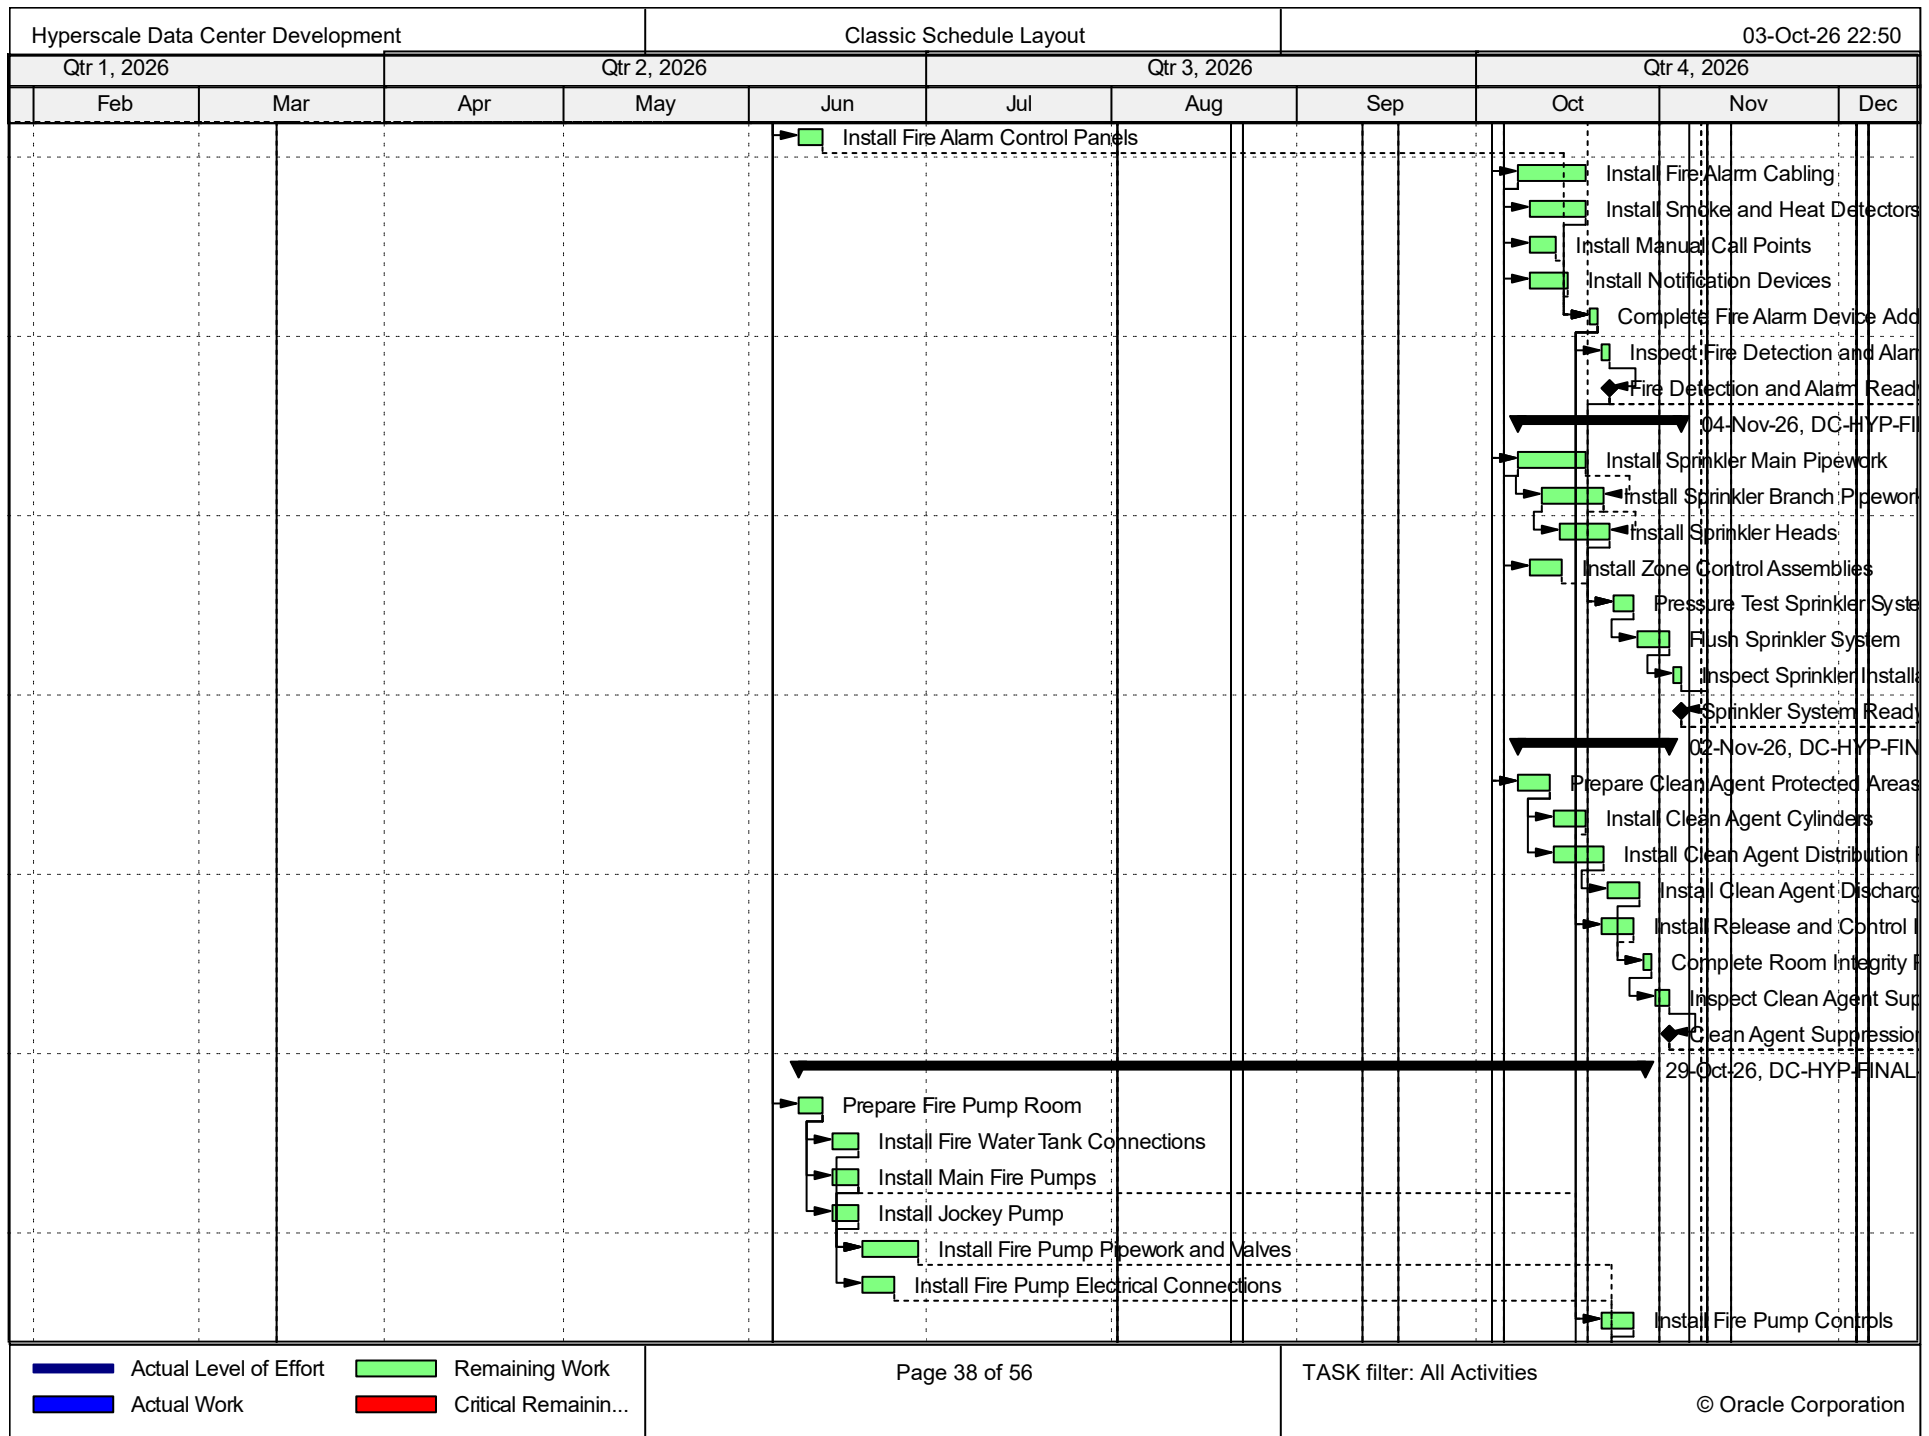


Page 38 of 56

TASK filter: All Activities

© Oracle Corporation



Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
								Nov	Dec	Jan	
 DC-HYP-FINAL-6.10.5 Sensors & Fiel		36	36	0%	10-Oct-26	20-Nov-26	55				
 SFD-010	Install Environmental Sensc	5	5	0%	10-Oct-26	15-Oct-26	77				
 SFD-020	Install Temperature and Hu	5	5	0%	12-Oct-26	16-Oct-26	77				
 SFD-030	Install Differential Pressure	5	5	0%	12-Oct-26	16-Oct-26	77				
 SFD-040	Install Leak Detection Sens	5	5	0%	12-Oct-26	16-Oct-26	77				
 SFD-050	Install Energy Metering Dev	5	5	0%	12-Oct-26	16-Oct-26	77				
 SFD-060	Terminate Sensor and Field	8	8	0%	12-Nov-26	20-Nov-26	55				
 SFD-070	Sensors and Field Devices	0	0	0%		20-Nov-26	55				
 DC-HYP-FINAL-6.10.6 Controls Netw		21	21	0%	19-Oct-26	11-Nov-26	42				
 CNW-010	Install Controls Network Sw	5	5	0%	26-Oct-26	30-Oct-26	42				
 CNW-020	Install Controls Network Ca	8	8	0%	19-Oct-26	27-Oct-26	45				
 CNW-030	Configure Controls Network	4	4	0%	31-Oct-26	04-Nov-26	42				
 CNW-040	Configure Network Segmer	3	3	0%	05-Nov-26	07-Nov-26	42				
 CNW-050	Perform Controls Network C	3	3	0%	09-Nov-26	11-Nov-26	42				
 CNW-060	Controls Network Ready	0	0	0%		11-Nov-26	42				
 DC-HYP-FINAL-6.10.7 System Integr		21	21	0%	26-Dec-26	19-Jan-27	28				
 CSI-010	Integrate BMS with Electric	4	4	0%	07-Jan-27	11-Jan-27	33				
 CSI-020	Integrate BMS with Mechar	4	4	0%	26-Dec-26	30-Dec-26	43				
 CSI-030	Integrate BMS with Fire Alai	3	3	0%	06-Jan-27	08-Jan-27	35				
 CSI-040	Integrate BMS with UPS ar	4	4	0%	07-Jan-27	11-Jan-27	33				
 CSI-050	Integrate DCIM with Power	4	4	0%	13-Jan-27	16-Jan-27	28				
 CSI-060	Integrate DCIM with Coolin	4	4	0%	13-Jan-27	16-Jan-27	28				
 CSI-070	Verify System Integration In	2	2	0%	18-Jan-27	19-Jan-27	28				
 CSI-080	Controls Integration Ready	0	0	0%		19-Jan-27	28				
 DC-HYP-FINAL-6.10.8 Graphics, Con		13	13	0%	06-Aug-26	20-Aug-26	129				
 GCP-010	Develop BMS Control Logic	8	8	0%	06-Aug-26	14-Aug-26	129				
 GCP-020	Configure BMS Alarm Logic	5	5	0%	08-Aug-26	13-Aug-26	132				
 GCP-030	Develop BMS Graphics	8	8	0%	08-Aug-26	17-Aug-26	129				
 GCP-040	Configure DCIM Dashboar	5	5	0%	08-Aug-26	13-Aug-26	132				
 GCP-050	Configure Trend Logging ar	4	4	0%	08-Aug-26	12-Aug-26	133				
 GCP-060	Complete Controls Softwar	3	3	0%	18-Aug-26	20-Aug-26	129				
 GCP-070	BMS and DCIM Configurat	0	0	0%		20-Aug-26	129				
 DC-HYP-FINAL-6.11 Utility Con		229	229	0%	18-Mar-26	01-Feb-27	0				
Actual Level of Effort Remaining Work Actual Work Critical Remainin...											

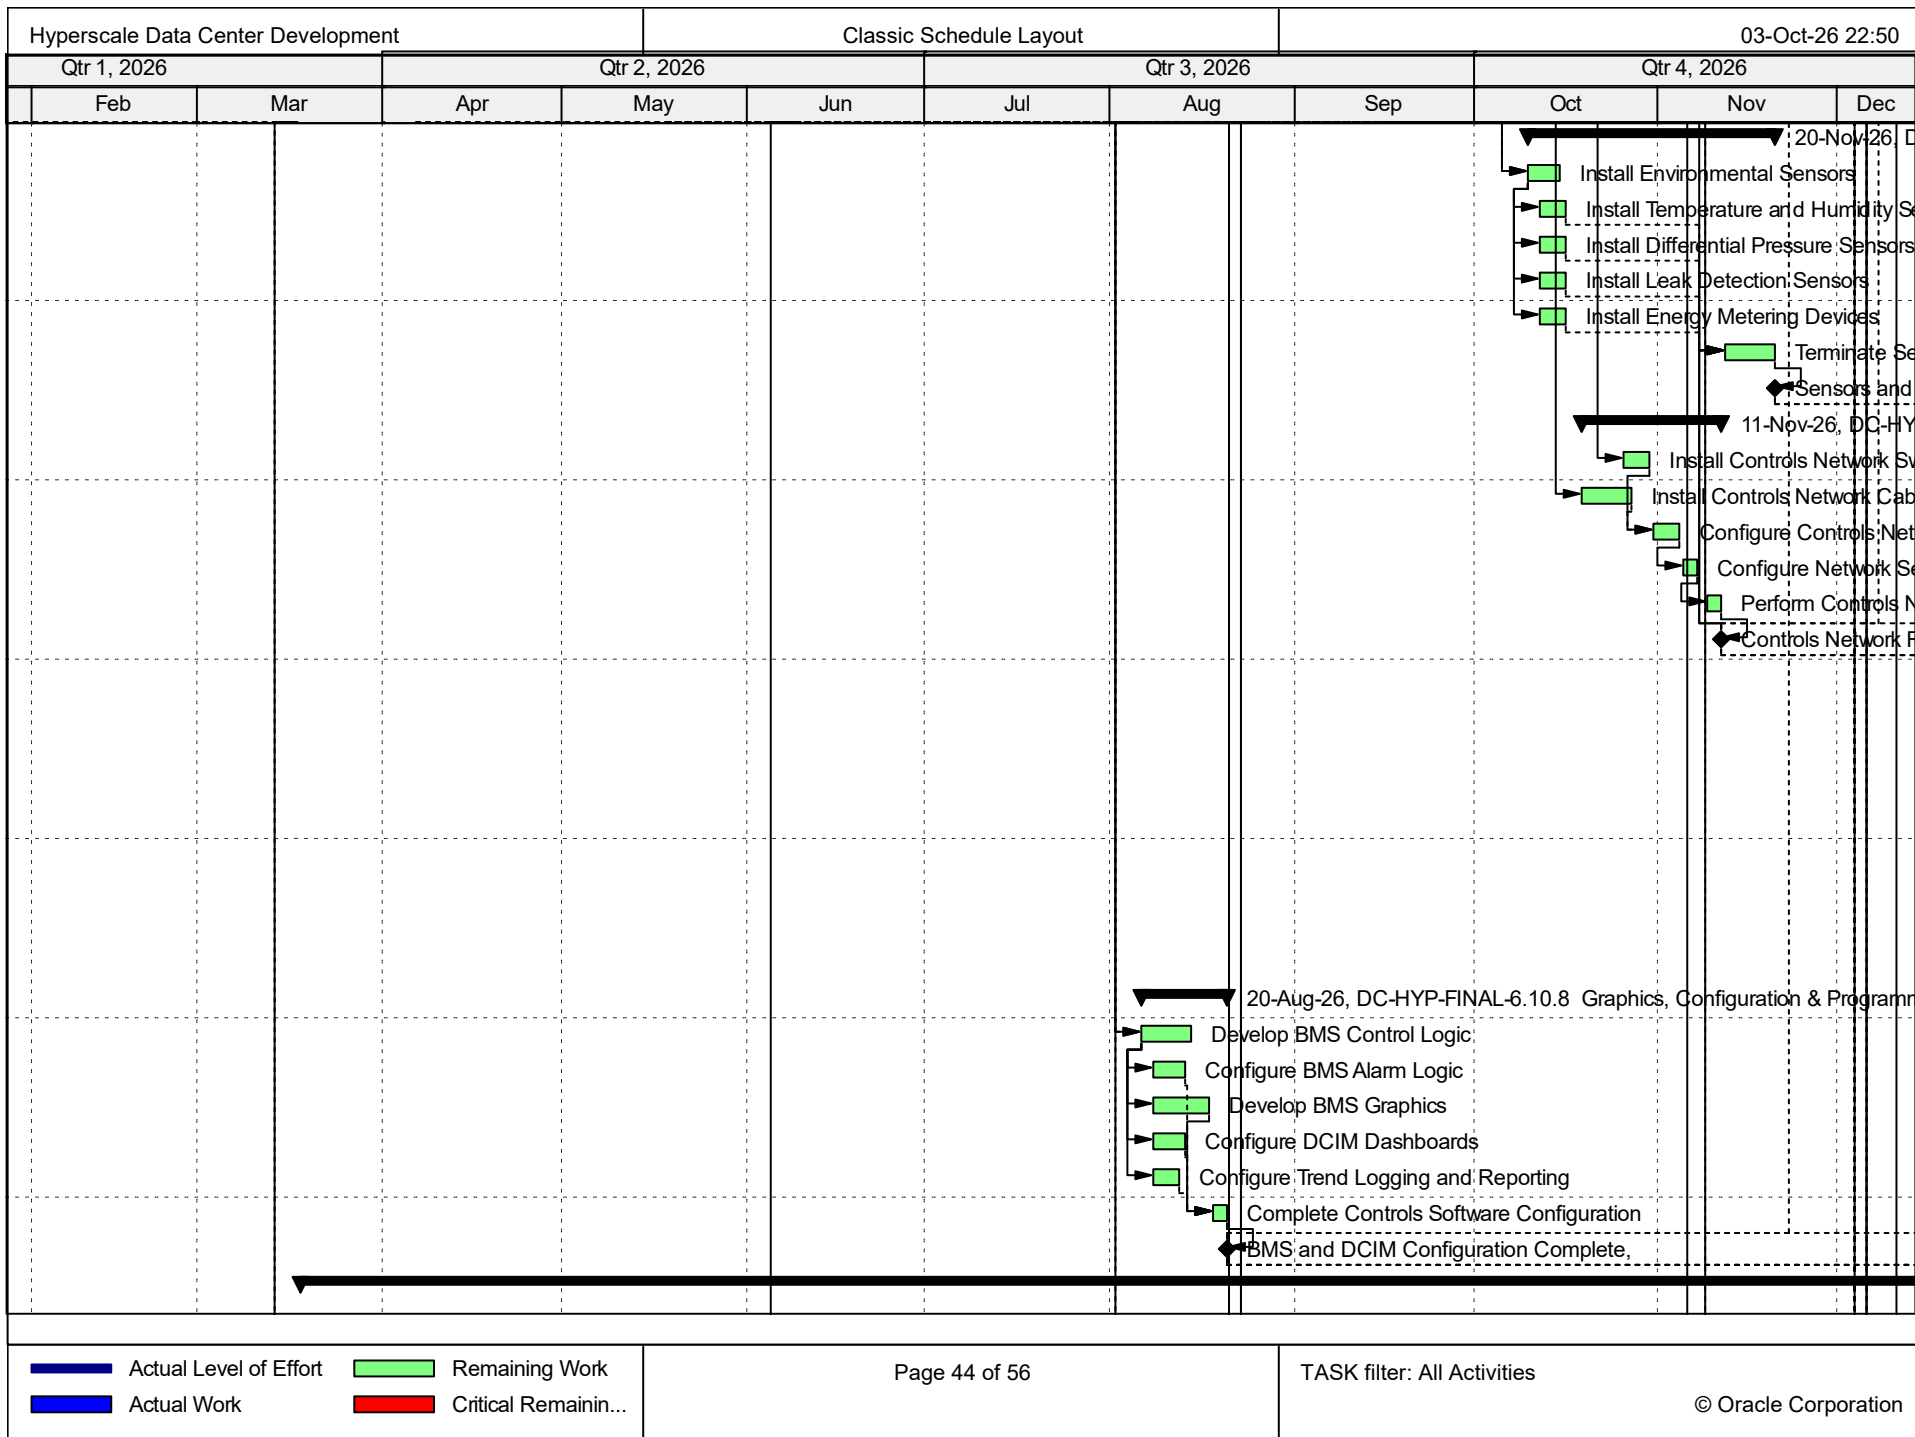

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
DC-HYP-FINAL-6.11.1 Utility Coordin		25	25	0%	18-Mar-26	15-Apr-26	177			
UTL-010	Submit Utility Connection A	5	5	0%	18-Mar-26	23-Mar-26	177			
UTL-020	Coordinate Utility Technical	10	10	0%	24-Mar-26	03-Apr-26	177			
UTL-030	Submit Utility Protection Stu	10	10	0%	24-Mar-26	03-Apr-26	177			
UTL-040	Resolve Utility Review Corr	10	10	0%	04-Apr-26	15-Apr-26	177			
UTL-050	Obtain Utility Connection At	0	0	0%		15-Apr-26	177			
DC-HYP-FINAL-6.11.2 Incoming Utilit		20	20	0%	16-Apr-26	08-May-26	177			
UCMV-01	Complete Incoming Utility M	15	15	0%	16-Apr-26	02-May-26	177			
UCMV-02	Install Utility Metering Equip	5	5	0%	20-Apr-26	24-Apr-26	189			
UCMV-03	Complete Utility MV Cable	5	5	0%	04-May-26	08-May-26	177			
UCMV-04	Complete Utility Protection	5	5	0%	22-Apr-26	27-Apr-26	187			
UCMV-05	Incoming Utility Connection	0	0	0%		08-May-26	177			
DC-HYP-FINAL-6.11.3 Utility Substat		10	10	0%	09-May-26	20-May-26	177			
SUB-010	Inspect Utility Substation In	2	2	0%	09-May-26	11-May-26	177			
SUB-020	Complete Substation Prote	3	3	0%	12-May-26	14-May-26	177			
SUB-030	Complete Substation Mete	3	3	0%	12-May-26	14-May-26	177			
SUB-040	Close Utility Substation Pur	5	5	0%	15-May-26	20-May-26	177			
SUB-050	Utility Substation Ready for	0	0	0%		20-May-26	177			
DC-HYP-FINAL-6.11.4 MV System Er		9	9	0%	13-Nov-26	23-Nov-26	26			
MVE-010	Complete MV Pre-Energiza	2	2	0%	13-Nov-26	14-Nov-26	26			
MVE-020	Verify MV Protection Setting	2	2	0%	16-Nov-26	17-Nov-26	26			
MVE-030	Obtain MV Energization Pe	2	2	0%	18-Nov-26	19-Nov-26	26			
MVE-040	Energize Incoming MV Sys	1	1	0%	20-Nov-26	20-Nov-26	26			
MVE-050	Verify MV System Operatio	2	2	0%	21-Nov-26	23-Nov-26	26			
MVE-060	MV System Energized	0	0	0%		23-Nov-26	26			
DC-HYP-FINAL-6.11.6 LV System Enr		6	6	0%	24-Dec-26	30-Dec-26	0			
TRE-010	Complete Transformer Pre-l	1	1	0%	24-Dec-26	24-Dec-26	0			
TRE-020	Verify Transformer Protectio	2	2	0%	25-Dec-26	26-Dec-26	0			
TRE-030	Energize Transformers	1	1	0%	28-Dec-26	28-Dec-26	0			
TRE-040	Perform Transformer Opera	2	2	0%	29-Dec-26	30-Dec-26	0			
TRE-050	Transformers Energized	0	0	0%		30-Dec-26	0			
DC-HYP-FINAL-6.11.7 UPS & Critical		9	9	0%	31-Dec-26	09-Jan-27	0			
LVE-010	Complete LV Pre-Energizat	1	1	0%	31-Dec-26	31-Dec-26	0			
LVE-020	Verify LV Protection Setting	2	2	0%	01-Jan-27	02-Jan-27	0			

Actual Level of Effort

Remaining Work

Actual Work

Critical Remainin...

Page 45 of 56

TASK filter: All Activities

© Oracle Corporation



Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50		
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026
								Nov	Dec	Jan
■ CXP-060	Commissioning Plan Appro	0	0	0%		22-Jan-26	314			
■ DC-HYP-FINAL-6.12.2 Pre-Commissi		44	44	0%	08-Dec-26	27-Jan-27	2			
■ PRE-010	Complete Electrical Pre-Co	2	2	0%	22-Jan-27	23-Jan-27	2			
■ PRE-020	Complete Mechanical Pre-(	2	2	0%	08-Dec-26	09-Dec-26	41			
■ PRE-030	Complete Fire System Pre-	2	2	0%	06-Jan-27	07-Jan-27	16			
■ PRE-040	Complete BMS and Contro	2	2	0%	13-Jan-27	14-Jan-27	10			
■ PRE-050	Complete Pre-Commissioni	3	3	0%	25-Jan-27	27-Jan-27	2			
■ PRE-060	Systems Ready for Functio	0	0	0%		27-Jan-27	2			
■ DC-HYP-FINAL-6.12.3 Electrical Syst		14	14	0%	28-Jan-27	12-Feb-27	0			
■ ELC-CX-	Commission MV Switchgea	5	5	0%	02-Feb-27	06-Feb-27	5			
■ ELC-CX-	Commission Transformers	5	5	0%	28-Jan-27	02-Feb-27	9			
■ ELC-CX-	Commission LV Switchgear	5	5	0%	28-Jan-27	02-Feb-27	9			
■ ELC-CX-	Commission UPS Systems	5	5	0%	28-Jan-27	02-Feb-27	9			
■ ELC-CX-	Commission Battery Syste	5	5	0%	28-Jan-27	02-Feb-27	9			
■ ELC-CX-	Commission Standby Gene	5	5	0%	28-Jan-27	02-Feb-27	9			
■ ELC-CX-	Commission PDU and Bus	10	10	0%	02-Feb-27	12-Feb-27	0			
■ ELC-CX-	Electrical Systems Functio	0	0	0%		12-Feb-27	0			
■ DC-HYP-FINAL-6.12.4 Mechanical & I		12	12	0%	28-Jan-27	10-Feb-27	2			
■ MEC-CX-	Commission Chillers and H	5	5	0%	28-Jan-27	02-Feb-27	2			
■ MEC-CX-	Commission Cooling Pump	5	5	0%	28-Jan-27	02-Feb-27	2			
■ MEC-CX-	Commission Chilled Water	5	5	0%	28-Jan-27	02-Feb-27	2			
■ MEC-CX-	Commission CRAH CRAC	5	5	0%	28-Jan-27	02-Feb-27	2			
■ MEC-CX-	Perform Air and Water Bala	5	5	0%	03-Feb-27	08-Feb-27	2			
■ MEC-CX-	Verify Cooling System Cont	2	2	0%	09-Feb-27	10-Feb-27	2			
■ MEC-CX-	Mechanical Systems Functi	0	0	0%		10-Feb-27	2			
■ DC-HYP-FINAL-6.12.5 Fire & Life Saf		7	7	0%	28-Jan-27	04-Feb-27	10			
■ FLS-CX-	Commission Fire Detection	5	5	0%	28-Jan-27	02-Feb-27	10			
■ FLS-CX-	Commission Sprinkler Syste	5	5	0%	28-Jan-27	02-Feb-27	10			
■ FLS-CX-	Commission Clean Agent F	5	5	0%	28-Jan-27	02-Feb-27	10			
■ FLS-CX-	Commission Fire Pumps	5	5	0%	28-Jan-27	02-Feb-27	10			
■ FLS-CX-	Commission VESDA Syste	5	5	0%	28-Jan-27	02-Feb-27	10			
■ FLS-CX-	Verify Fire Cause and Effec	2	2	0%	03-Feb-27	04-Feb-27	10			
■ FLS-CX-	Fire and Life Safety Commi	0	0	0%		04-Feb-27	10			
■ DC-HYP-FINAL-6.12.6 BMS & DCIM (		16	16	0%	28-Jan-27	15-Feb-27	1			

■ Actual Level of Effort

■ Actual Work

■ Remaining Work

■ Critical Remainin...

Page 49 of 56

TASK filter: All Activities

© Oracle Corporation

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50				
Activity ID		Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
									Nov	Dec	Jan	
		BMS-CX- Commission BMS Infrastruc	5	5	0%	28-Jan-27	02-Feb-27	5				
		BMS-CX- Verify BMS Field Points	2	2	0%	03-Feb-27	04-Feb-27	5				
		BMS-CX- Commission BMS Graphics	5	5	0%	05-Feb-27	10-Feb-27	5				
		BMS-CX- Commission DCIM Platform	5	5	0%	28-Jan-27	02-Feb-27	10				
		BMS-CX- Verify DCIM Power Monitori	2	2	0%	13-Feb-27	15-Feb-27	1				
		BMS-CX- Verify DCIM Cooling Monitc	2	2	0%	11-Feb-27	12-Feb-27	3				
		BMS-CX- BMS and DCIM Commissic	0	0	0%		15-Feb-27	1				
		DC-HYP-FINAL-6.12.7 Controls & Sy	4	4	0%	16-Feb-27	19-Feb-27	1				
		INT-CX-0 Verify Electrical to BMS Inte	2	2	0%	16-Feb-27	17-Feb-27	1				
		INT-CX-0: Verify Mechanical to BMS Ir	2	2	0%	16-Feb-27	17-Feb-27	1				
		INT-CX-0: Verify Fire System Integratic	2	2	0%	16-Feb-27	17-Feb-27	1				
		INT-CX-0: Verify UPS and Generator (	2	2	0%	16-Feb-27	17-Feb-27	1				
		INT-CX-0: Complete Integrated Contr	2	2	0%	18-Feb-27	19-Feb-27	1				
		INT-CX-0: Systems Integration Compl	0	0	0%		19-Feb-27	1				
		DC-HYP-FINAL-6.12.8 Integrated Sys	353	353	0%	23-Jan-26	10-Mar-27	0				
		IST-010 Prepare Integrated System:	10	10	0%	23-Jan-26	03-Feb-26	328				
		IST-020 Conduct Utility Power Failur	5	5	0%	22-Feb-27	26-Feb-27	0				
		IST-030 Conduct Generator Transfe	5	5	0%	22-Feb-27	26-Feb-27	0				
		IST-040 Conduct UPS Battery Ride-	5	5	0%	22-Feb-27	26-Feb-27	0				
		IST-050 Conduct Cooling Failure Sc	5	5	0%	22-Feb-27	26-Feb-27	0				
		IST-060 Conduct Fire Alarm Integrat	5	5	0%	22-Feb-27	26-Feb-27	0				
		IST-070 Conduct BMS DCIM Alarm	3	3	0%	22-Feb-27	24-Feb-27	2				
		IST-080 Resolve IST Deficiencies	10	10	0%	27-Feb-27	10-Mar-27	0				
		IST-090 Integrated Systems Testing	0	0	0%		10-Mar-27	0				
		DC-HYP-FINAL-6.12.9 Load Bank & F	17	17	0%	02-Feb-27	20-Feb-27	0				
		LBT-010 Mobilize Load Bank Equipn	5	5	0%	02-Feb-27	06-Feb-27	0				
		LBT-020 Connect Load Bank Equipr	5	5	0%	08-Feb-27	12-Feb-27	0				
		LBT-030 Perform UPS Load Bank Te	5	5	0%	13-Feb-27	18-Feb-27	0				
		LBT-040 Perform Generator Load Bc	5	5	0%	13-Feb-27	18-Feb-27	0				
		LBT-050 Perform Cooling Performan	5	5	0%	13-Feb-27	18-Feb-27	0				
		LBT-060 Verify Data Hall Environmer	2	2	0%	19-Feb-27	20-Feb-27	0				
		LBT-070 Load Bank and Performanc	0	0	0%		20-Feb-27	0				
		DC-HYP-FINAL-6.12.10 Reliability / R	365	365	0%	23-Jan-26	24-Mar-27	0				
		RRT-010 Develop Reliability Test Pla	10	10	0%	23-Jan-26	03-Feb-26	343				
			Page 51 of 56					TASK filter: All Activities				
								© Oracle Corporation				

Hyperscale Data Center Development			Classic Schedule Layout					03-Oct-26 22:50			
Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025		Qtr 1, 2026	
								Nov	Dec	Jan	
<											

