

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float
DC-HYP-FINAL-6	Hyperscale D	401	381	0%	05-Jan-26 A	19-Jul-27	0
DC-HYP-FINAL-6.1	Project Man	30	10	0%	05-Jan-26	13-Feb-26	86
DC-HYP-FINAL-6.1.1	Project Manage	20	0	0%	05-Jan-26	19-Jan-26	
PM-001	Notice to Proceed	0	0	0%	05-Jan-26		
PM-010	Project Kick-Off Meeting	1	0	100%	05-Jan-26	05-Jan-26	
PM-020	Establish Project Organizati	5	0	100%	06-Jan-26	12-Jan-26	
PM-030	Establish Project Managem	10	0	100%	06-Jan-26	19-Jan-26	
DC-HYP-FINAL-6.1.2	Project Control	30	10	0%	05-Jan-26	13-Feb-26	26
PC-010	Develop Project Controls Pl	5	0	100%	05-Jan-26	09-Jan-26	
PC-020	Develop Detailed Baseline	15	0	100%	12-Jan-26	30-Jan-26	
PC-030	Baseline Schedule Review	5	5	0%	02-Feb-26	06-Feb-26	26
PC-040	Baseline Schedule Approva	5	5	0%	09-Feb-26	13-Feb-26	26
PC-050	Baseline Programme Appro	0	0	0%		13-Feb-26	26
DC-HYP-FINAL-6.1.3	HSE Manageme	18	0	0%	05-Jan-26	28-Jan-26	
HSE-010	Develop Project HSE Plan	10	0	100%	05-Jan-26	16-Jan-26	
HSE-020	HSE Plan Review	5	0	100%	19-Jan-26	23-Jan-26	
HSE-030	HSE Plan Approval	3	0	100%	26-Jan-26	28-Jan-26	
DC-HYP-FINAL-6.1.4	Quality Manage	18	0	0%	05-Jan-26	28-Jan-26	
QA-010	Develop Project Quality Pla	10	0	100%	05-Jan-26	16-Jan-26	
QA-020	Quality Plan Review	5	0	100%	19-Jan-26	23-Jan-26	
QA-030	Quality Plan Approval	3	0	100%	26-Jan-26	28-Jan-26	
DC-HYP-FINAL-6.1.5	Contract & Con	10	0	0%	06-Jan-26	19-Jan-26	
COM-010	Establish Contract Administ	5	0	100%	06-Jan-26	12-Jan-26	
COM-020	Establish Change and Varia	5	0	100%	13-Jan-26	19-Jan-26	
COM-030	Establish Payment and Cos	5	0	100%	13-Jan-26	19-Jan-26	
COM-040	Establish Commercial Repo	5	0	100%	13-Jan-26	19-Jan-26	
DC-HYP-FINAL-6.1.6	Stakeholder & I	20	1	0%	06-Jan-26	02-Feb-26	35
INT-010	Develop Stakeholder Regis	5	0	100%	06-Jan-26	12-Jan-26	
INT-020	Develop Interface Register	10	0	100%	13-Jan-26	26-Jan-26	
INT-030	Establish Interface Manage	5	1	80%	27-Jan-26	02-Feb-26	35
INT-040	Establish Communication a	5	0	100%	13-Jan-26	19-Jan-26	
DC-HYP-FINAL-6.2	Design & En	91	72	0%	06-Jan-26	12-May-26	134
DC-HYP-FINAL-6.2.1	Design Manage	73	54	0%	06-Jan-26	16-Apr-26	152

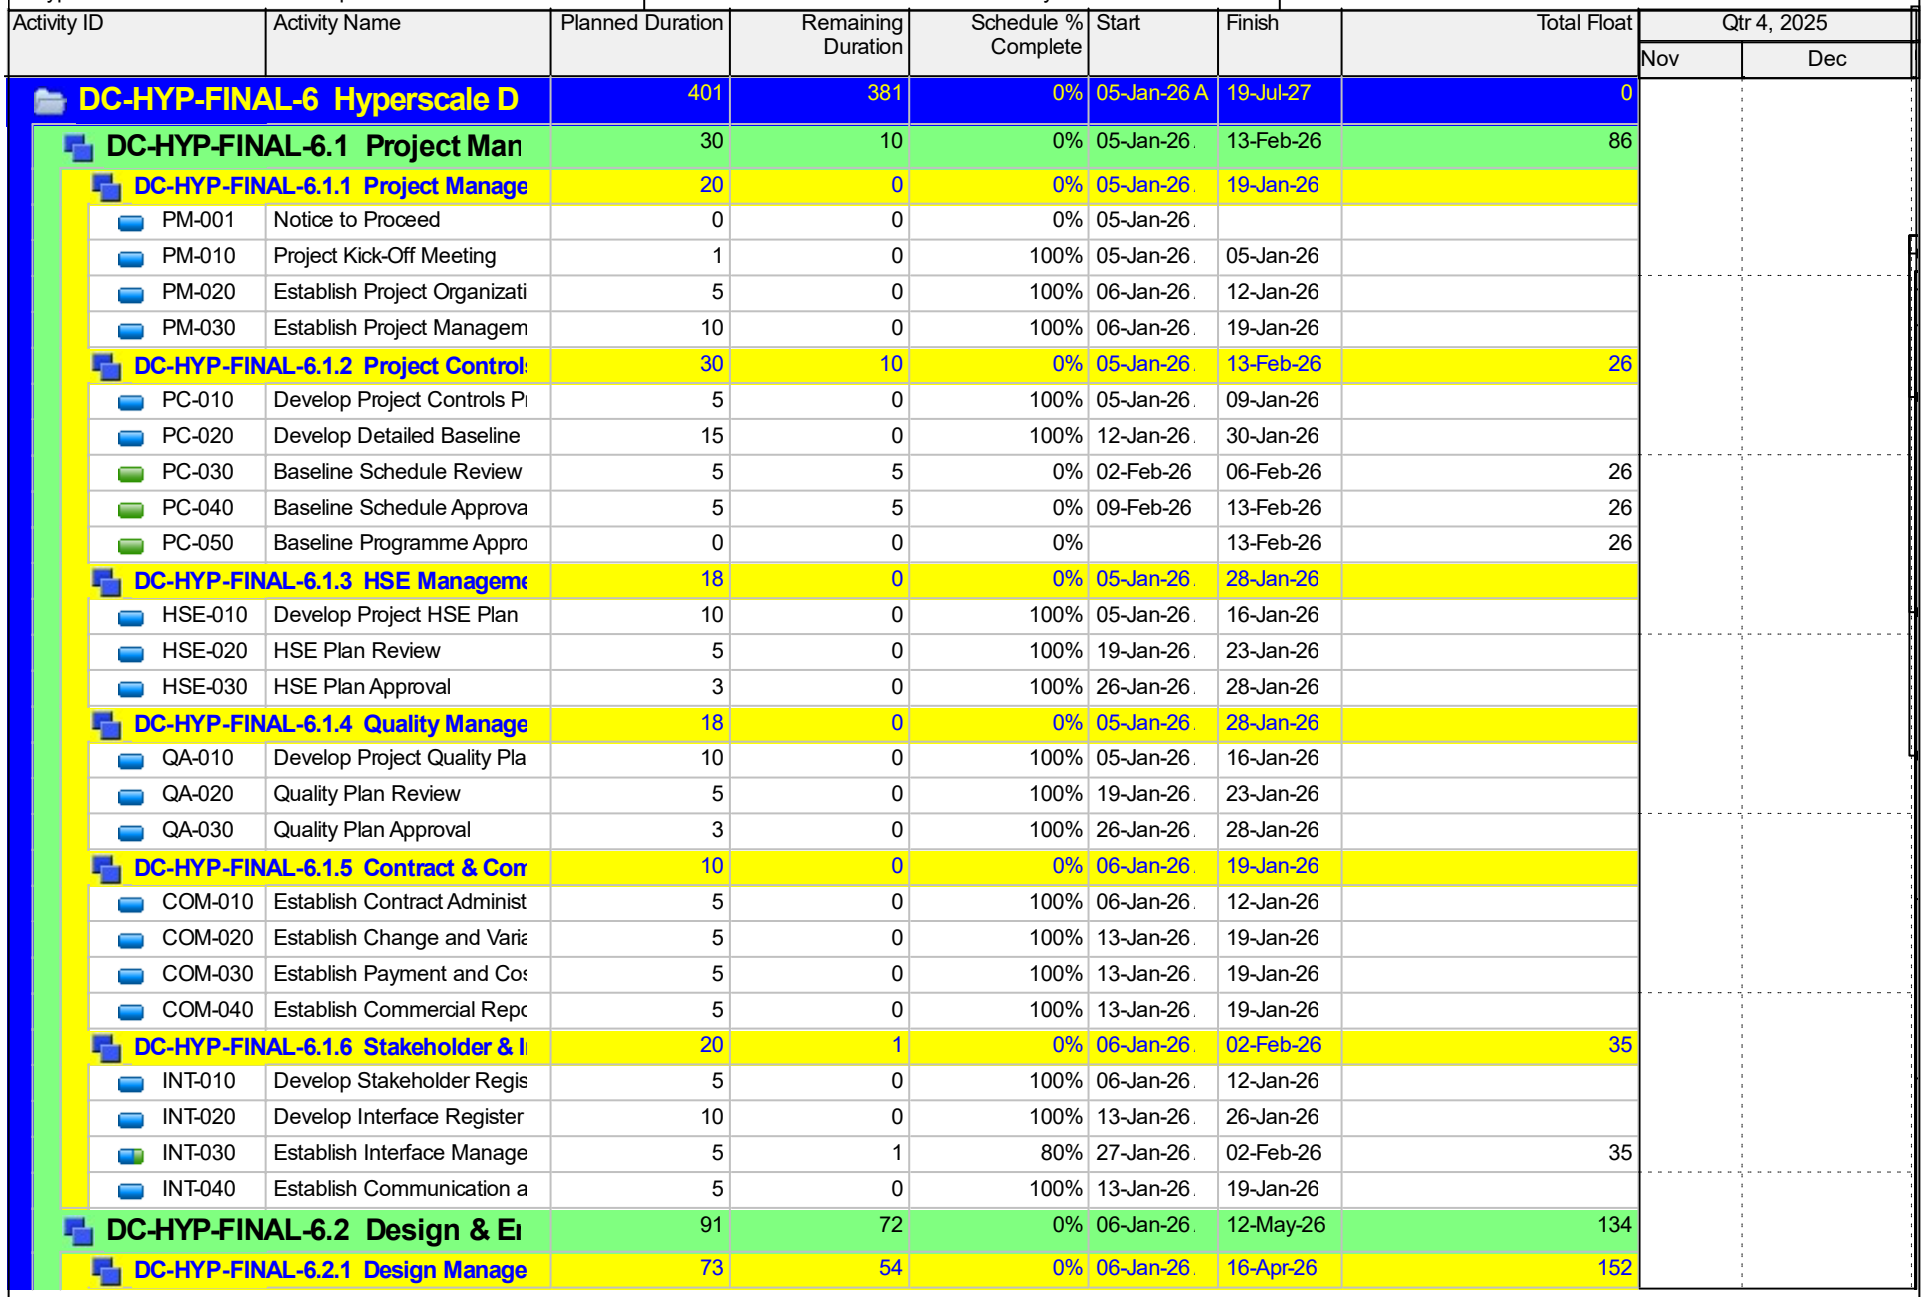


© Oracle Corporation

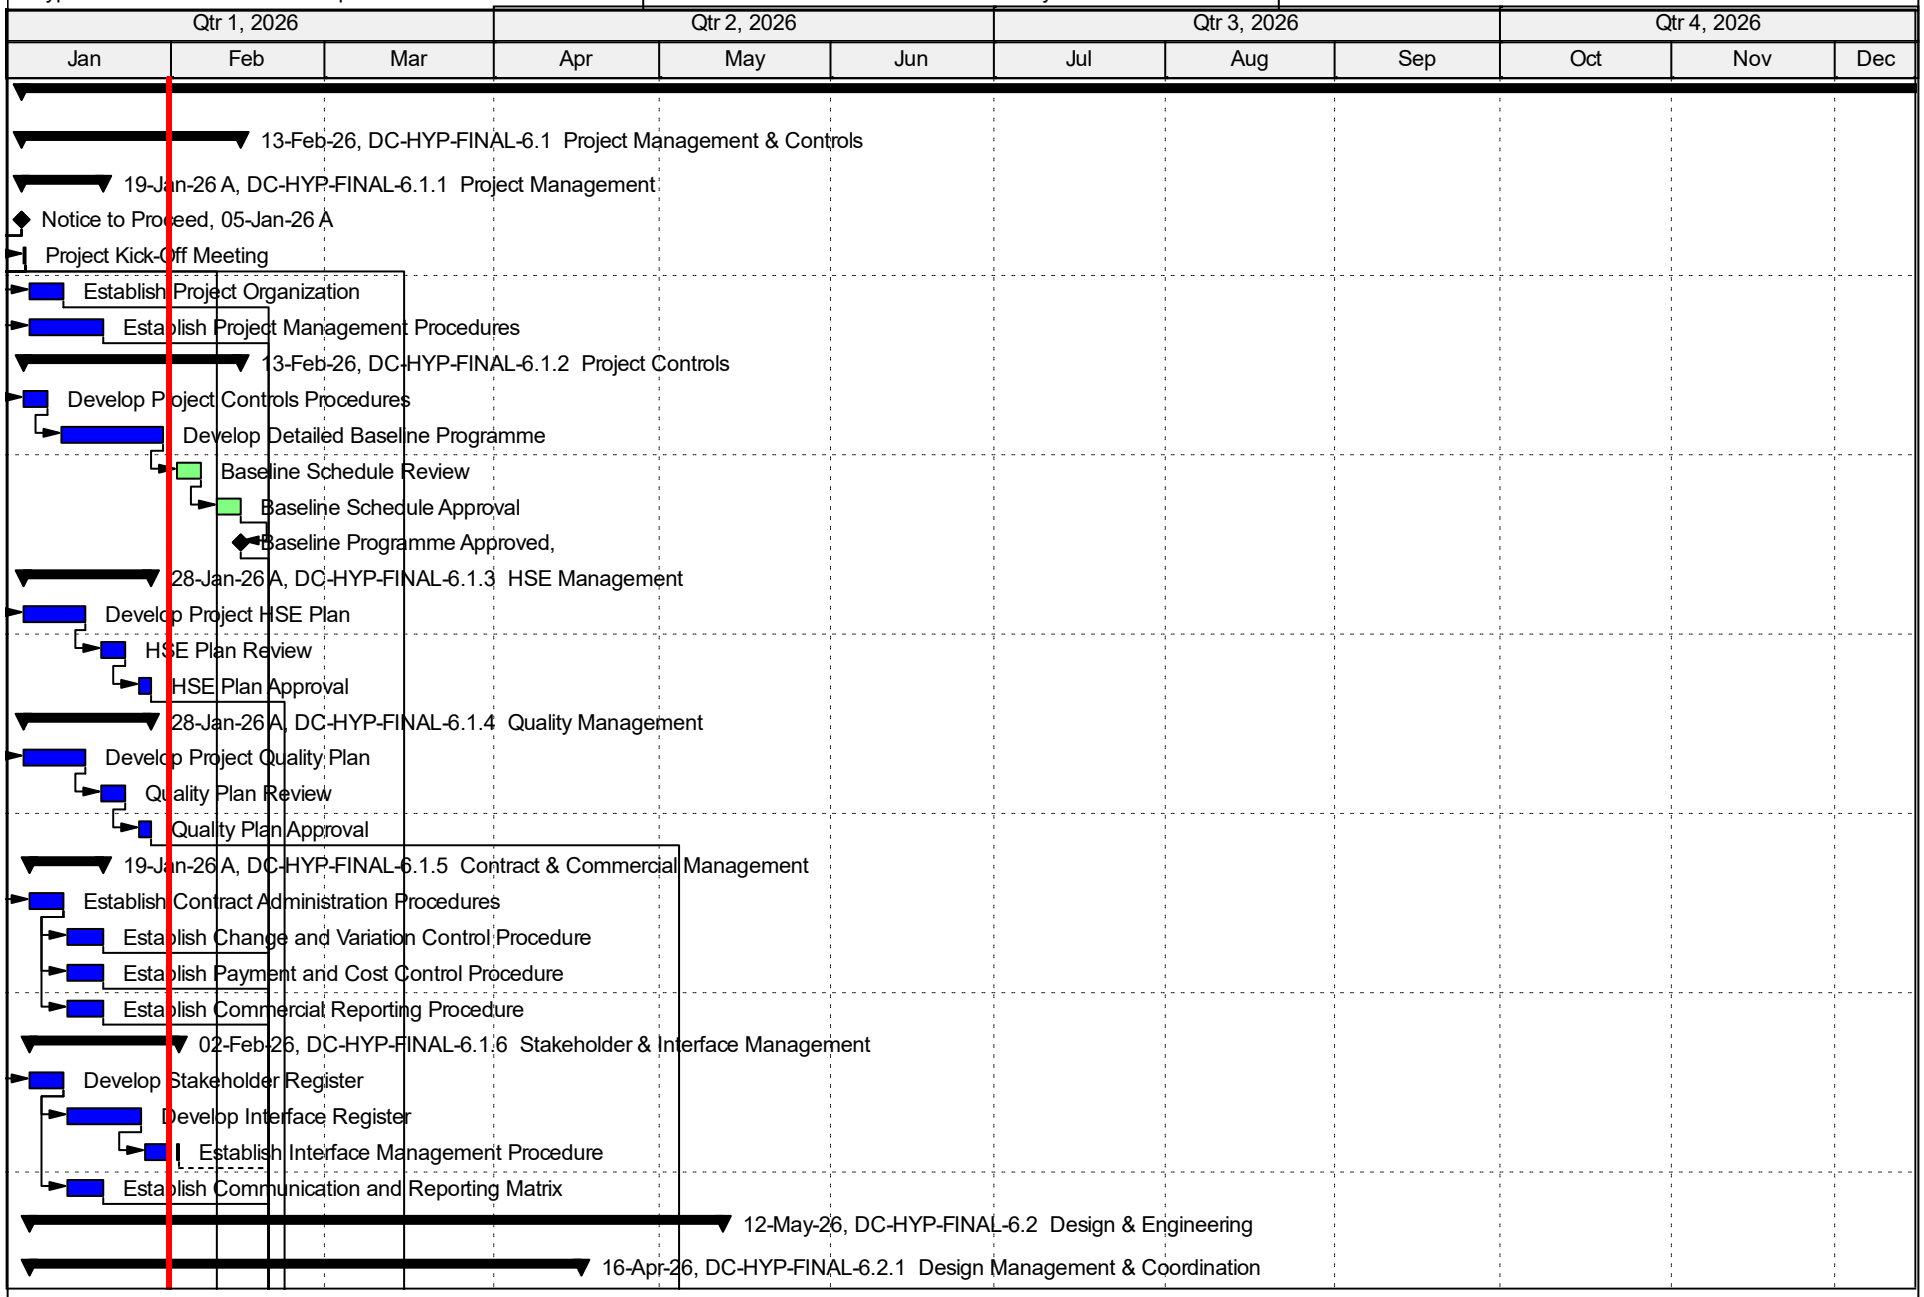

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DM-010	Establish Design Managem	5	0	100%	06-Jan-26	12-Jan-26			
DM-020	Establish Design Deliverabl	3	0	100%	08-Jan-26	12-Jan-26			
DM-030	Establish Design Responsil	3	0	100%	08-Jan-26	12-Jan-26			
DM-040	Develop Design Coordinati	5	0	100%	13-Jan-26	19-Jan-26			
DM-050	Conduct Multidiscipline Des	40	31	22.5%	20-Jan-26	16-Mar-26	175		
DM-060	Design Coordination Comp	0	0	0%		16-Apr-26	152		
DC-HYP-FINAL-6.2.2 Civil & Structur		46	32	0%	13-Jan-26	17-Mar-26	64		
CIV-010	Develop Civil and Structura	5	0	100%	13-Jan-26	20-Jan-26			
CIV-020	Develop Site Grading and I	10	2	90%	21-Jan-26	03-Feb-26	89		
CIV-030	Develop Foundation Design	15	6	60%	20-Jan-26	09-Feb-26	85		
CIV-040	Develop Main Structural Fra	20	11	45%	20-Jan-26	16-Feb-26	12		
CIV-050	Develop Equipment Found	10	10	0%	25-Feb-26	10-Mar-26	64		
CIV-060	Civil and Structural Design I	5	5	0%	11-Mar-26	17-Mar-26	64		
CIV-070	Civil and Structural Design /	0	0	0%		17-Mar-26	64		
DC-HYP-FINAL-6.2.3 Architectural De		32	18	0%	13-Jan-26	25-Feb-26	94		
ARC-010	Develop Architectural Desig	5	0	100%	13-Jan-26	21-Jan-26			
ARC-020	Develop Data Hall Layout	10	1	90%	20-Jan-26	02-Feb-26	17		
ARC-030	Develop Technical Room L	10	3	90%	21-Jan-26	04-Feb-26	0		
ARC-040	Develop Building Envelope	15	6	60%	20-Jan-26	09-Feb-26	101		
ARC-050	Develop Internal Partition a	10	10	0%	05-Feb-26	18-Feb-26	94		
ARC-060	Architectural Design Reviev	5	5	0%	19-Feb-26	25-Feb-26	94		
ARC-070	Architectural Design Approv	0	0	0%		25-Feb-26	94		
DC-HYP-FINAL-6.2.4 Electrical Desig		54	40	0%	13-Jan-26	27-Mar-26	0		
ELE-D-01	Develop Electrical Design C	5	0	100%	13-Jan-26	22-Jan-26			
ELE-D-02	Develop Electrical Load Sch	10	3	90%	21-Jan-26	04-Feb-26	0		
ELE-D-03	Develop MV Distribution De	15	15	0%	12-Feb-26	04-Mar-26	10		
ELE-D-04	Develop Transformer Desig	10	10	0%	05-Feb-26	18-Feb-26	20		
ELE-D-05	Develop Generator System	10	10	0%	05-Feb-26	18-Feb-26	20		
ELE-D-06	Develop LV Distribution Des	15	15	0%	05-Feb-26	25-Feb-26	0		
ELE-D-07	Develop UPS and Battery S	15	15	0%	05-Feb-26	25-Feb-26	0		
ELE-D-08	Develop Busway and Data	15	15	0%	26-Feb-26	18-Mar-26	0		
ELE-D-09	Develop Earthing and Light	10	10	0%	17-Feb-26	02-Mar-26	12		
ELE-D-10	Electrical Design Review	7	7	0%	19-Mar-26	27-Mar-26	0		
ELE-D-11	Electrical Design Approved	0	0	0%		27-Mar-26	0		


© Oracle Corporation

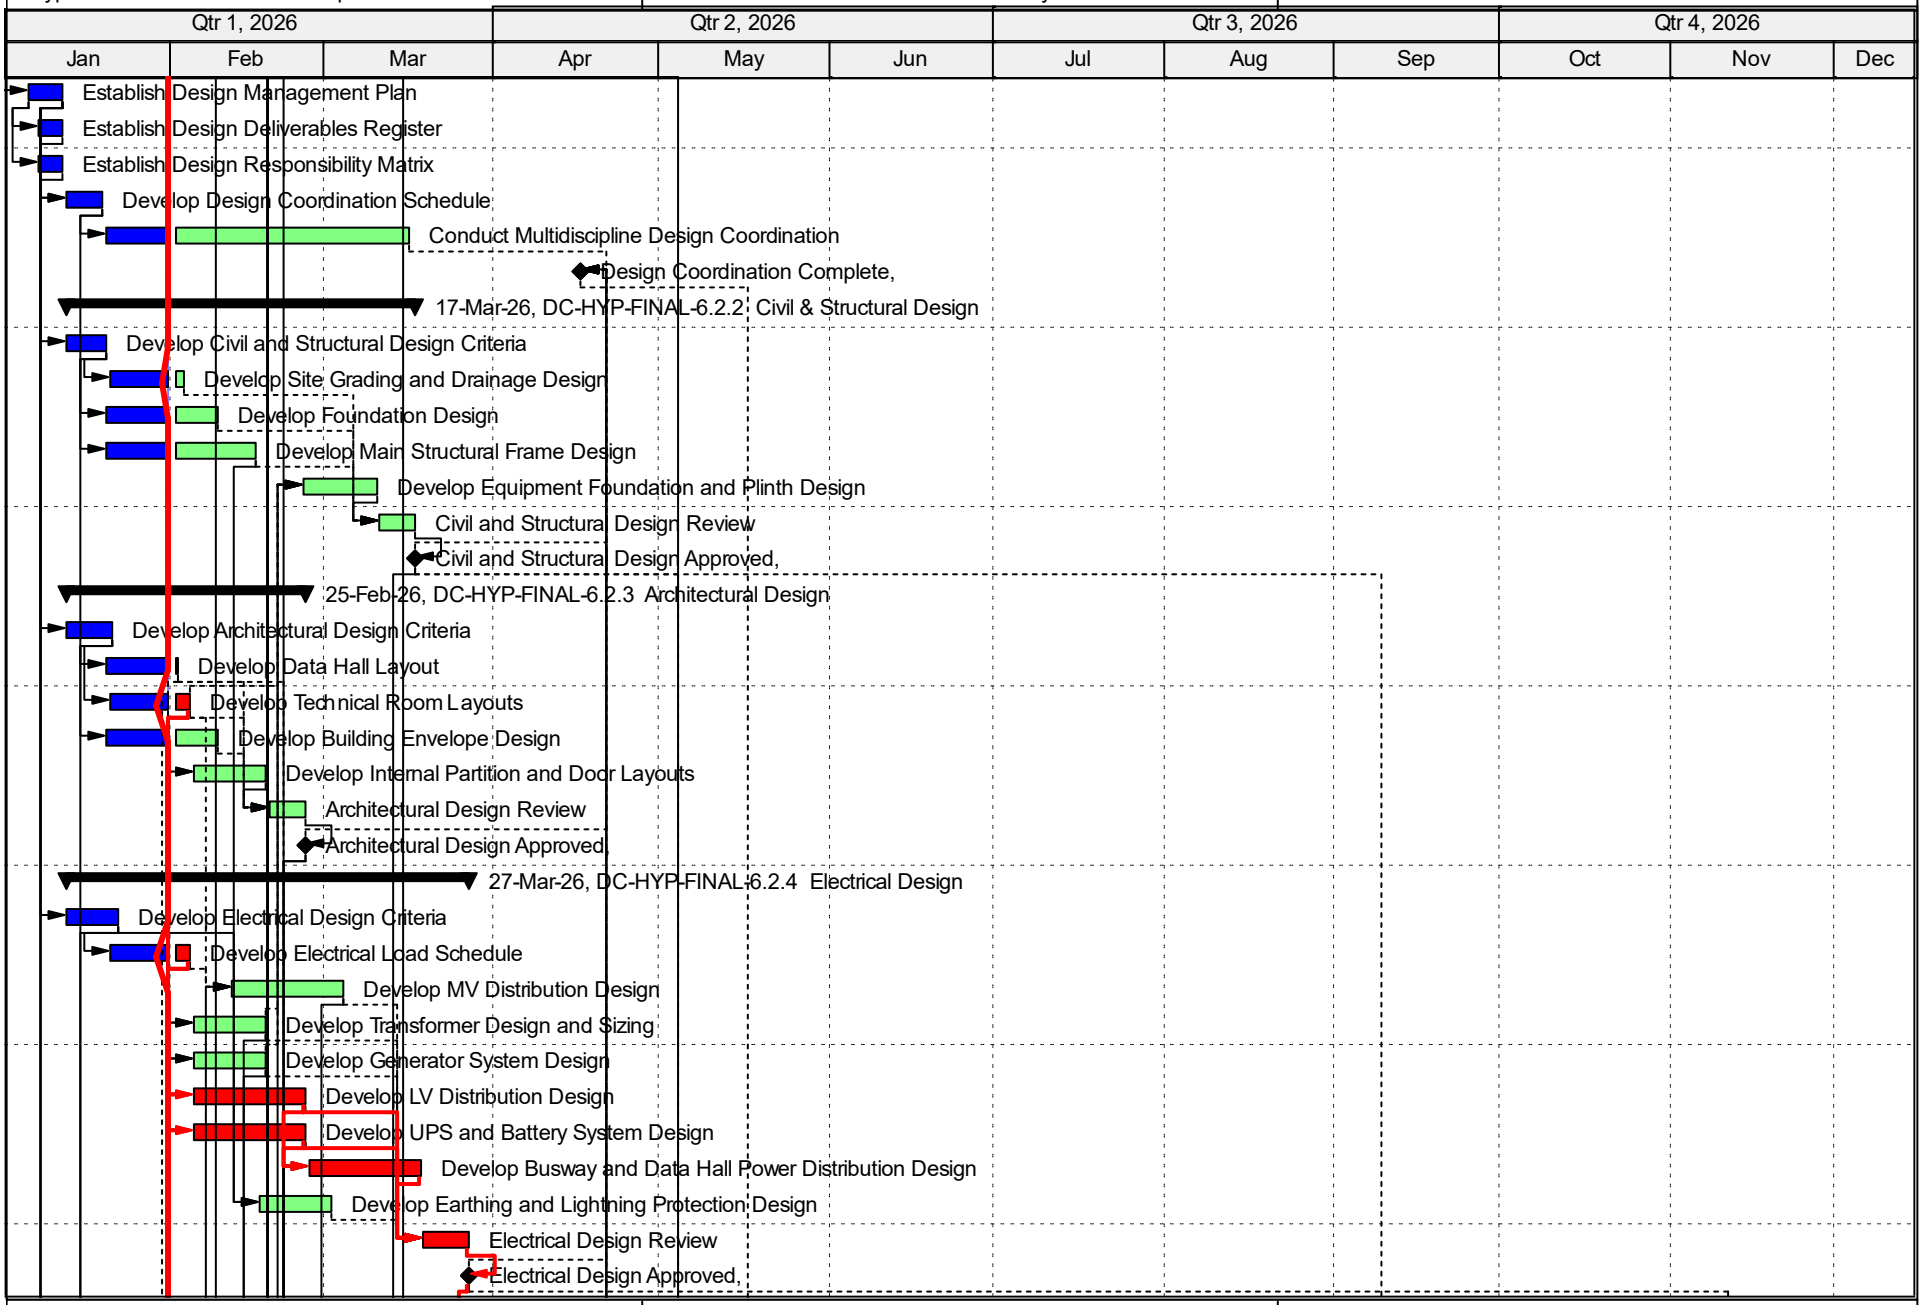

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.2.5	**Mechanical & C**	43	29	0%	13-Jan-26	12-Mar-26	39		
MEC-D-0	Develop Mechanical Desigr	5	0	100%	13-Jan-26	21-Jan-26			
MEC-D-0	Develop Cooling Load Calc	10	2	90%	21-Jan-26	03-Feb-26	39		
MEC-D-0	Develop Cooling Plant Des	15	15	0%	04-Feb-26	24-Feb-26	39		
MEC-D-0	Develop Chilled Water Distr	15	15	0%	11-Feb-26	03-Mar-26	39		
MEC-D-0	Develop CRAH CRAC Sys	10	10	0%	04-Feb-26	17-Feb-26	44		
MEC-D-0	Develop Ventilation and Exl	10	10	0%	05-Feb-26	18-Feb-26	43		
MEC-D-0	Develop Mechanical Contrc	10	10	0%	18-Feb-26	03-Mar-26	39		
MEC-D-0	Mechanical Design Review	7	7	0%	04-Mar-26	12-Mar-26	39		
MEC-D-0	Mechanical Design Approve	0	0	0%		12-Mar-26	39		
DC-HYP-FINAL-6.2.6	**Fire & Life Safet**	21	7	0%	13-Jan-26	10-Feb-26	145		
FLS-D-01	Develop Fire and Life Safet	5	0	100%	13-Jan-26	19-Jan-26			
FLS-D-02	Develop Fire Detection and	10	1	90%	20-Jan-26	02-Feb-26	113		
FLS-D-03	Develop Fire Suppression S	10	1	90%	20-Jan-26	02-Feb-26	113		
FLS-D-04	Develop VESDA and Early	8	2	100%	21-Jan-26	03-Feb-26	112		
FLS-D-05	Develop Fire System Interfa	5	1	80%	27-Jan-26	03-Feb-26	112		
FLS-D-06	Fire and Life Safety Design	5	5	0%	04-Feb-26	10-Feb-26	145		
FLS-D-07	Fire and Life Safety Design	0	0	0%		10-Feb-26	145		
DC-HYP-FINAL-6.2.7	**BMS, DCIM & C**	56	47	0%	20-Jan-26	07-Apr-26	82		
BMS-D-0	Develop BMS Design Archi	10	1	90%	20-Jan-26	02-Feb-26	103		
BMS-D-0	Develop Mechanical Contrc	10	10	0%	04-Mar-26	17-Mar-26	82		
BMS-D-0	Develop Electrical Monitorir	10	10	0%	26-Feb-26	11-Mar-26	86		
BMS-D-0	Develop DCIM Architecture	10	10	0%	03-Feb-26	16-Feb-26	103		
BMS-D-0	Develop Controls Integratio	10	10	0%	18-Mar-26	31-Mar-26	82		
BMS-D-0	BMS DCIM and Controls D	5	5	0%	01-Apr-26	07-Apr-26	82		
BMS-D-0	BMS DCIM and Controls D	0	0	0%		07-Apr-26	82		
DC-HYP-FINAL-6.2.8	**ICT & Security S**	35	21	0%	13-Jan-26	02-Mar-26	185		
ICT-D-010	Develop ICT Infrastructure I	10	0	100%	13-Jan-26	26-Jan-26			
ICT-D-020	Develop Structured Cabling	10	6	40%	27-Jan-26	09-Feb-26	98		
ICT-D-030	Develop CCTV System Des	8	4	50%	27-Jan-26	05-Feb-26	100		
ICT-D-040	Develop Access Control Sy	8	4	50%	27-Jan-26	05-Feb-26	100		
ICT-D-050	Develop Security System In	10	10	0%	10-Feb-26	23-Feb-26	98		
ICT-D-060	ICT and Security Design Re	5	5	0%	24-Feb-26	02-Mar-26	185		
ICT-D-070	ICT and Security Design Ap	0	0	0%		02-Mar-26	185		


© Oracle Corporation

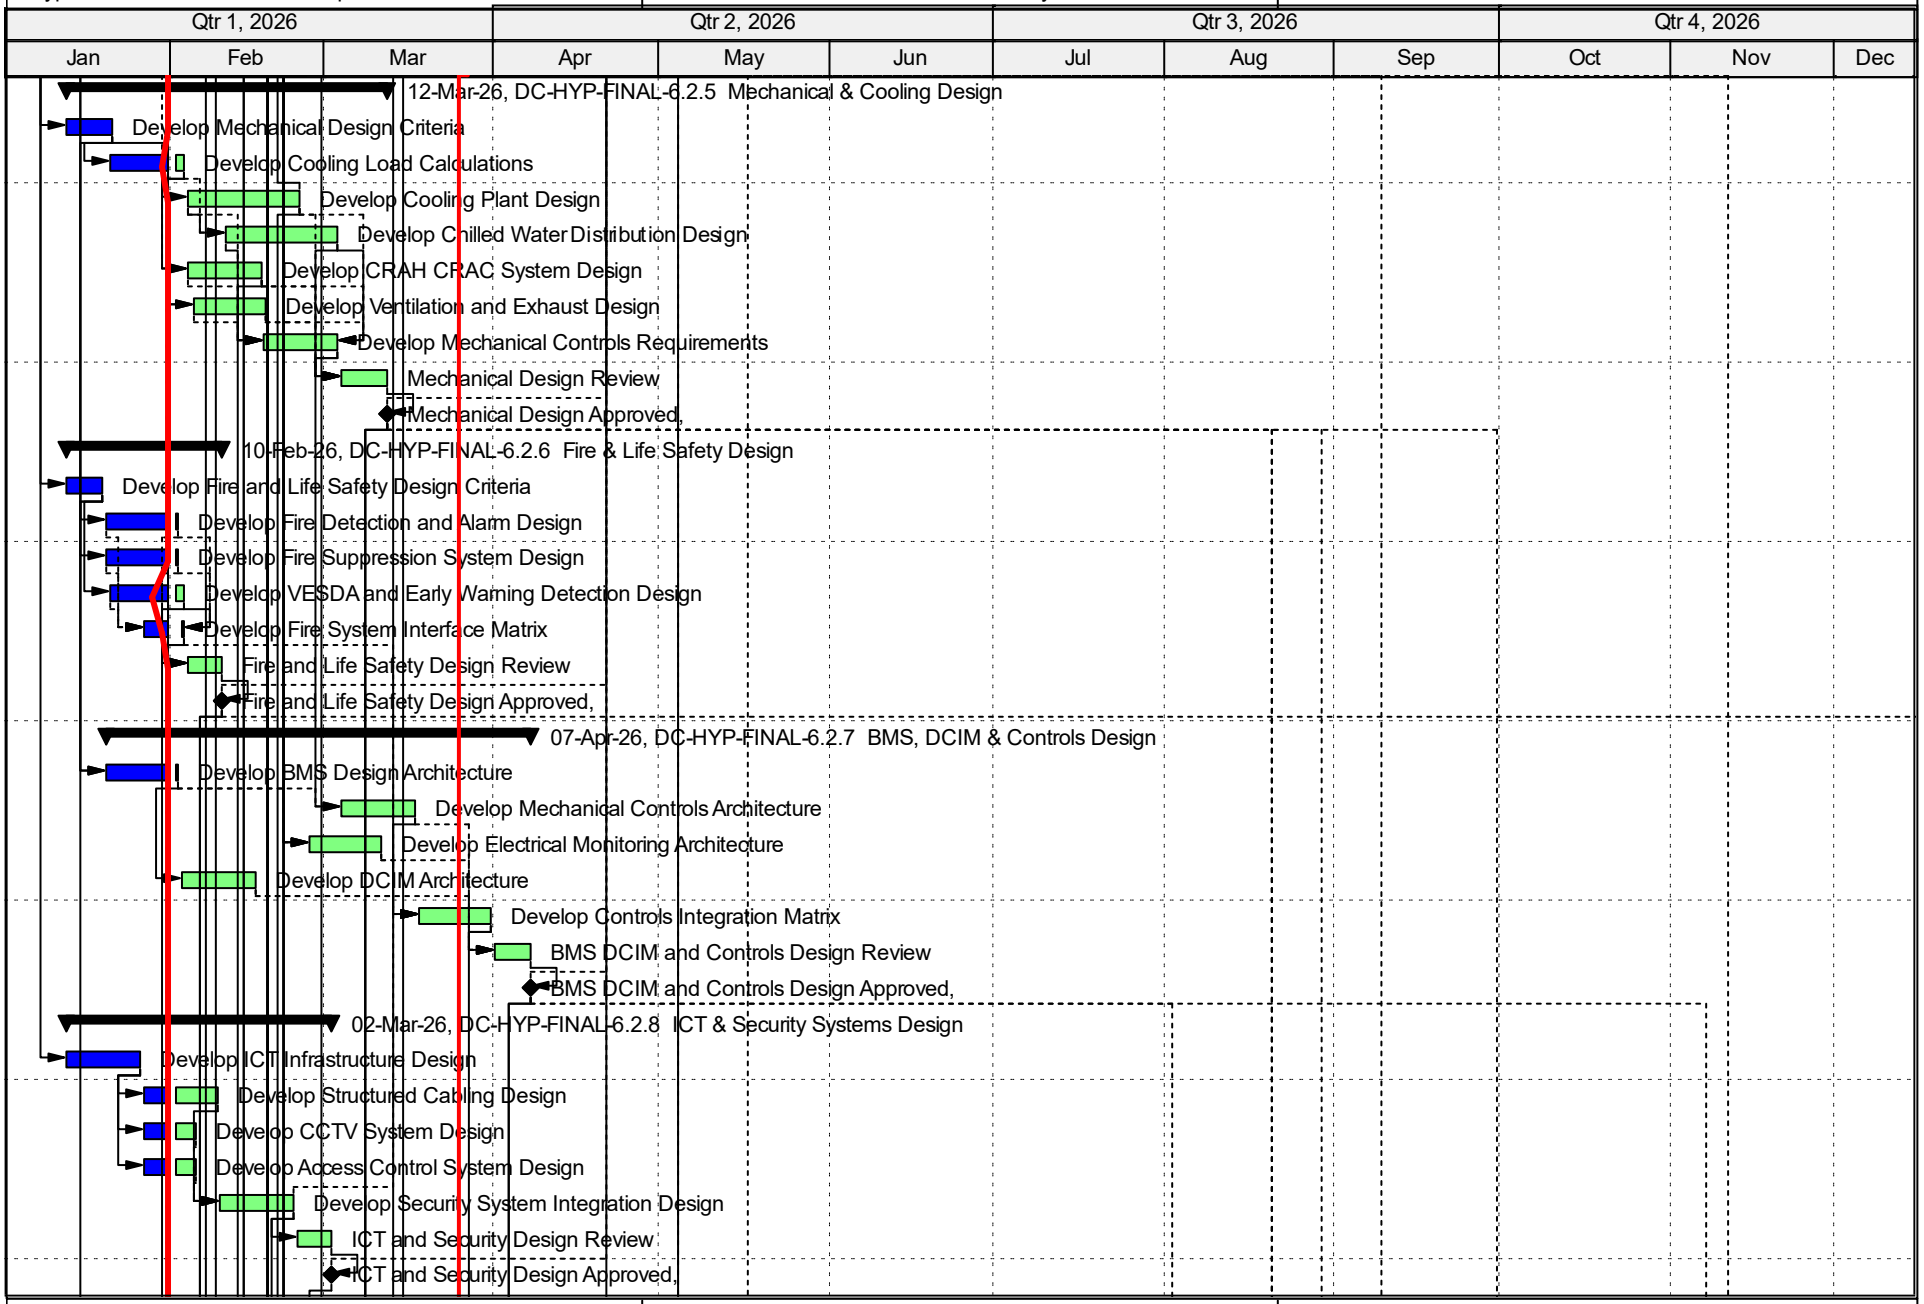

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.2.9	Utility & Grid Co	51	51	0%	05-Feb-26	16-Apr-26	138		
UTL-D-01	Confirm Utility Power Requi	5	5	0%	05-Feb-26	11-Feb-26	10		
UTL-D-02	Develop Utility Connection	15	15	0%	12-Feb-26	04-Mar-26	148		
UTL-D-03	Develop Incoming MV Con	15	15	0%	12-Feb-26	04-Mar-26	138		
UTL-D-04	Coordinate Utility Protectior	10	10	0%	05-Mar-26	18-Mar-26	138		
UTL-D-05	Submit Utility Connection D	1	1	0%	19-Mar-26	19-Mar-26	138		
UTL-D-06	Utility Design Review	20	20	0%	20-Mar-26	16-Apr-26	138		
UTL-D-07	Utility Connection Design A	0	0	0%		16-Apr-26	138		
DC-HYP-FINAL-6.2.10	Shop Drawing	81	65	0%	20-Jan-26	12-May-26	134		
SD-010	Establish Shop Drawing Scl	5	0	100%	20-Jan-26	26-Jan-26			
SD-020	Prepare Civil and Structural	15	15	0%	18-Mar-26	07-Apr-26	149		
SD-030	Prepare Architectural Shop	15	15	0%	26-Feb-26	18-Mar-26	163		
SD-040	Prepare Electrical Shop Dra	20	20	0%	30-Mar-26	24-Apr-26	136		
SD-050	Prepare Mechanical Shop D	20	20	0%	13-Mar-26	09-Apr-26	147		
SD-060	Prepare Fire and Life Safety	15	15	0%	11-Feb-26	03-Mar-26	174		
SD-070	Prepare BMS DCIM and Co	15	15	0%	08-Apr-26	28-Apr-26	134		
SD-080	Consultant Review of Shop	10	10	0%	15-Apr-26	28-Apr-26	134		
SD-090	Resolve Shop Drawing Cor	10	10	0%	29-Apr-26	12-May-26	134		
SD-100	Technical Shop Drawings Ap	0	0	0%		12-May-26	134		
DC-HYP-FINAL-6.3	Procuremer	244	225	0%	06-Jan-26	11-Dec-26	93		
DC-HYP-FINAL-6.3.1	Procurement M	39	20	0%	06-Jan-26	27-Feb-26	127		
PRM-010	Develop Project Procureme	5	0	100%	06-Jan-26	12-Jan-26			
PRM-020	Develop Procurement Sche	5	0	100%	13-Jan-26	19-Jan-26			
PRM-030	Establish Approved Vendor	7	3	100%	21-Jan-26	04-Feb-26	127		
PRM-040	Establish Procurement Trac	10	10	0%	05-Feb-26	18-Feb-26	127		
PRM-050	Procurement Strategy Appr	7	7	0%	19-Feb-26	27-Feb-26	127		
DC-HYP-FINAL-6.3.2	MV/LV Switchg	167	167	0%	05-Mar-26	23-Oct-26	21		
SWG-010	Prepare MV/LV Switchgear	7	7	0%	05-Mar-26	13-Mar-26	31		
SWG-020	MV/LV Switchgear Technica	7	7	0%	30-Mar-26	07-Apr-26	21		
SWG-030	Issue Purchase Order - MV/	3	3	0%	08-Apr-26	10-Apr-26	21		
SWG-040	Manufacture MV/LV Switch	120	120	0%	13-Apr-26	25-Sep-26	21		
SWG-050	Factory Acceptance Test - M	3	3	0%	28-Sep-26	30-Sep-26	21		
SWG-060	Ship MV/LV Switchgear	15	15	0%	01-Oct-26	21-Oct-26	21		


© Oracle Corporation

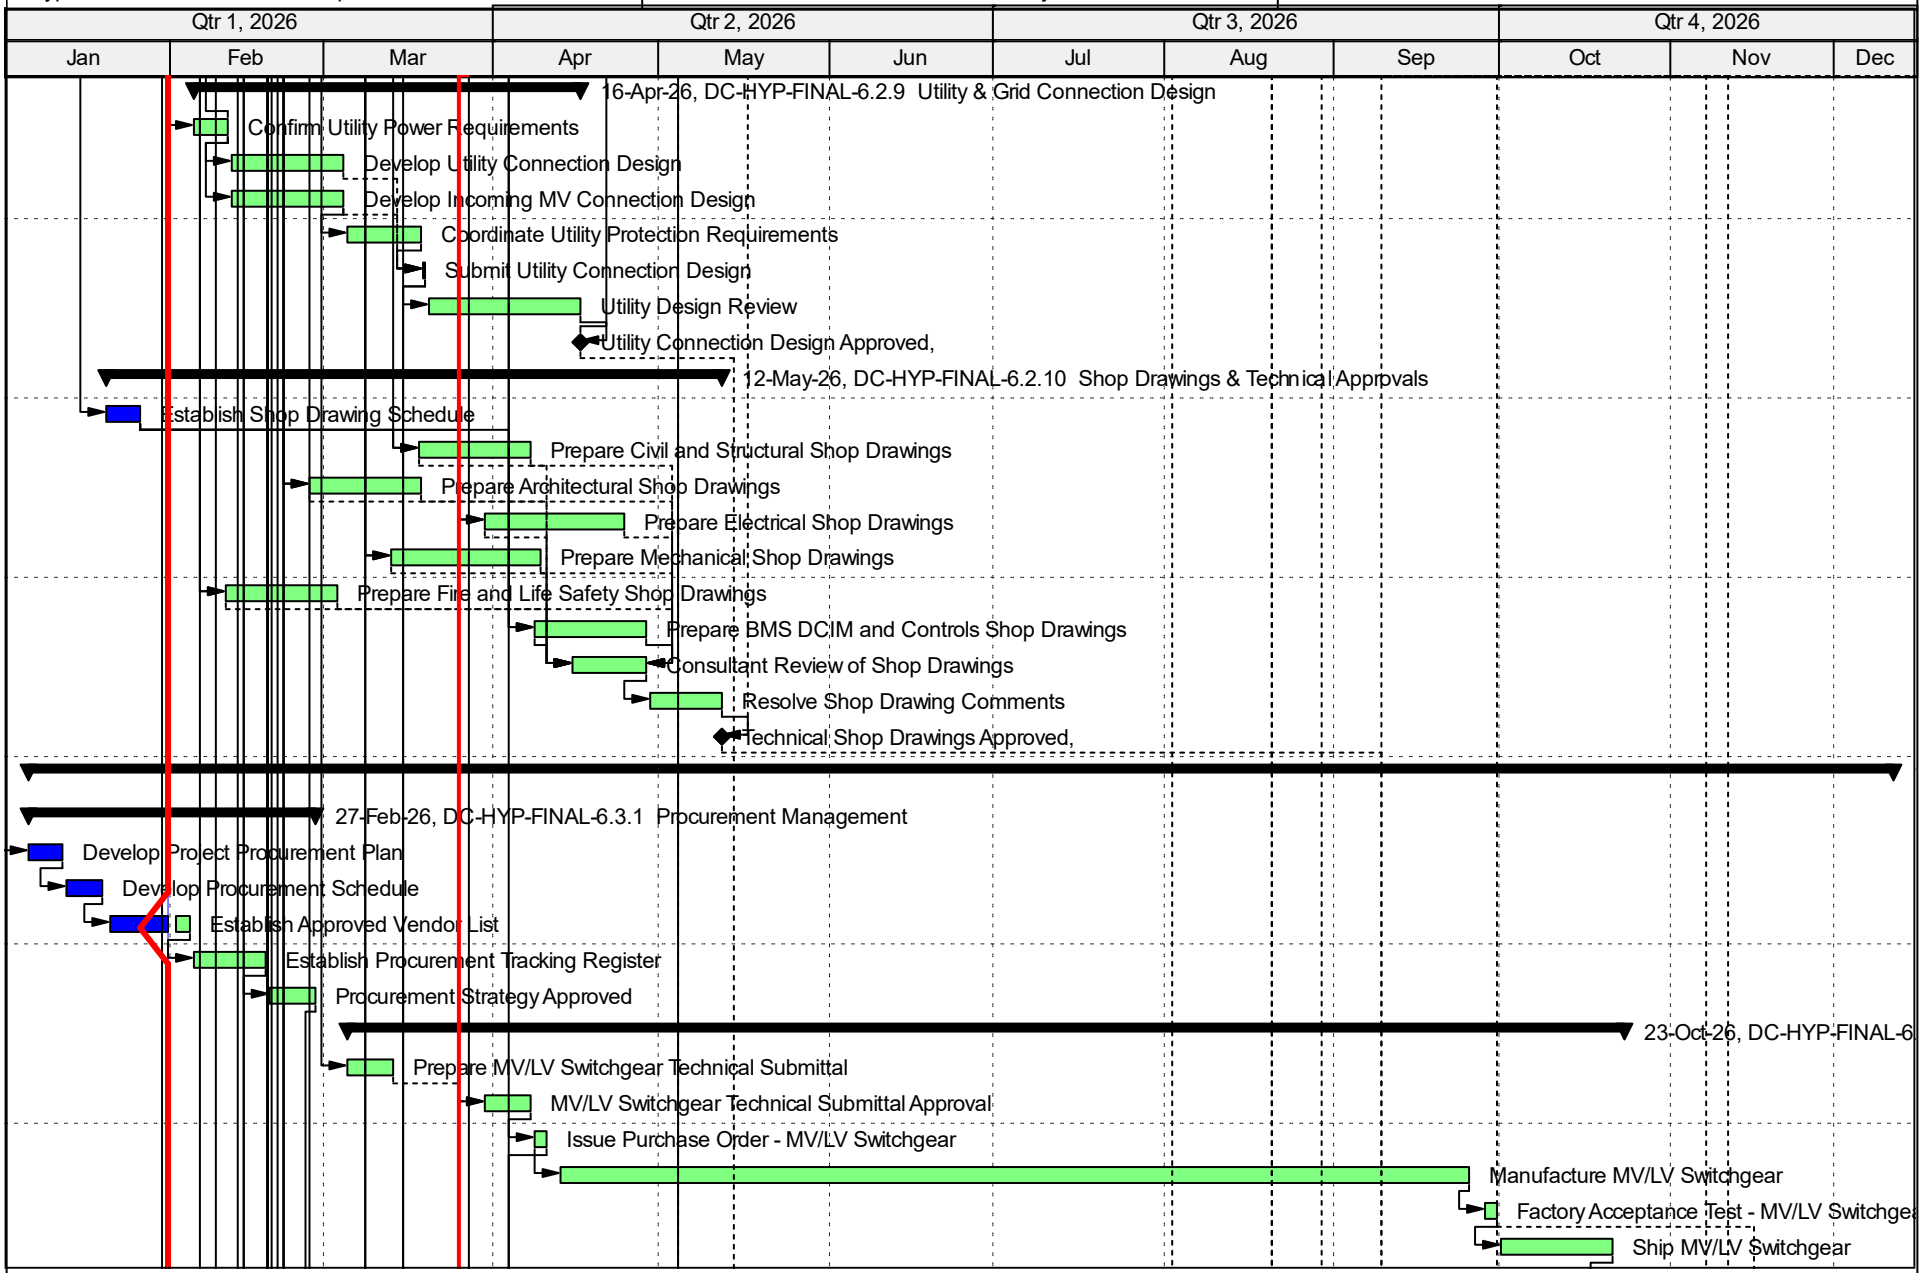

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
SWG-070	Deliver MV/LV Switchgear t	2	2	0%	22-Oct-26	23-Oct-26	21		
DC-HYP-FINAL-6.3.3 Transformers		212	212	0%	19-Feb-26	11-Dec-26	0		
TRF-010	Prepare Transformer Techni	7	7	0%	19-Feb-26	27-Feb-26	20		
TRF-020	Transformer Technical Subn	7	7	0%	30-Mar-26	07-Apr-26	0		
TRF-030	Issue Purchase Order - Trar	3	3	0%	08-Apr-26	10-Apr-26	0		
TRF-040	Manufacture Transformers	150	150	0%	13-Apr-26	06-Nov-26	0		
TRF-050	Factory Acceptance Test - T	3	3	0%	09-Nov-26	11-Nov-26	0		
TRF-060	Ship Transformers	20	20	0%	12-Nov-26	09-Dec-26	0		
TRF-070	Deliver Transformers to Site	2	2	0%	10-Dec-26	11-Dec-26	0		
DC-HYP-FINAL-6.3.4 UPS Systems &		172	172	0%	26-Feb-26	23-Oct-26	37		
UPS-010	Prepare UPS and Battery T	7	7	0%	26-Feb-26	06-Mar-26	52		
UPS-020	UPS and Battery Technical	7	7	0%	30-Mar-26	07-Apr-26	37		
UPS-030	Issue Purchase Order - UPS	3	3	0%	08-Apr-26	10-Apr-26	37		
UPS-040	Manufacture UPS Systems	120	120	0%	13-Apr-26	25-Sep-26	37		
UPS-050	Factory Acceptance Test - U	3	3	0%	28-Sep-26	30-Sep-26	37		
UPS-060	Ship UPS Systems and Bat	15	15	0%	01-Oct-26	21-Oct-26	37		
UPS-070	Deliver UPS Systems and E	2	2	0%	22-Oct-26	23-Oct-26	37		
DC-HYP-FINAL-6.3.5 Standby Gener		212	212	0%	19-Feb-26	11-Dec-26	18		
GEN-010	Prepare Standby Generator	7	7	0%	19-Feb-26	27-Feb-26	38		
GEN-020	Standby Generator Technic	7	7	0%	30-Mar-26	07-Apr-26	18		
GEN-030	Issue Purchase Order - Stal	3	3	0%	08-Apr-26	10-Apr-26	18		
GEN-040	Manufacture Standby Gene	150	150	0%	13-Apr-26	06-Nov-26	18		
GEN-050	Factory Acceptance Test - S	3	3	0%	09-Nov-26	11-Nov-26	18		
GEN-060	Ship Standby Generators	20	20	0%	12-Nov-26	09-Dec-26	18		
GEN-070	Deliver Standby Generators	2	2	0%	10-Dec-26	11-Dec-26	18		
DC-HYP-FINAL-6.3.6 Cooling Plant E		132	132	0%	25-Feb-26	27-Aug-26	39		
CLP-010	Prepare Cooling Plant Equi	7	7	0%	25-Feb-26	05-Mar-26	44		
CLP-020	Cooling Plant Equipment Te	7	7	0%	13-Mar-26	23-Mar-26	39		
CLP-030	Issue Purchase Order - Coc	3	3	0%	24-Mar-26	26-Mar-26	39		
CLP-040	Manufacture Cooling Plant	90	90	0%	27-Mar-26	30-Jul-26	39		
CLP-050	Factory Acceptance Test - C	3	3	0%	31-Jul-26	04-Aug-26	39		
CLP-060	Ship Cooling Plant Equipm	15	15	0%	05-Aug-26	25-Aug-26	39		
CLP-070	Deliver Cooling Plant Equip	2	2	0%	26-Aug-26	27-Aug-26	39		
DC-HYP-FINAL-6.3.7 CRAH/CRAC Ur		137	137	0%	18-Feb-26	27-Aug-26	53		


© Oracle Corporation

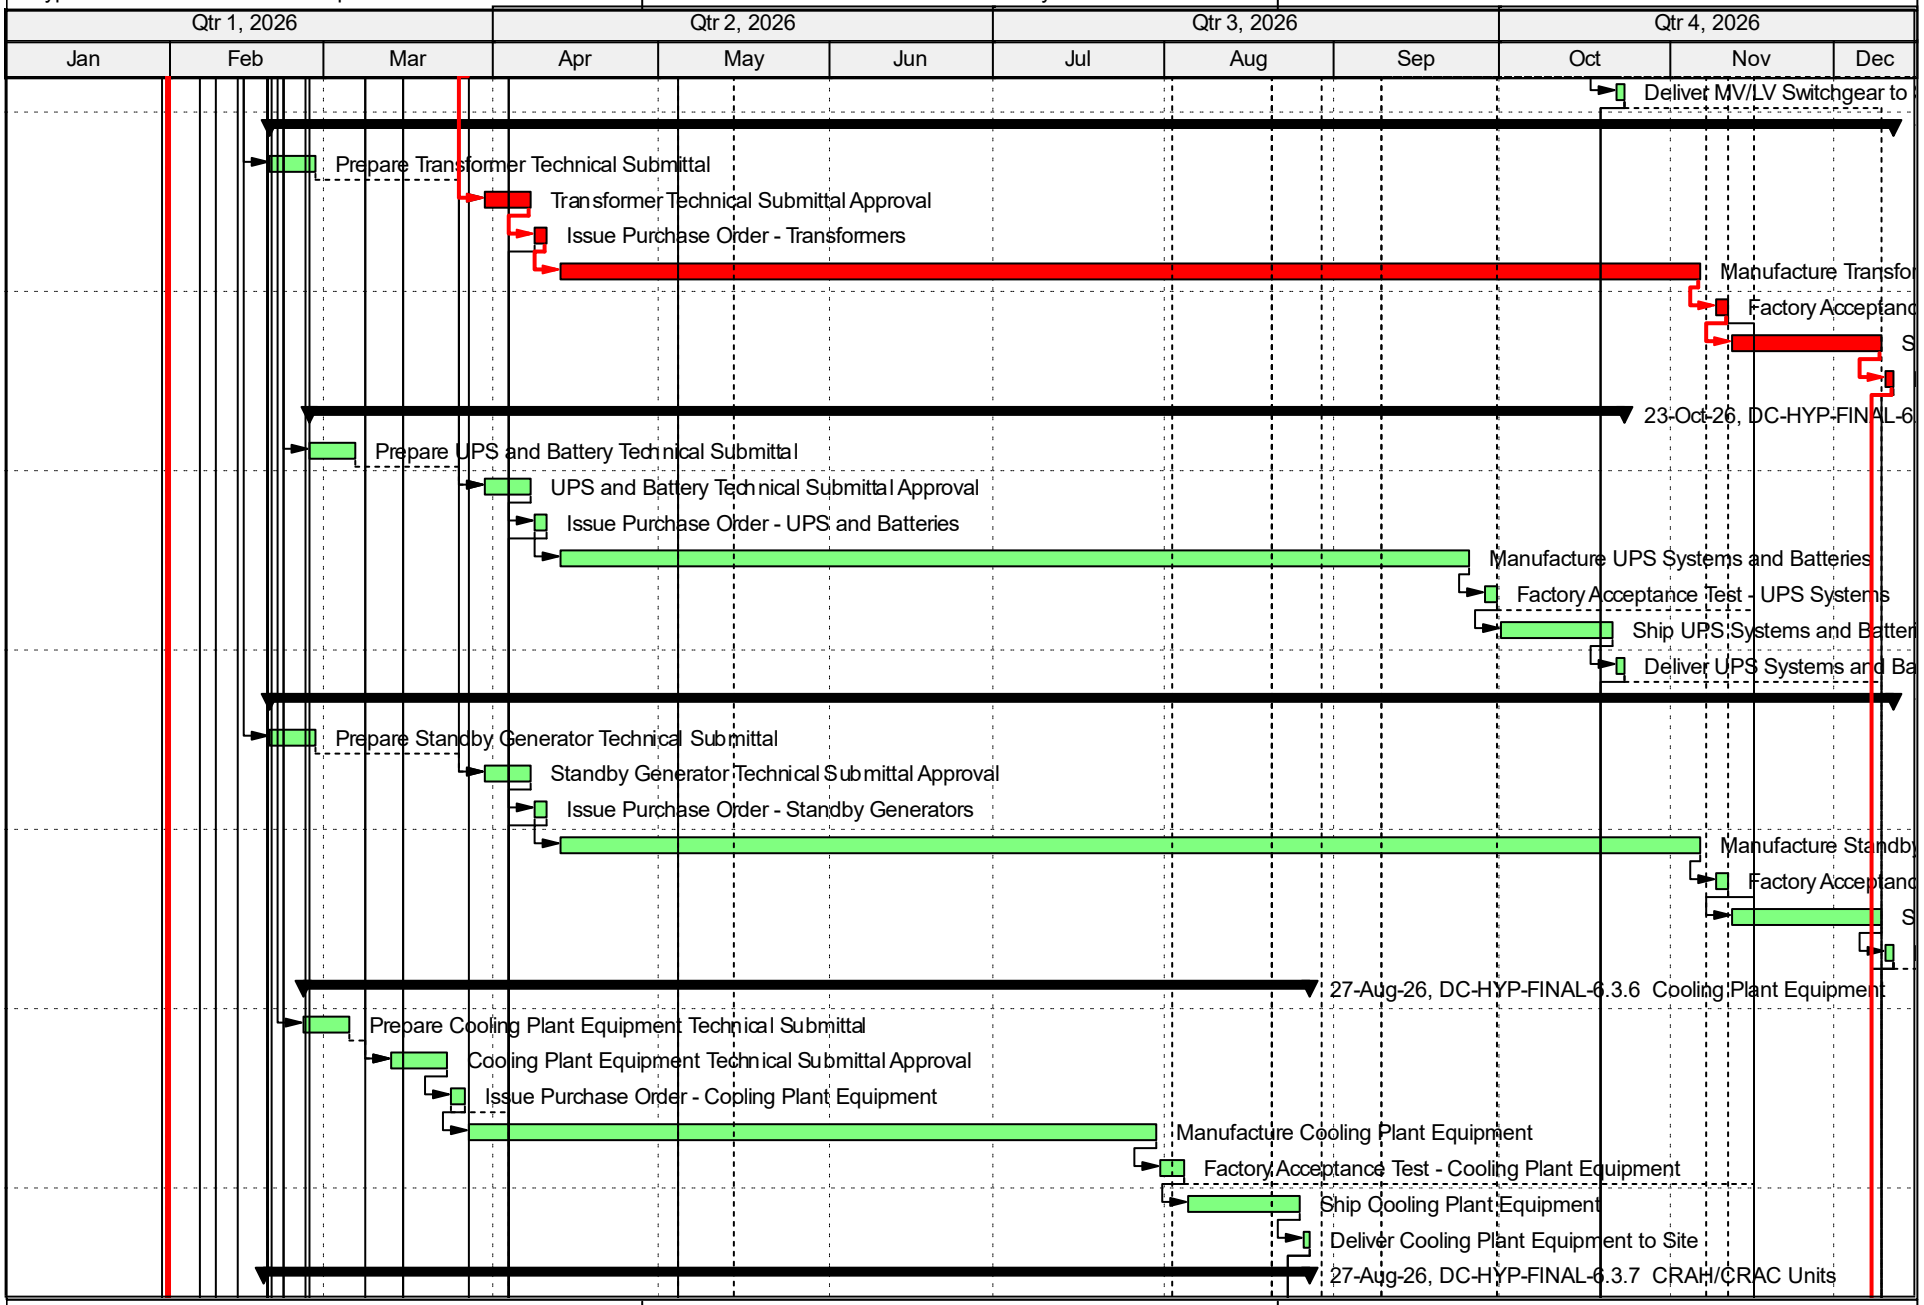

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
CRAH-010	Prepare CRAH/CRAC Tech	7	7	0%	18-Feb-26	26-Feb-26	63		
CRAH-020	CRAH/CRAC Technical Su	7	7	0%	13-Mar-26	23-Mar-26	53		
CRAH-030	Issue Purchase Order - CR	3	3	0%	24-Mar-26	26-Mar-26	53		
CRAH-040	Manufacture CRAH/CRAC	90	90	0%	27-Mar-26	30-Jul-26	53		
CRAH-050	Factory Acceptance Test - C	3	3	0%	31-Jul-26	04-Aug-26	53		
CRAH-060	Ship CRAH/CRAC Units	15	15	0%	05-Aug-26	25-Aug-26	53		
CRAH-070	Deliver CRAH/CRAC Units	2	2	0%	26-Aug-26	27-Aug-26	53		
DC-HYP-FINAL-6.3.8 Fire & Life Safe		90	90	0%	04-Feb-26	09-Jun-26	145		
FLS-P-010	Prepare Fire and Life Safet	5	5	0%	04-Feb-26	10-Feb-26	145		
FLS-P-020	Fire and Life Safety Equipm	7	7	0%	11-Feb-26	19-Feb-26	145		
FLS-P-030	Issue Purchase Order - Fire	3	3	0%	20-Feb-26	24-Feb-26	145		
FLS-P-040	Manufacture Fire and Life S	60	60	0%	25-Feb-26	19-May-26	145		
FLS-P-050	Factory Testing - Fire and Li	3	3	0%	20-May-26	22-May-26	145		
FLS-P-060	Ship Fire and Life Safety Ec	10	10	0%	25-May-26	05-Jun-26	145		
FLS-P-070	Deliver Fire and Life Safety	2	2	0%	08-Jun-26	09-Jun-26	145		
DC-HYP-FINAL-6.3.9 BMS, DCIM & C		92	92	0%	01-Apr-26	06-Aug-26	82		
BMS-P-0	Prepare BMS DCIM and C	5	5	0%	01-Apr-26	07-Apr-26	82		
BMS-P-0	BMS DCIM and Controls E	7	7	0%	08-Apr-26	16-Apr-26	82		
BMS-P-0	Issue Purchase Order - BM	3	3	0%	17-Apr-26	21-Apr-26	82		
BMS-P-0	Configure and Manufacture	60	60	0%	22-Apr-26	14-Jul-26	82		
BMS-P-0	Factory Testing - BMS DCI	5	5	0%	15-Jul-26	21-Jul-26	82		
BMS-P-0	Ship BMS DCIM and Contr	10	10	0%	22-Jul-26	04-Aug-26	82		
BMS-P-0	Deliver BMS DCIM and Co	2	2	0%	05-Aug-26	06-Aug-26	82		
DC-HYP-FINAL-6.3.10 ICT & Security		60	60	0%	24-Feb-26	18-May-26	242		
ICT-P-010	Prepare ICT and Security E	5	5	0%	24-Feb-26	02-Mar-26	242		
ICT-P-020	ICT and Security Equipmer	5	5	0%	03-Mar-26	09-Mar-26	242		
ICT-P-030	Issue Purchase Order - ICT	3	3	0%	10-Mar-26	12-Mar-26	242		
ICT-P-040	Procure ICT and Security E	30	30	0%	13-Mar-26	23-Apr-26	242		
ICT-P-050	Factory Configuration and T	5	5	0%	24-Apr-26	30-Apr-26	242		
ICT-P-060	Ship ICT and Security Equi	10	10	0%	01-May-26	14-May-26	242		
ICT-P-070	Deliver ICT and Security Ec	2	2	0%	15-May-26	18-May-26	242		
DC-HYP-FINAL-6.3.11 Architectural &		63	63	0%	26-Feb-26	25-May-26	94		
ABM-010	Prepare Architectural Materi	5	5	0%	26-Feb-26	04-Mar-26	94		
ABM-020	Architectural Materials Subr	5	5	0%	05-Mar-26	11-Mar-26	94		


© Oracle Corporation

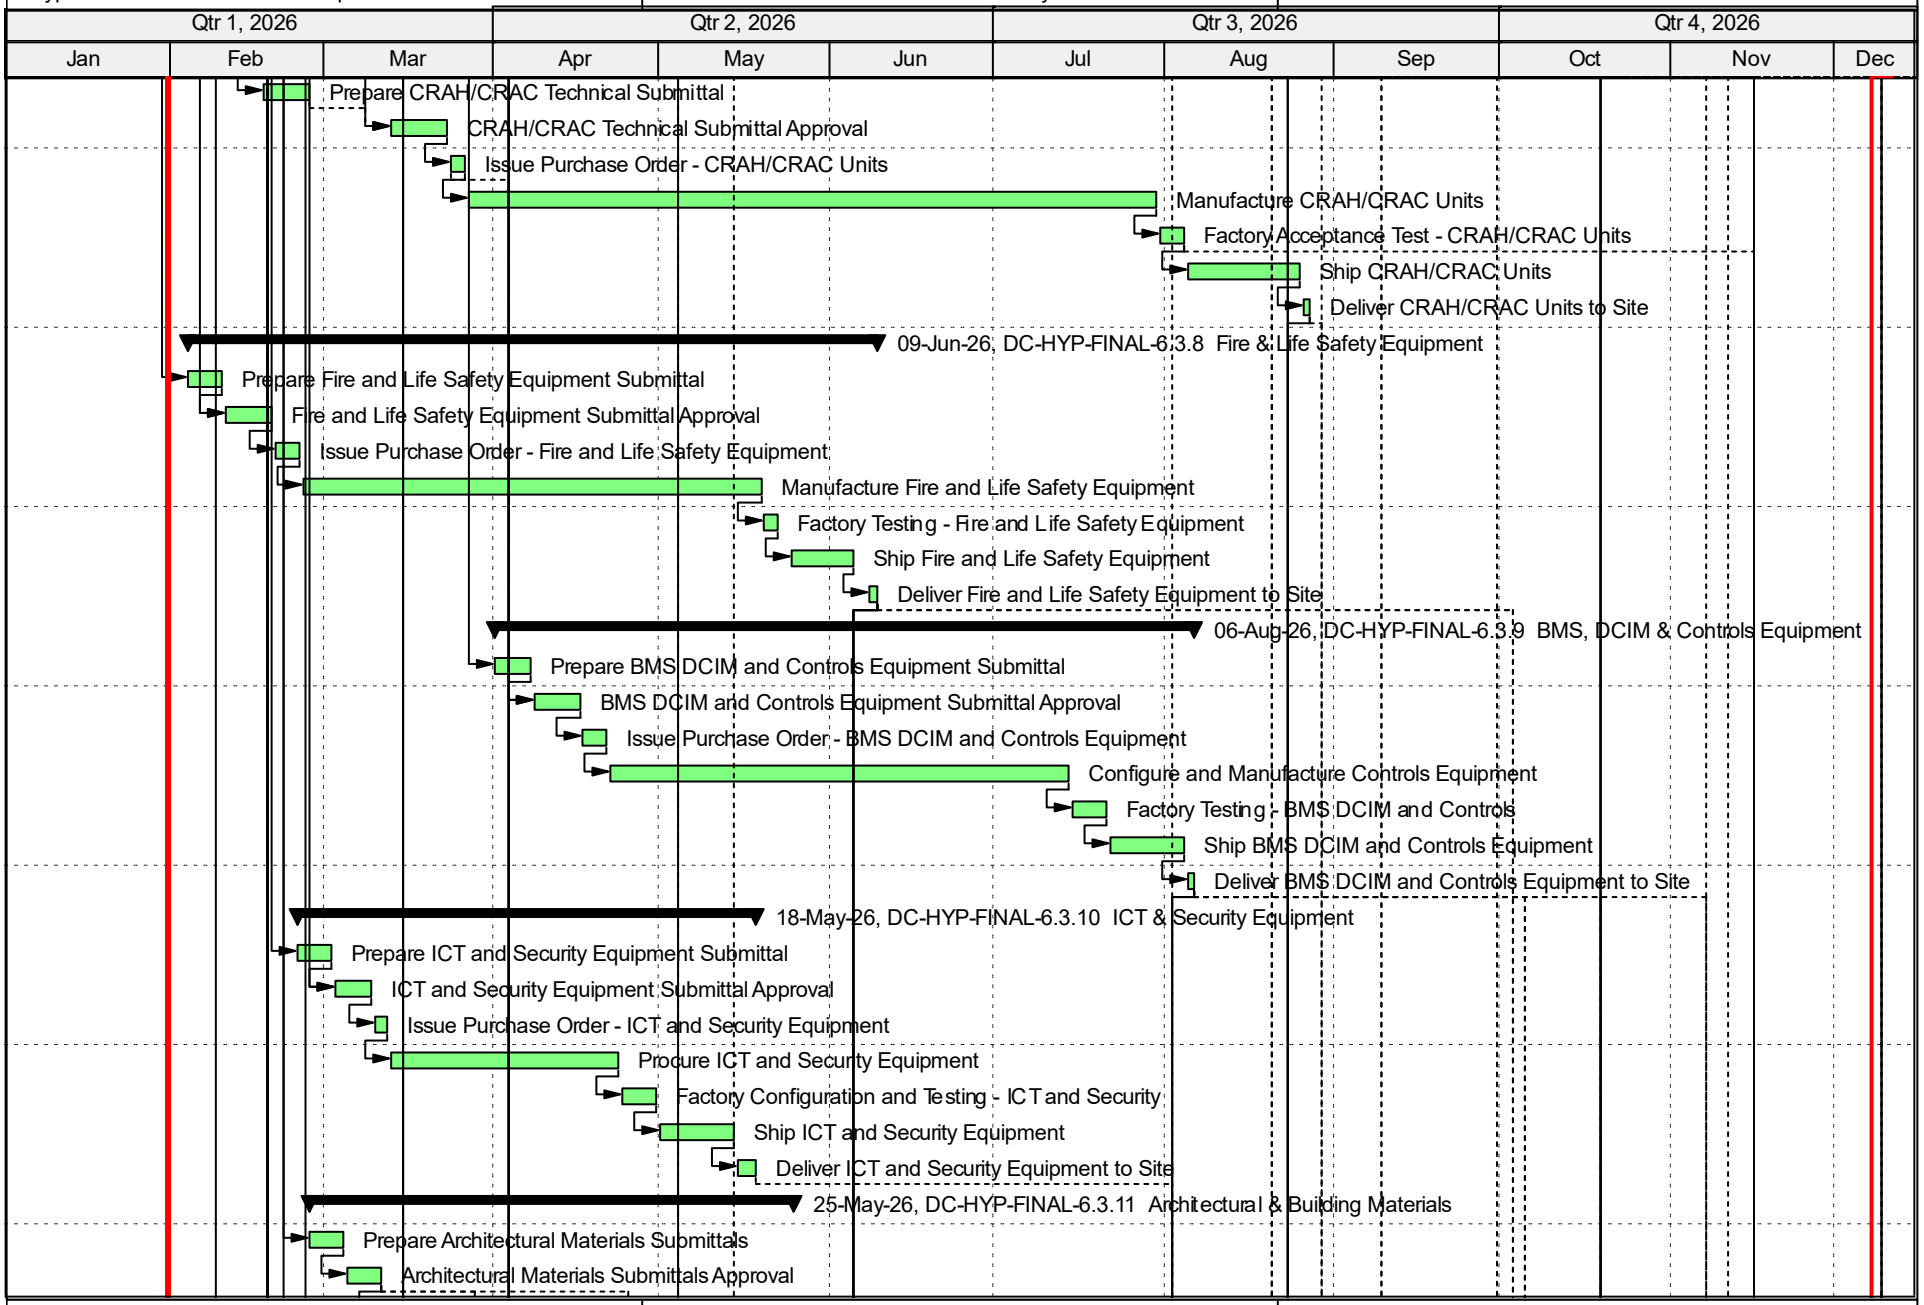

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
ABM-030	Procure Roofing and Water	15	15	0%	12-Mar-26	01-Apr-26	94		
ABM-040	Procure External Cladding I	20	20	0%	02-Apr-26	29-Apr-26	94		
ABM-050	Procure Doors Louvers and	15	15	0%	30-Apr-26	20-May-26	94		
ABM-060	Deliver Architectural Materia	3	3	0%	21-May-26	25-May-26	94		
DC-HYP-FINAL-6.3.12 Long-Lead Eq		183	183	0%	02-Mar-26	11-Nov-26	54		
LLE-010	Identify Long-Lead Equipm	5	5	0%	02-Mar-26	06-Mar-26	127		
LLE-020	Establish Long-Lead Equip	5	5	0%	09-Mar-26	13-Mar-26	127		
LLE-030	Confirm Required-on-Site D	5	5	0%	16-Mar-26	20-Mar-26	127		
LLE-040	Monitor Vendor Engineering	90	90	0%	08-Apr-26	11-Aug-26	115		
LLE-050	Monitor FAT and Shipping F	5	5	0%	12-Aug-26	18-Aug-26	115		
LLE-060	Long-Lead Equipment Deli	0	0	0%		11-Nov-26	54		
DC-HYP-FINAL-6.4 Enabling &		138	104	0%	06-Jan-26	16-Jun-26	271		
DC-HYP-FINAL-6.4.1 Mobilization &		34	0	0%	06-Jan-26	14-Feb-26	32		
MOB-010	Mobilize Project Team to Si	5	0	100%	06-Jan-26	10-Jan-26			
MOB-020	Establish Site Offices and V	5	0	100%	12-Jan-26	16-Jan-26			
MOB-030	Install Temporary Site Fenci	5	0	100%	12-Jan-26	16-Jan-26			
MOB-040	Establish Temporary Storag	5	0	100%	12-Jan-26	16-Jan-26			
MOB-050	Establish Site Security and	5	0	100%	12-Jan-26	16-Jan-26			
MOB-060	Site Mobilization Complete	0	0	0%	14-Feb-26	14-Feb-26	32		
DC-HYP-FINAL-6.4.2 Surveying & Se		13	13	0%	14-Feb-26	02-Mar-26	91		
SUR-010	Establish Survey Control Pc	3	3	0%	14-Feb-26	17-Feb-26	32		
SUR-020	Conduct Existing Site Topo	5	5	0%	18-Feb-26	23-Feb-26	32		
SUR-030	Verify Existing Site Levels a	2	2	0%	24-Feb-26	25-Feb-26	32		
SUR-040	Set Out Main Building Foot	3	3	0%	26-Feb-26	28-Feb-26	91		
SUR-050	Set Out External Infrastruct	3	3	0%	26-Feb-26	28-Feb-26	91		
SUR-060	Survey and Setting Out Co	0	0	0%	02-Mar-26	02-Mar-26	91		
DC-HYP-FINAL-6.4.3 Site Clearance &		27	27	0%	26-Feb-26	30-Mar-26	32		
SCP-010	Clear Existing Vegetation a	7	7	0%	26-Feb-26	05-Mar-26	32		
SCP-020	Remove Existing Surface M	5	5	0%	06-Mar-26	11-Mar-26	32		
SCP-030	Remove or Divert Existing M	7	7	0%	12-Mar-26	19-Mar-26	32		
SCP-040	Strip and Stockpile Topsoil	5	5	0%	20-Mar-26	25-Mar-26	32		
SCP-050	Prepare Site for Earthworks	3	3	0%	26-Mar-26	28-Mar-26	32		
SCP-060	Site Clearance Complete	0	0	0%	30-Mar-26	30-Mar-26	32		


© Oracle Corporation

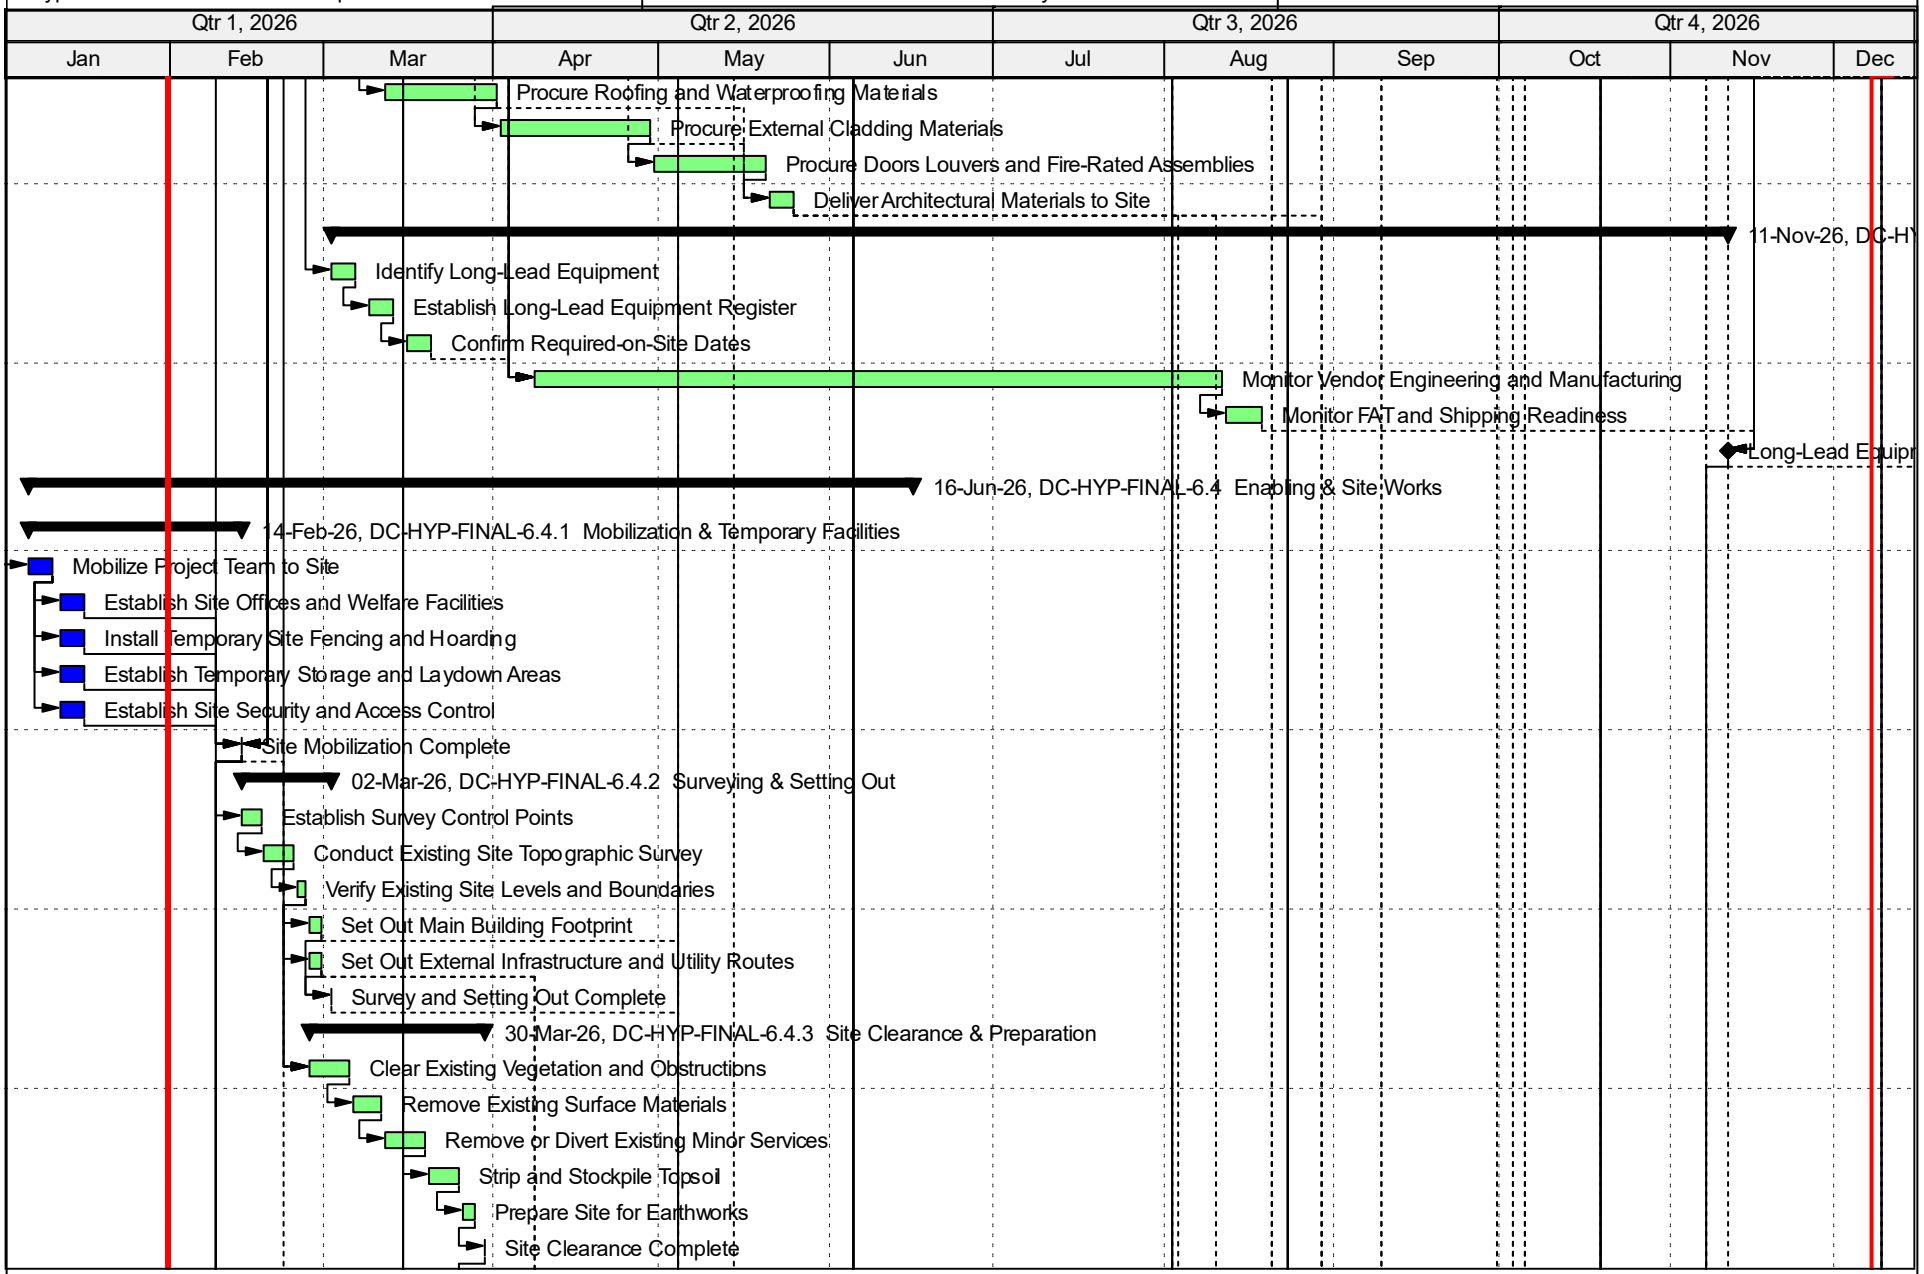

© Oracle Corporation


Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.4.4	Earthworks & E	35	35	0%	30-Mar-26	09-May-26	300		
EW-010	Bulk Excavation	10	10	0%	30-Mar-26	09-Apr-26	32		
EW-020	Excavate Building Formatio	10	10	0%	10-Apr-26	21-Apr-26	32		
EW-030	Excavate Utility and Draina	10	10	0%	01-Apr-26	11-Apr-26	139		
EW-040	Place Engineered Fill	7	7	0%	22-Apr-26	29-Apr-26	32		
EW-050	Compact and Test Formatic	3	3	0%	30-Apr-26	02-May-26	32		
EW-060	Prepare Formation for Four	5	5	0%	04-May-26	08-May-26	32		
EW-070	Earthworks Complete	0	0	0%	09-May-26	09-May-26	300		
DC-HYP-FINAL-6.4.5	Temporary Utilit	5	5	0%	14-Feb-26	20-Feb-26	37		
TU-010	Install Temporary Electrical	5	5	0%	14-Feb-26	19-Feb-26	37		
TU-020	Install Temporary Water Sup	5	5	0%	14-Feb-26	19-Feb-26	37		
TU-030	Install Temporary Drainage	5	5	0%	14-Feb-26	19-Feb-26	37		
TU-040	Install Temporary Site Lighti	5	5	0%	14-Feb-26	19-Feb-26	37		
TU-050	Temporary Site Utilities Ope	0	0	0%	20-Feb-26	20-Feb-26	37		
DC-HYP-FINAL-6.4.6	Underground S	31	31	0%	13-Apr-26	19-May-26	139		
UGU-010	Set Out Underground Utility	3	3	0%	13-Apr-26	15-Apr-26	139		
UGU-020	Excavate Underground Utili	10	10	0%	16-Apr-26	27-Apr-26	139		
UGU-030	Install Underground Electric	10	10	0%	28-Apr-26	08-May-26	139		
UGU-040	Install Underground ICT Du	8	8	0%	28-Apr-26	06-May-26	141		
UGU-050	Install Underground Water	8	8	0%	28-Apr-26	06-May-26	141		
UGU-060	Install Underground Fire Wa	8	8	0%	28-Apr-26	06-May-26	141		
UGU-070	Install Utility Chambers and	8	8	0%	28-Apr-26	06-May-26	141		
UGU-080	Inspect and Test Undergrou	3	3	0%	09-May-26	12-May-26	139		
UGU-090	Backfill and Compact Utility	5	5	0%	13-May-26	18-May-26	139		
UGU-100	Underground Site Utilities C	0	0	0%	19-May-26	19-May-26	139		
DC-HYP-FINAL-6.4.7	Site Roads & Ac	37	37	0%	04-May-26	16-Jun-26	271		
RDA-010	Prepare Site Road Subgrac	5	5	0%	04-May-26	08-May-26	271		
RDA-020	Install Road Subbase and I	7	7	0%	09-May-26	16-May-26	271		
RDA-030	Construct Heavy Equipmer	5	5	0%	18-May-26	22-May-26	271		
RDA-040	Construct Permanent Interr	10	10	0%	23-May-26	03-Jun-26	271		
RDA-050	Construct Kerbs and Hards	7	7	0%	04-Jun-26	11-Jun-26	271		
RDA-060	Complete Final Road Surfa	3	3	0%	12-Jun-26	15-Jun-26	271		
RDA-070	Site Roads and Access Cor	0	0	0%	16-Jun-26	16-Jun-26	271		
DC-HYP-FINAL-6.4.8	External Draina	29	29	0%	13-Apr-26	16-May-26	277		

© Oracle Corporation

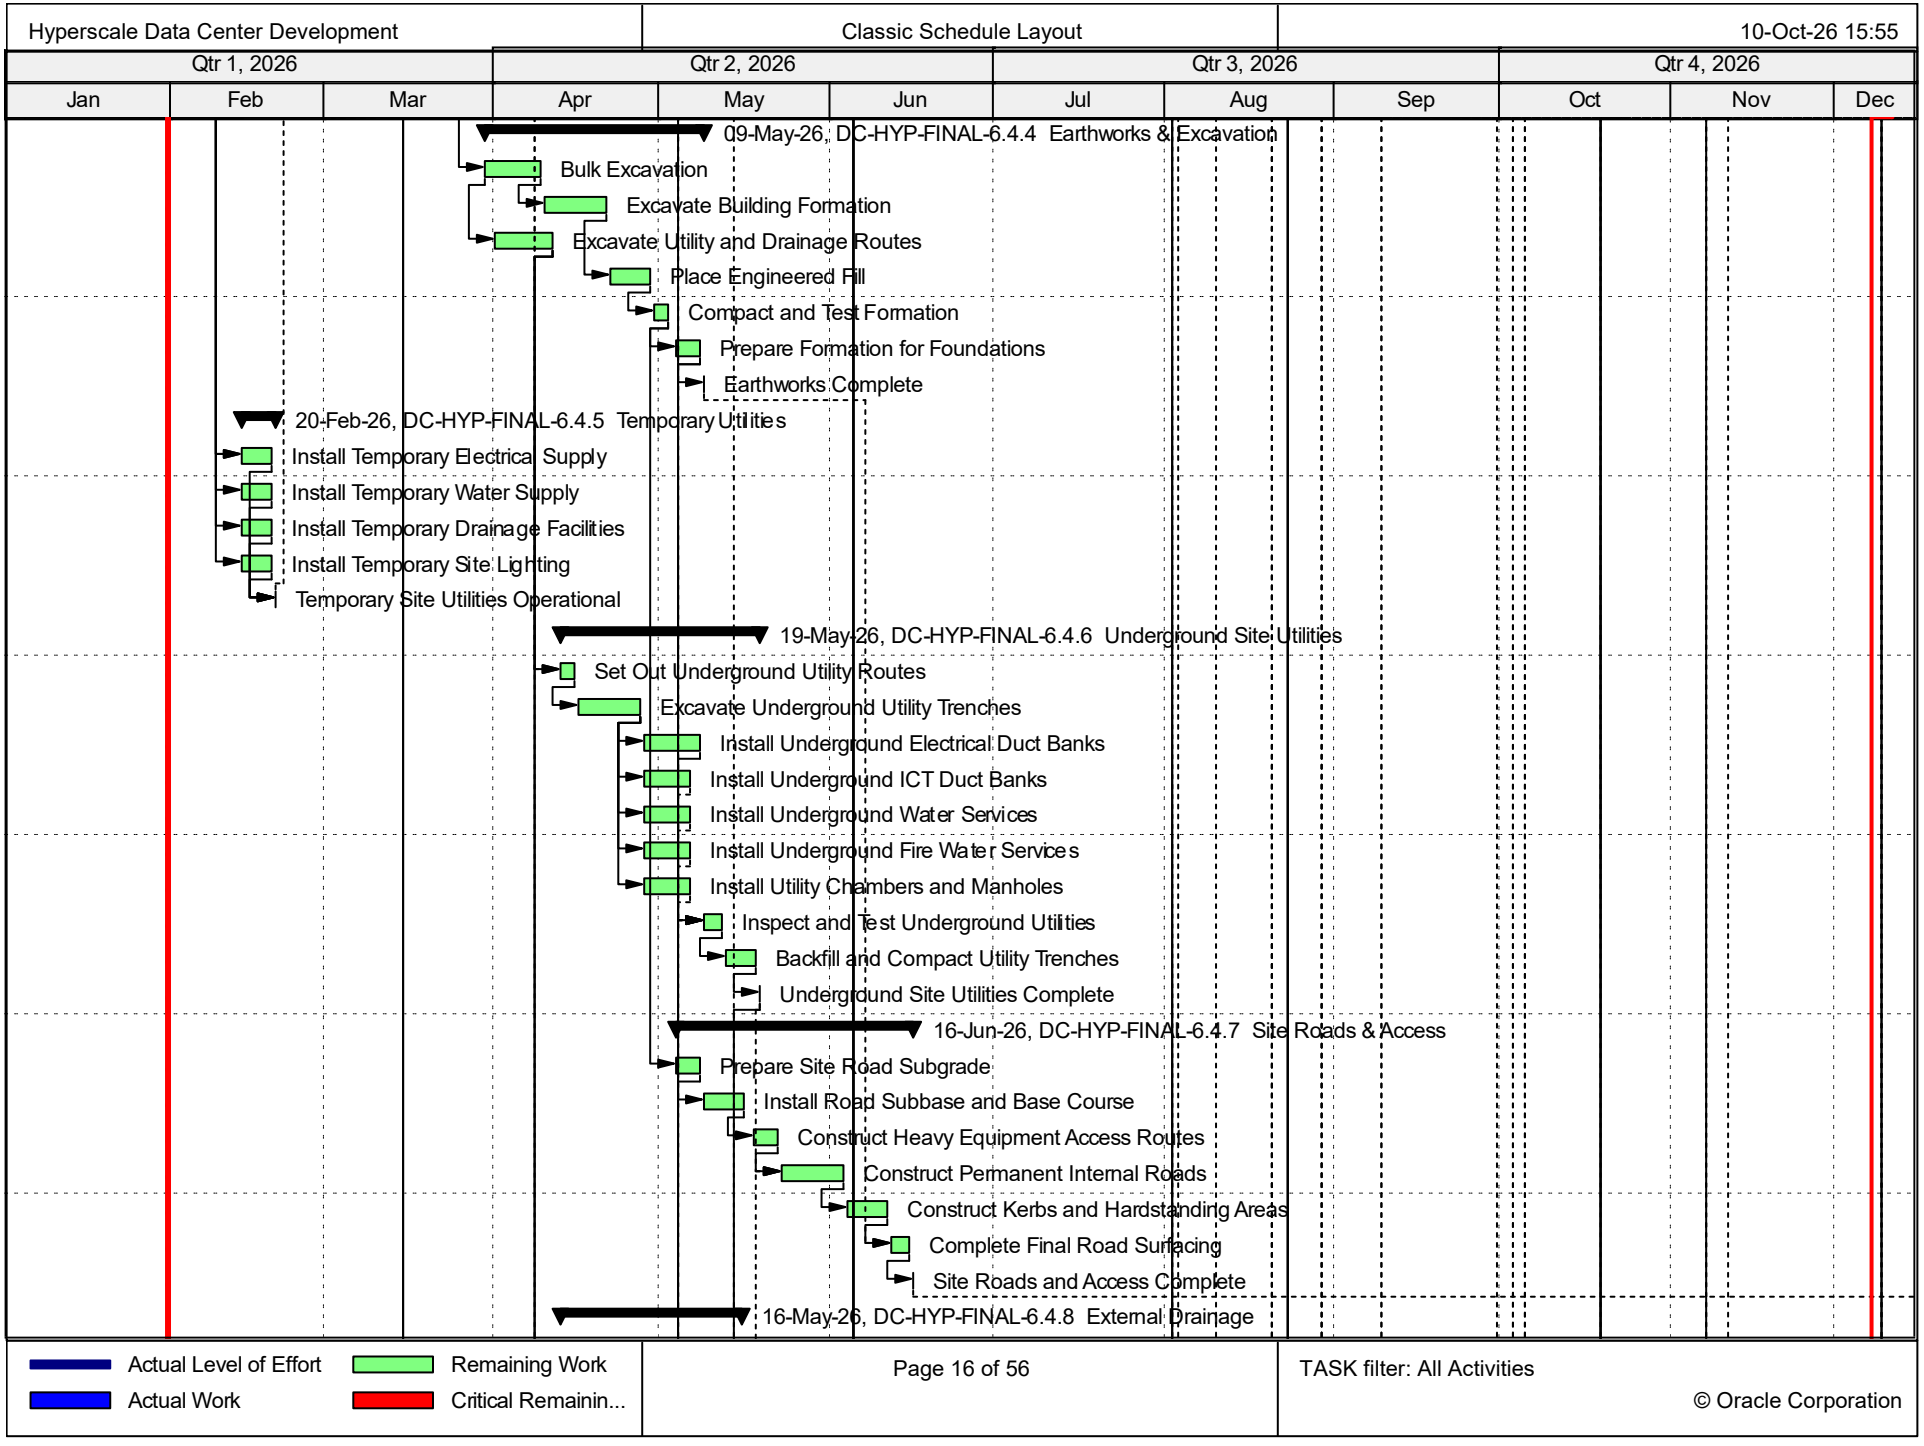
Hyperscale Data Center Development
Classic Schedule Layout
10-Oct-26 15:55
Qtr 1, 2026
Qtr 2, 2026
Qtr 3, 2026
Qtr 4, 2026
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
09-May-26, DC-HYP-FINAL-6.4.4 Earthworks & Excavation
Bulk Excavation
Excavate Building Formation
Excavate Utility and Drainage Routes
Place Engineered Fill
Compact and Test Formation
Prepare Formation for Foundations
Earthworks Complete
20-Feb-26, DC-HYP-FINAL-6.4.5 Temporary Utilities
Install Temporary Electrical Supply
Install Temporary Water Supply
Install Temporary Drainage Facilities
Install Temporary Site Lighting
Temporary Site Utilities Operational
19-May-26, DC-HYP-FINAL-6.4.6 Underground Site Utilities
Set Out Underground Utility Routes
Excavate Underground Utility Trenches
Install Underground Electrical Duct Banks
Install Underground ICT Duct Banks
Install Underground Water Services
Install Underground Fire Water Services
Install Utility Chambers and Manholes
Inspect and Test Underground Utilities
Backfill and Compact Utility Trenches
Underground Site Utilities Complete
16-Jun-26, DC-HYP-FINAL-6.4.7 Site Roads & Access
Prepare Site Road Subgrade
Install Road Subbase and Base Course
Construct Heavy Equipment Access Routes
Construct Permanent Internal Roads
Construct Kerbs and Hardstanding Areas
Complete Final Road Surfacing
Site Roads and Access Complete
16-May-26, DC-HYP-FINAL-6.4.8 External Drainage
Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Page 16 of 56
TASK filter: All Activities
© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DRN-010	Set Out External Drainage I	3	3	0%	13-Apr-26	15-Apr-26	277		
DRN-020	Excavate Drainage Trenche	8	8	0%	16-Apr-26	24-Apr-26	277		
DRN-030	Install Stormwater Drainage	10	10	0%	25-Apr-26	06-May-26	277		
DRN-040	Install Drainage Manholes a	8	8	0%	18-Apr-26	27-Apr-26	285		
DRN-050	Construct Stormwater Mana	10	10	0%	18-Apr-26	29-Apr-26	283		
DRN-060	Test and Inspect External D	3	3	0%	07-May-26	09-May-26	277		
DRN-070	Backfill Drainage Trenches	5	5	0%	11-May-26	15-May-26	277		
DRN-080	External Drainage Complet	0	0	0%	16-May-26	16-May-26	277		
DC-HYP-FINAL-6.5 Civil & Struc		130	130	0%	09-May-26	08-Oct-26	77		
DC-HYP-FINAL-6.5.1 Foundations		66	66	0%	09-May-26	25-Jul-26	32		
FND-010	Set Out Building Foundatio	3	3	0%	09-May-26	12-May-26	32		
FND-020	Excavate Building Foundati	10	10	0%	13-May-26	23-May-26	32		
FND-030	Prepare Foundation Format	5	5	0%	25-May-26	29-May-26	32		
FND-040	Place Blinding Concrete	3	3	0%	30-May-26	02-Jun-26	32		
FND-050	Install Foundation Reinforce	10	10	0%	03-Jun-26	13-Jun-26	32		
FND-060	Install Foundation Formwor	8	8	0%	06-Jun-26	15-Jun-26	32		
FND-070	Install Foundation Embedd	5	5	0%	06-Jun-26	11-Jun-26	35		
FND-080	Cast Foundation Concrete	5	5	0%	16-Jun-26	20-Jun-26	32		
FND-090	Cure Foundation Concrete	7	7	0%	22-Jun-26	29-Jun-26	32		
FND-100	Strip Foundation Formwork	3	3	0%	30-Jun-26	02-Jul-26	32		
FND-110	Backfill Around Foundations	5	5	0%	20-Jul-26	24-Jul-26	32		
FND-120	Building Foundations Comp	0	0	0%	25-Jul-26	25-Jul-26	32		
DC-HYP-FINAL-6.5.2 Ground Floor &		43	43	0%	25-Jul-26	14-Sep-26	42		
SLB-010	Prepare Ground Floor Subg	5	5	0%	25-Jul-26	30-Jul-26	42		
SLB-020	Install Subbase and Compa	5	5	0%	31-Jul-26	05-Aug-26	42		
SLB-030	Install Under-Slab Services	10	10	0%	06-Aug-26	17-Aug-26	42		
SLB-040	Install Damp-Proof Membra	3	3	0%	18-Aug-26	20-Aug-26	42		
SLB-050	Install Ground Floor Reinfo	8	8	0%	21-Aug-26	29-Aug-26	42		
SLB-060	Install Slab Embedded Iten	5	5	0%	25-Aug-26	29-Aug-26	42		
SLB-070	Cast Ground Floor Slab	5	5	0%	31-Aug-26	04-Sep-26	42		
SLB-080	Cure Ground Floor Slab	7	7	0%	05-Sep-26	12-Sep-26	42		
SLB-090	Ground Floor Slab Complet	0	0	0%	14-Sep-26	14-Sep-26	42		
DC-HYP-FINAL-6.5.3 Structural Fram		26	26	0%	25-Jul-26	25-Aug-26	32		

© Oracle Corporation

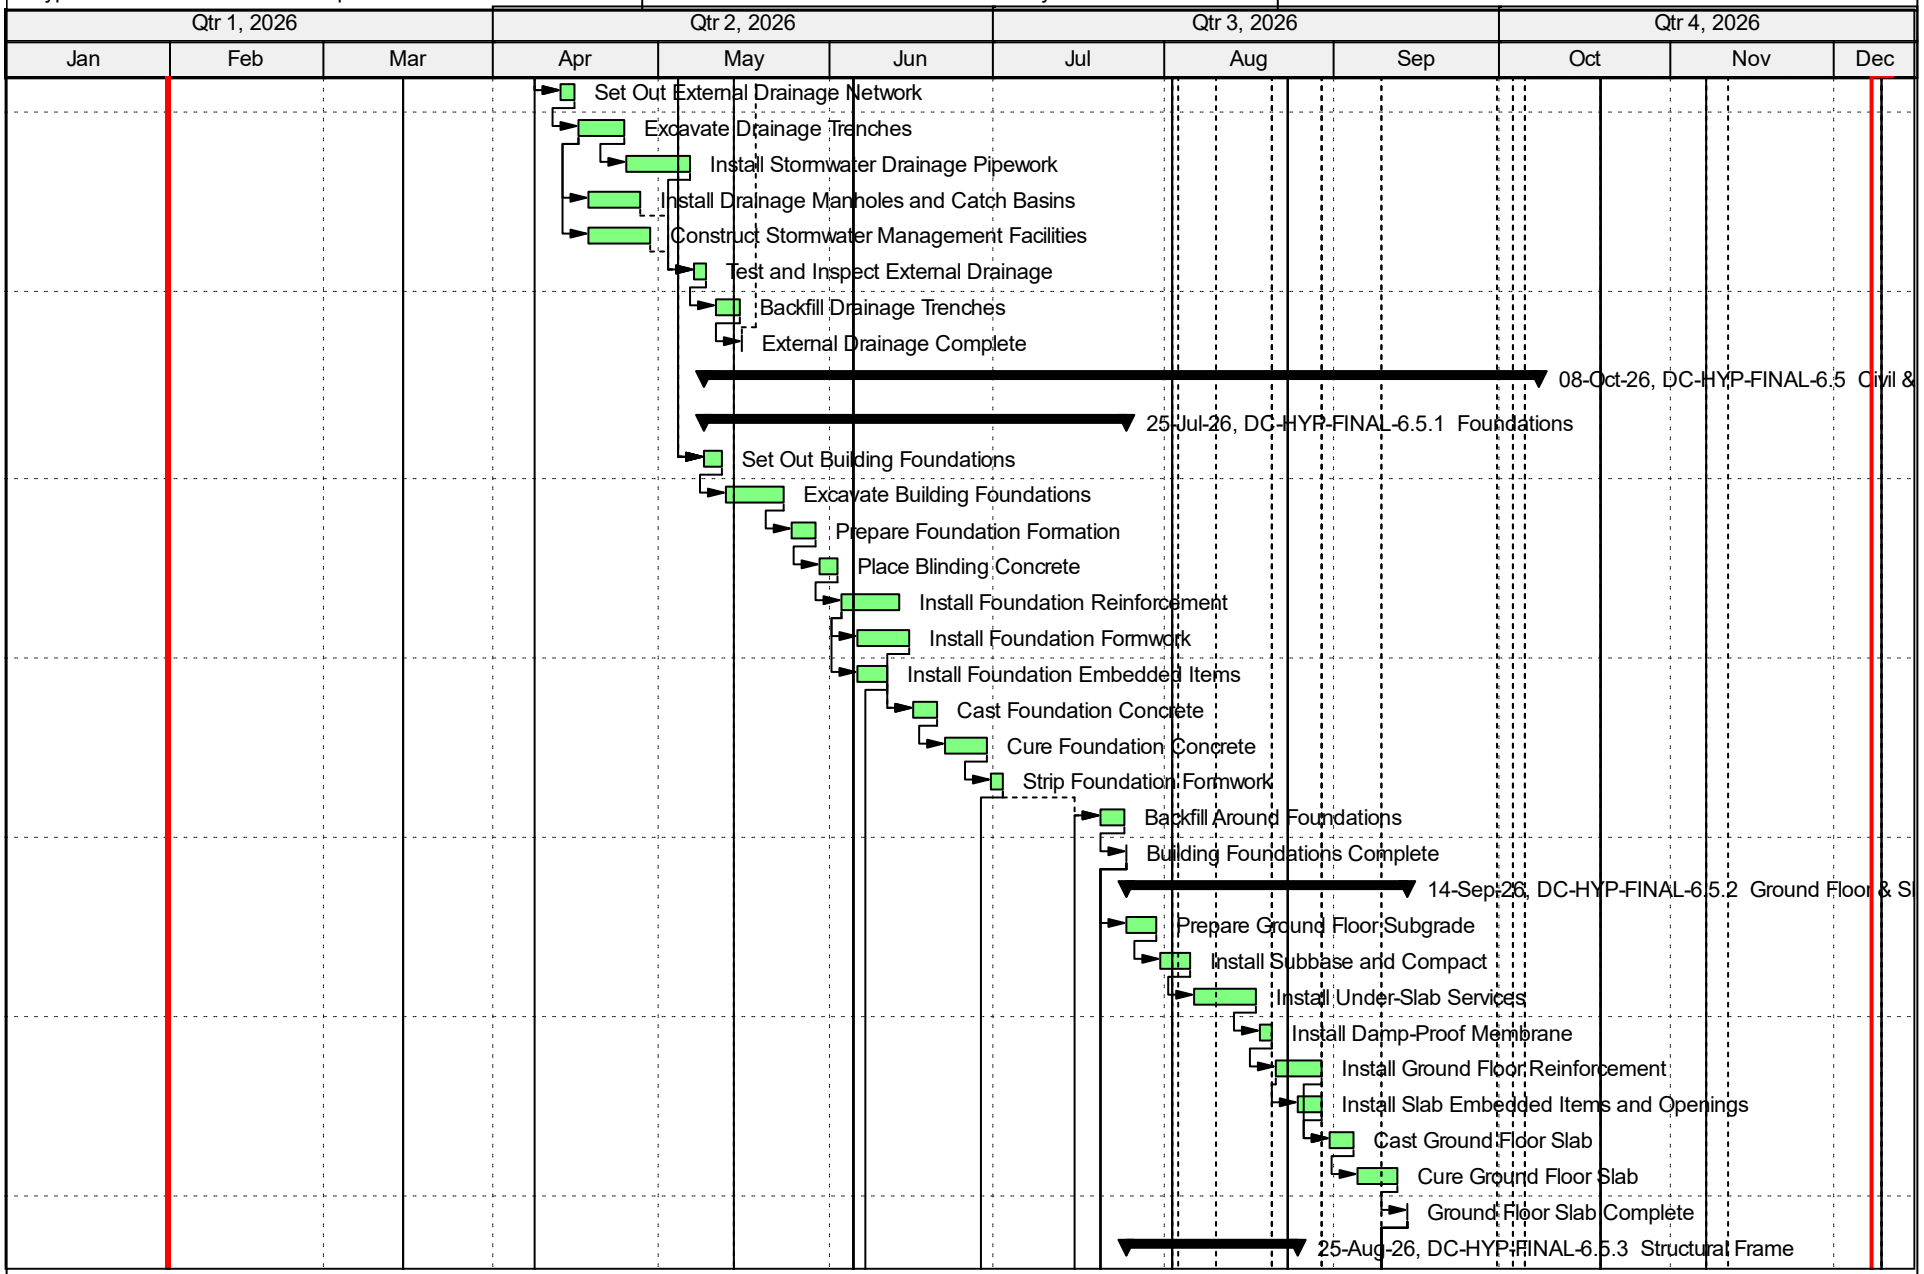


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
STR-010	Mobilize Structural Steel Er	3	3	0%	25-Jul-26	28-Jul-26	32		
STR-020	Erect Primary Structural Col	10	10	0%	29-Jul-26	08-Aug-26	32		
STR-030	Erect Primary Structural Bea	10	10	0%	03-Aug-26	13-Aug-26	32		
STR-040	Install Secondary Structural	8	8	0%	07-Aug-26	15-Aug-26	32		
STR-050	Install Structural Bracing	5	5	0%	07-Aug-26	12-Aug-26	35		
STR-060	Complete Bolting and Conr	4	4	0%	17-Aug-26	20-Aug-26	32		
STR-070	Structural Alignment and In:	3	3	0%	21-Aug-26	24-Aug-26	32		
STR-080	Structural Frame Complete	0	0	0%	25-Aug-26	25-Aug-26	32		
DC-HYP-FINAL-6.5.4 Data Hall Struct		22	22	0%	08-Aug-26	03-Sep-26	59		
DHS-010	Construct Data Hall Structu	15	15	0%	08-Aug-26	25-Aug-26	59		
DHS-020	Install Data Hall Floor Struc	8	8	0%	14-Aug-26	22-Aug-26	61		
DHS-030	Install Data Hall Roof Supp	8	8	0%	17-Aug-26	25-Aug-26	59		
DHS-040	Install Data Hall Equipment	5	5	0%	17-Aug-26	21-Aug-26	62		
DHS-050	Complete Data Hall Structu	4	4	0%	26-Aug-26	29-Aug-26	59		
DHS-060	Inspect Data Hall Structure	3	3	0%	31-Aug-26	02-Sep-26	59		
DHS-070	Data Hall Structure Comple	0	0	0%	03-Sep-26	03-Sep-26	59		
DC-HYP-FINAL-6.5.5 Electrical & UPS		18	18	0%	14-Sep-26	05-Oct-26	42		
EUS-010	Construct Electrical Room S	10	10	0%	14-Sep-26	24-Sep-26	42		
EUS-020	Construct UPS and Battery	10	10	0%	14-Sep-26	24-Sep-26	42		
EUS-030	Construct MV and LV Switc	10	10	0%	14-Sep-26	24-Sep-26	42		
EUS-040	Construct Transformer Roo	10	10	0%	14-Sep-26	24-Sep-26	42		
EUS-050	Install Equipment Support S	5	5	0%	25-Sep-26	30-Sep-26	42		
EUS-060	Complete Equipment Acces	3	3	0%	01-Oct-26	03-Oct-26	42		
EUS-070	Electrical and UPS Rooms	0	0	0%	05-Oct-26	05-Oct-26	42		
DC-HYP-FINAL-6.5.6 Generator & Uti		23	23	0%	25-Jul-26	21-Aug-26	118		
GUS-010	Construct Generator Found	10	10	0%	25-Jul-26	05-Aug-26	118		
GUS-020	Construct Generator Suppc	8	8	0%	06-Aug-26	14-Aug-26	118		
GUS-030	Construct Utility and MV St	8	8	0%	06-Aug-26	14-Aug-26	123		
GUS-040	Construct Fuel System Stru	5	5	0%	06-Aug-26	11-Aug-26	121		
GUS-050	Install Generator Equipmen	5	5	0%	15-Aug-26	20-Aug-26	118		
GUS-060	Generator and Utility Struct	0	0	0%	21-Aug-26	21-Aug-26	118		
DC-HYP-FINAL-6.5.7 Cooling Plant S		26	26	0%	25-Jul-26	25-Aug-26	44		
CPS-010	Construct Cooling Plant Fo	10	10	0%	25-Jul-26	05-Aug-26	44		
CPS-020	Construct Chiller Equipmen	5	5	0%	06-Aug-26	11-Aug-26	55		

© Oracle Corporation

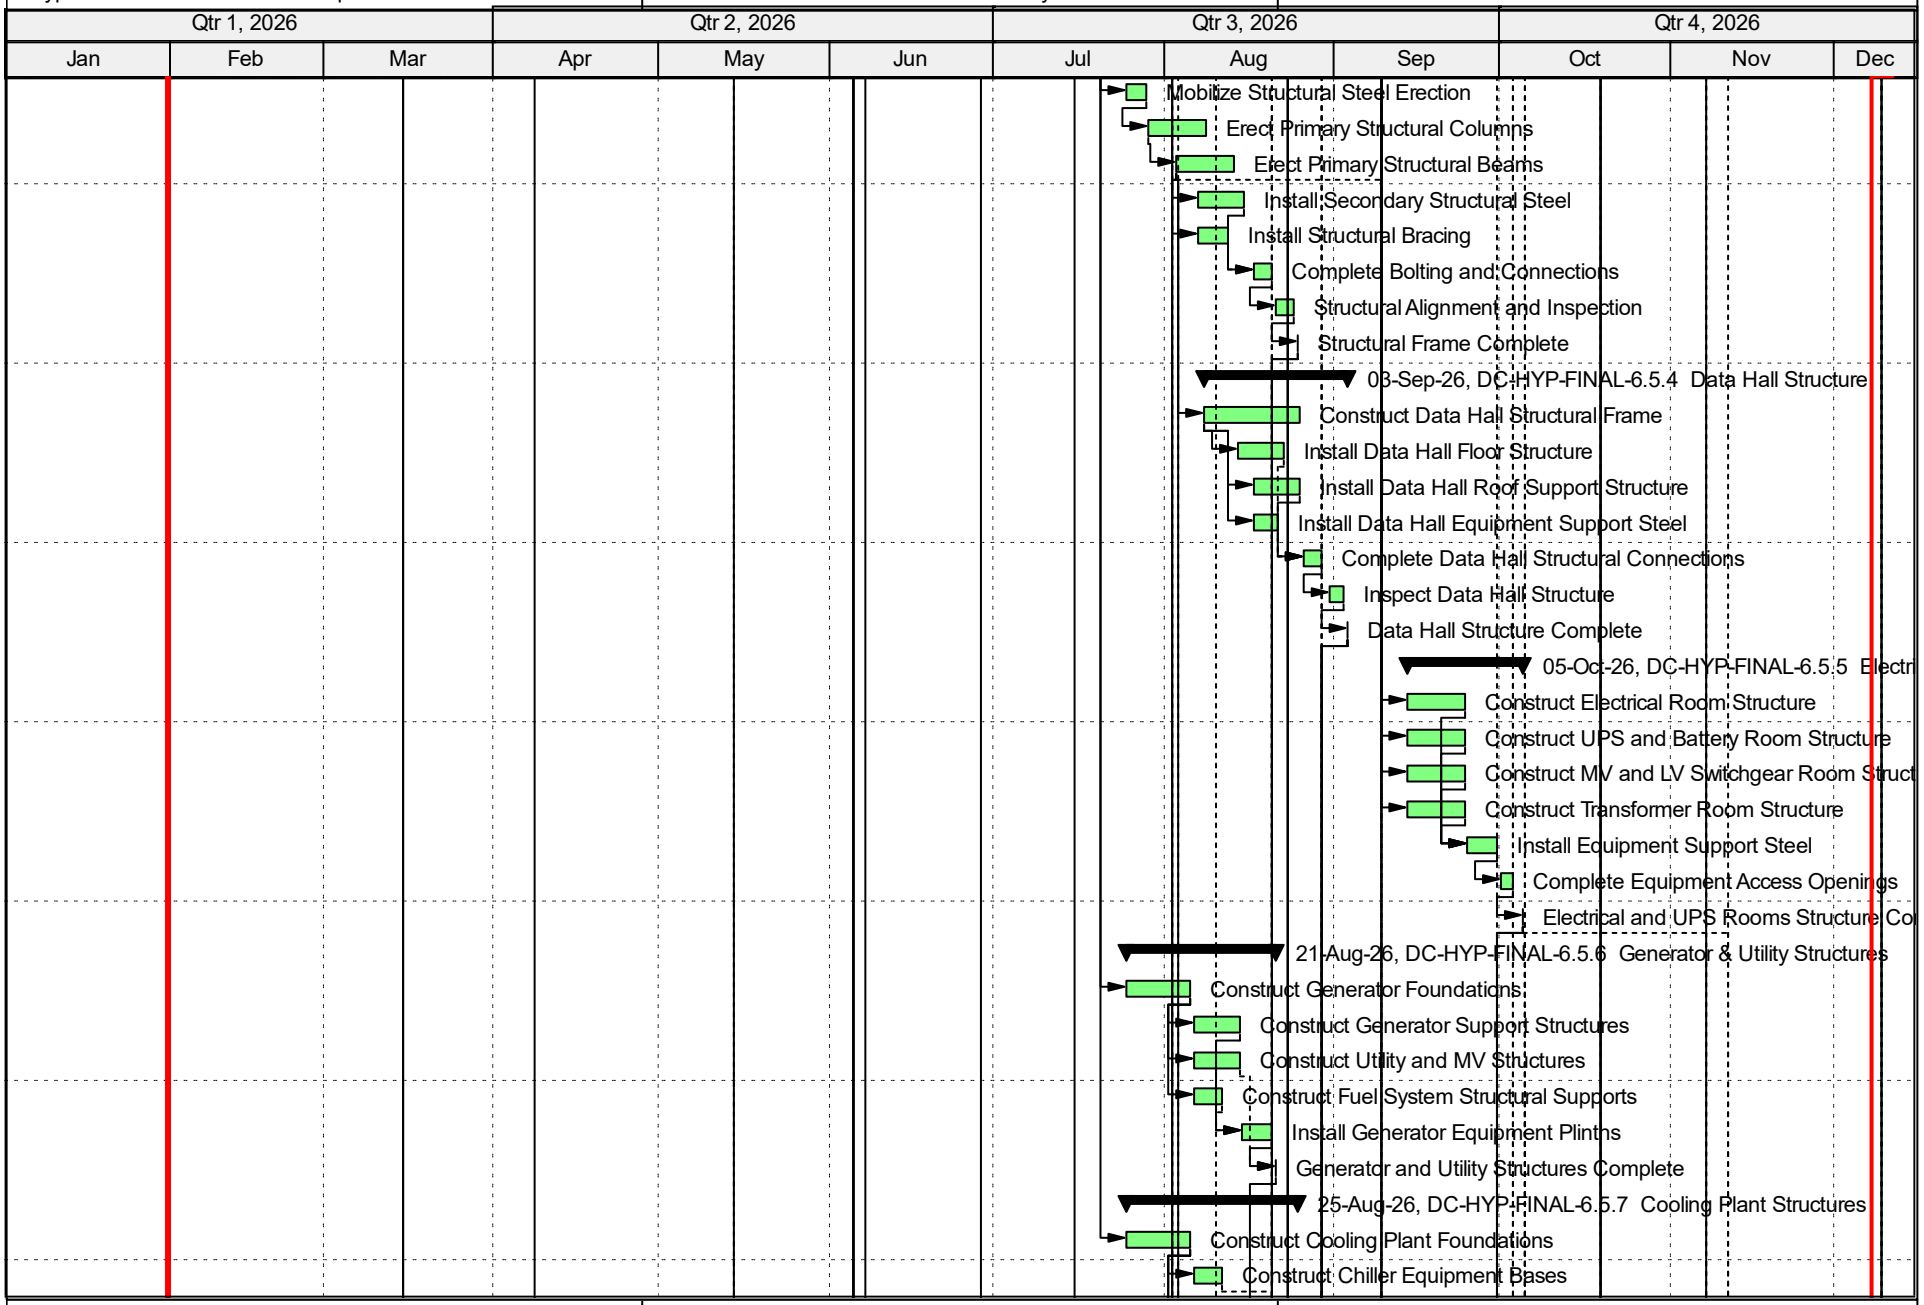


Actual Level of Effort | Remaining Work
Actual Work | Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
CPS-030	Construct Pump Equipmen	5	5	0%	06-Aug-26	11-Aug-26	55		
CPS-040	Construct Cooling Plant Str	8	8	0%	06-Aug-26	14-Aug-26	44		
CPS-050	Install Pipework Support Str	8	8	0%	15-Aug-26	24-Aug-26	44		
CPS-060	Cooling Plant Structures Cc	0	0	0%	25-Aug-26	25-Aug-26	44		
DC-HYP-FINAL-6.5.8 Roof Structure		8	8	0%	25-Aug-26	03-Sep-26	32		
RFS-050	Complete Roof Structural C	5	5	0%	25-Aug-26	29-Aug-26	32		
RFS-060	Inspect Roof Structure	3	3	0%	31-Aug-26	02-Sep-26	32		
RFS-070	Roof Structure Complete	0	0	0%	03-Sep-26	03-Sep-26	32		
DC-HYP-FINAL-6.5.9 Equipment Plin		21	21	0%	14-Sep-26	08-Oct-26	55		
EPF-010	Confirm Equipment Founda	5	5	0%	14-Sep-26	18-Sep-26	55		
EPF-020	Set Out Equipment Founda	3	3	0%	19-Sep-26	22-Sep-26	55		
EPF-030	Construct Transformer Plint	5	5	0%	23-Sep-26	28-Sep-26	55		
EPF-040	Construct Switchgear and U	5	5	0%	23-Sep-26	28-Sep-26	55		
EPF-050	Construct Generator Equipr	5	5	0%	23-Sep-26	28-Sep-26	55		
EPF-060	Construct Cooling Equipme	5	5	0%	23-Sep-26	28-Sep-26	55		
EPF-070	Install Equipment Anchor B	5	5	0%	29-Sep-26	03-Oct-26	55		
EPF-080	Inspect Equipment Founda	3	3	0%	05-Oct-26	07-Oct-26	55		
EPF-090	Equipment Foundations Re	0	0	0%	08-Oct-26	08-Oct-26	55		
DC-HYP-FINAL-6.6 Building En		85	85	0%	03-Jul-26	10-Oct-26	65		
DC-HYP-FINAL-6.6.1 External Walls &		26	26	0%	08-Aug-26	08-Sep-26	48		
CLD-010	Set Out External Wall and C	3	3	0%	08-Aug-26	11-Aug-26	48		
CLD-020	Install External Wall Framin	10	10	0%	12-Aug-26	22-Aug-26	48		
CLD-030	Install External Wall Insulati	8	8	0%	15-Aug-26	24-Aug-26	48		
CLD-040	Install External Cladding Pa	12	12	0%	19-Aug-26	01-Sep-26	48		
CLD-050	Install Flashings and Interfa	5	5	0%	27-Aug-26	01-Sep-26	48		
CLD-060	Complete Cladding Joint Se	3	3	0%	02-Sep-26	04-Sep-26	48		
CLD-070	Inspect External Walls and	2	2	0%	05-Sep-26	07-Sep-26	48		
CLD-080	External Walls and Cladding	0	0	0%	08-Sep-26	08-Sep-26	48		
DC-HYP-FINAL-6.6.2 Roofing Systen		20	20	0%	03-Sep-26	26-Sep-26	32		
ROF-010	Prepare Roof Deck for Roo	3	3	0%	03-Sep-26	05-Sep-26	32		
ROF-020	Install Roof Vapour Control	5	5	0%	07-Sep-26	11-Sep-26	32		
ROF-030	Install Roof Insulation	5	5	0%	09-Sep-26	14-Sep-26	32		
ROF-040	Install Roofing Membrane	8	8	0%	11-Sep-26	19-Sep-26	32		

© Oracle Corporation

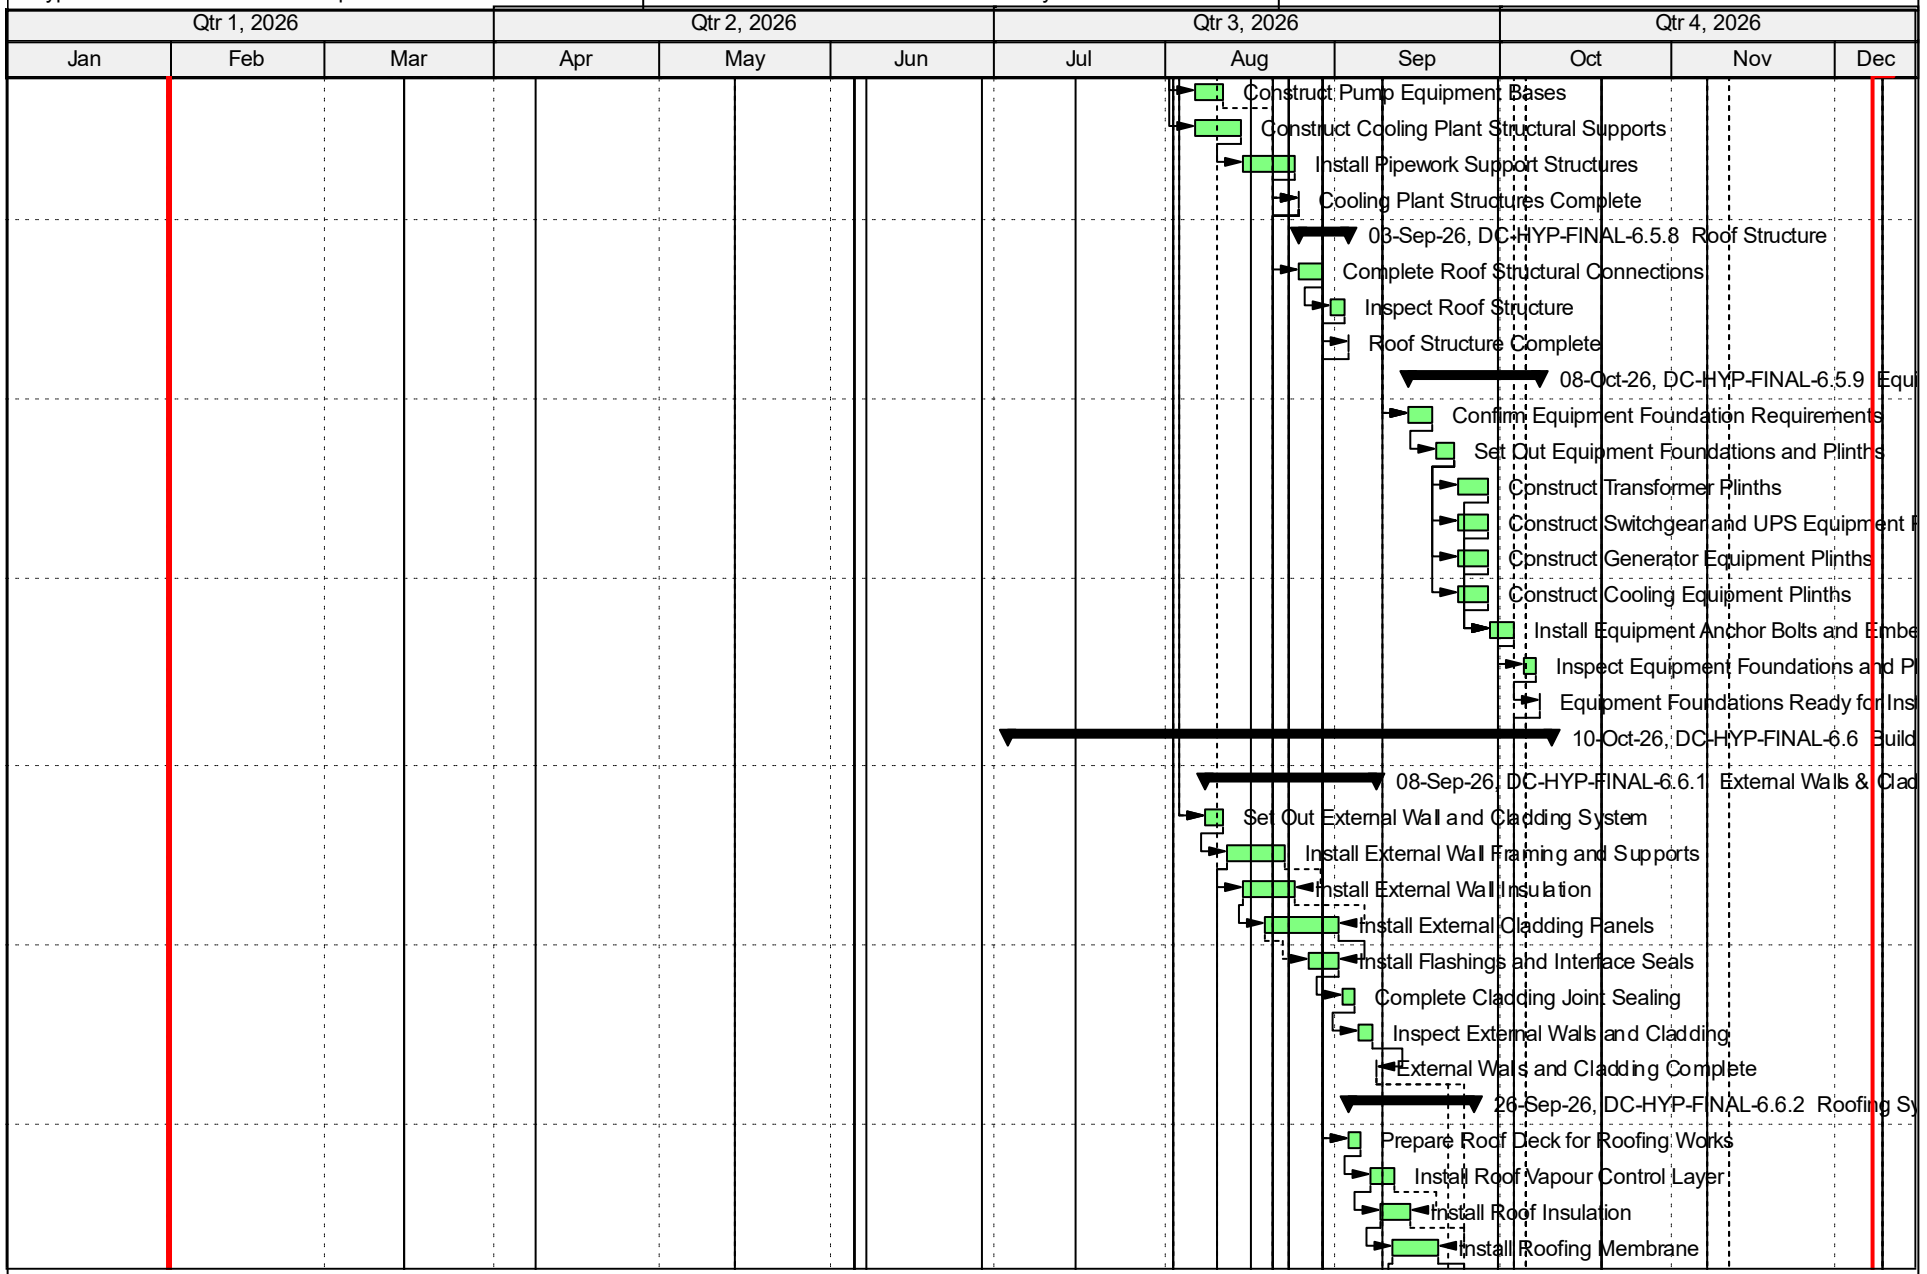


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
ROF-050	Install Roof Flashings and U	5	5	0%	15-Sep-26	19-Sep-26	32		
ROF-060	Seal Roof Equipment Pene	3	3	0%	21-Sep-26	23-Sep-26	32		
ROF-070	Inspect and Test Roofing S	2	2	0%	24-Sep-26	25-Sep-26	32		
ROF-080	Roofing System Complete	0	0	0%	26-Sep-26	26-Sep-26	32		
DC-HYP-FINAL-6.6.3 Waterproofing		14	14	0%	03-Jul-26	20-Jul-26	32		
WPF-010	Prepare Surfaces for Water	2	2	0%	03-Jul-26	04-Jul-26	32		
WPF-020	Apply Foundation Waterpro	5	5	0%	06-Jul-26	10-Jul-26	32		
WPF-030	Apply Below-Grade Wall Wa	5	5	0%	08-Jul-26	13-Jul-26	32		
WPF-040	Waterproof Service Penetra	3	3	0%	10-Jul-26	13-Jul-26	32		
WPF-050	Install Waterproofing Protec	3	3	0%	14-Jul-26	16-Jul-26	32		
WPF-060	Inspect and Test Waterproo	2	2	0%	17-Jul-26	18-Jul-26	32		
WPF-070	Waterproofing Complete	0	0	0%	20-Jul-26	20-Jul-26	32		
DC-HYP-FINAL-6.6.4 External Doors		19	19	0%	15-Aug-26	07-Sep-26	49		
EDL-010	Prepare External Door and	3	3	0%	15-Aug-26	18-Aug-26	49		
EDL-020	Install External Door Frame	5	5	0%	19-Aug-26	24-Aug-26	49		
EDL-030	Install External Doors	5	5	0%	21-Aug-26	26-Aug-26	49		
EDL-040	Install External Louvers	5	5	0%	21-Aug-26	26-Aug-26	53		
EDL-050	Install Door Hardware and S	4	4	0%	27-Aug-26	31-Aug-26	49		
EDL-060	Seal Door and Louver Inter	3	3	0%	01-Sep-26	03-Sep-26	49		
EDL-070	Inspect External Doors and	2	2	0%	04-Sep-26	05-Sep-26	49		
EDL-080	External Doors and Louvers	0	0	0%	07-Sep-26	07-Sep-26	49		
DC-HYP-FINAL-6.6.5 Internal Partitio		21	21	0%	14-Sep-26	08-Oct-26	67		
PAR-010	Set Out Internal Partitions	4	4	0%	14-Sep-26	17-Sep-26	67		
PAR-020	Install Internal Partition Frar	8	8	0%	18-Sep-26	26-Sep-26	67		
PAR-030	Install Fire-Rated Wall Syste	6	6	0%	22-Sep-26	28-Sep-26	67		
PAR-040	Construct Electrical Room F	8	8	0%	24-Sep-26	02-Oct-26	69		
PAR-050	Construct UPS and Battery	8	8	0%	24-Sep-26	02-Oct-26	69		
PAR-060	Construct Data Hall Fire-Ra	10	10	0%	24-Sep-26	05-Oct-26	67		
PAR-070	Install Fire-Stopping at Serv	5	5	0%	30-Sep-26	05-Oct-26	67		
PAR-080	Inspect Fire-Rated Partition	2	2	0%	06-Oct-26	07-Oct-26	67		
PAR-090	Internal Partitions and Fire-I	0	0	0%	08-Oct-26	08-Oct-26	67		
DC-HYP-FINAL-6.6.6 Weather-Tightn		12	12	0%	26-Sep-26	10-Oct-26	32		
ENV-010	Inspect Building Envelope I	2	2	0%	26-Sep-26	28-Sep-26	32		
ENV-020	Perform Roof Water-Tightne	3	3	0%	29-Sep-26	01-Oct-26	32		

© Oracle Corporation

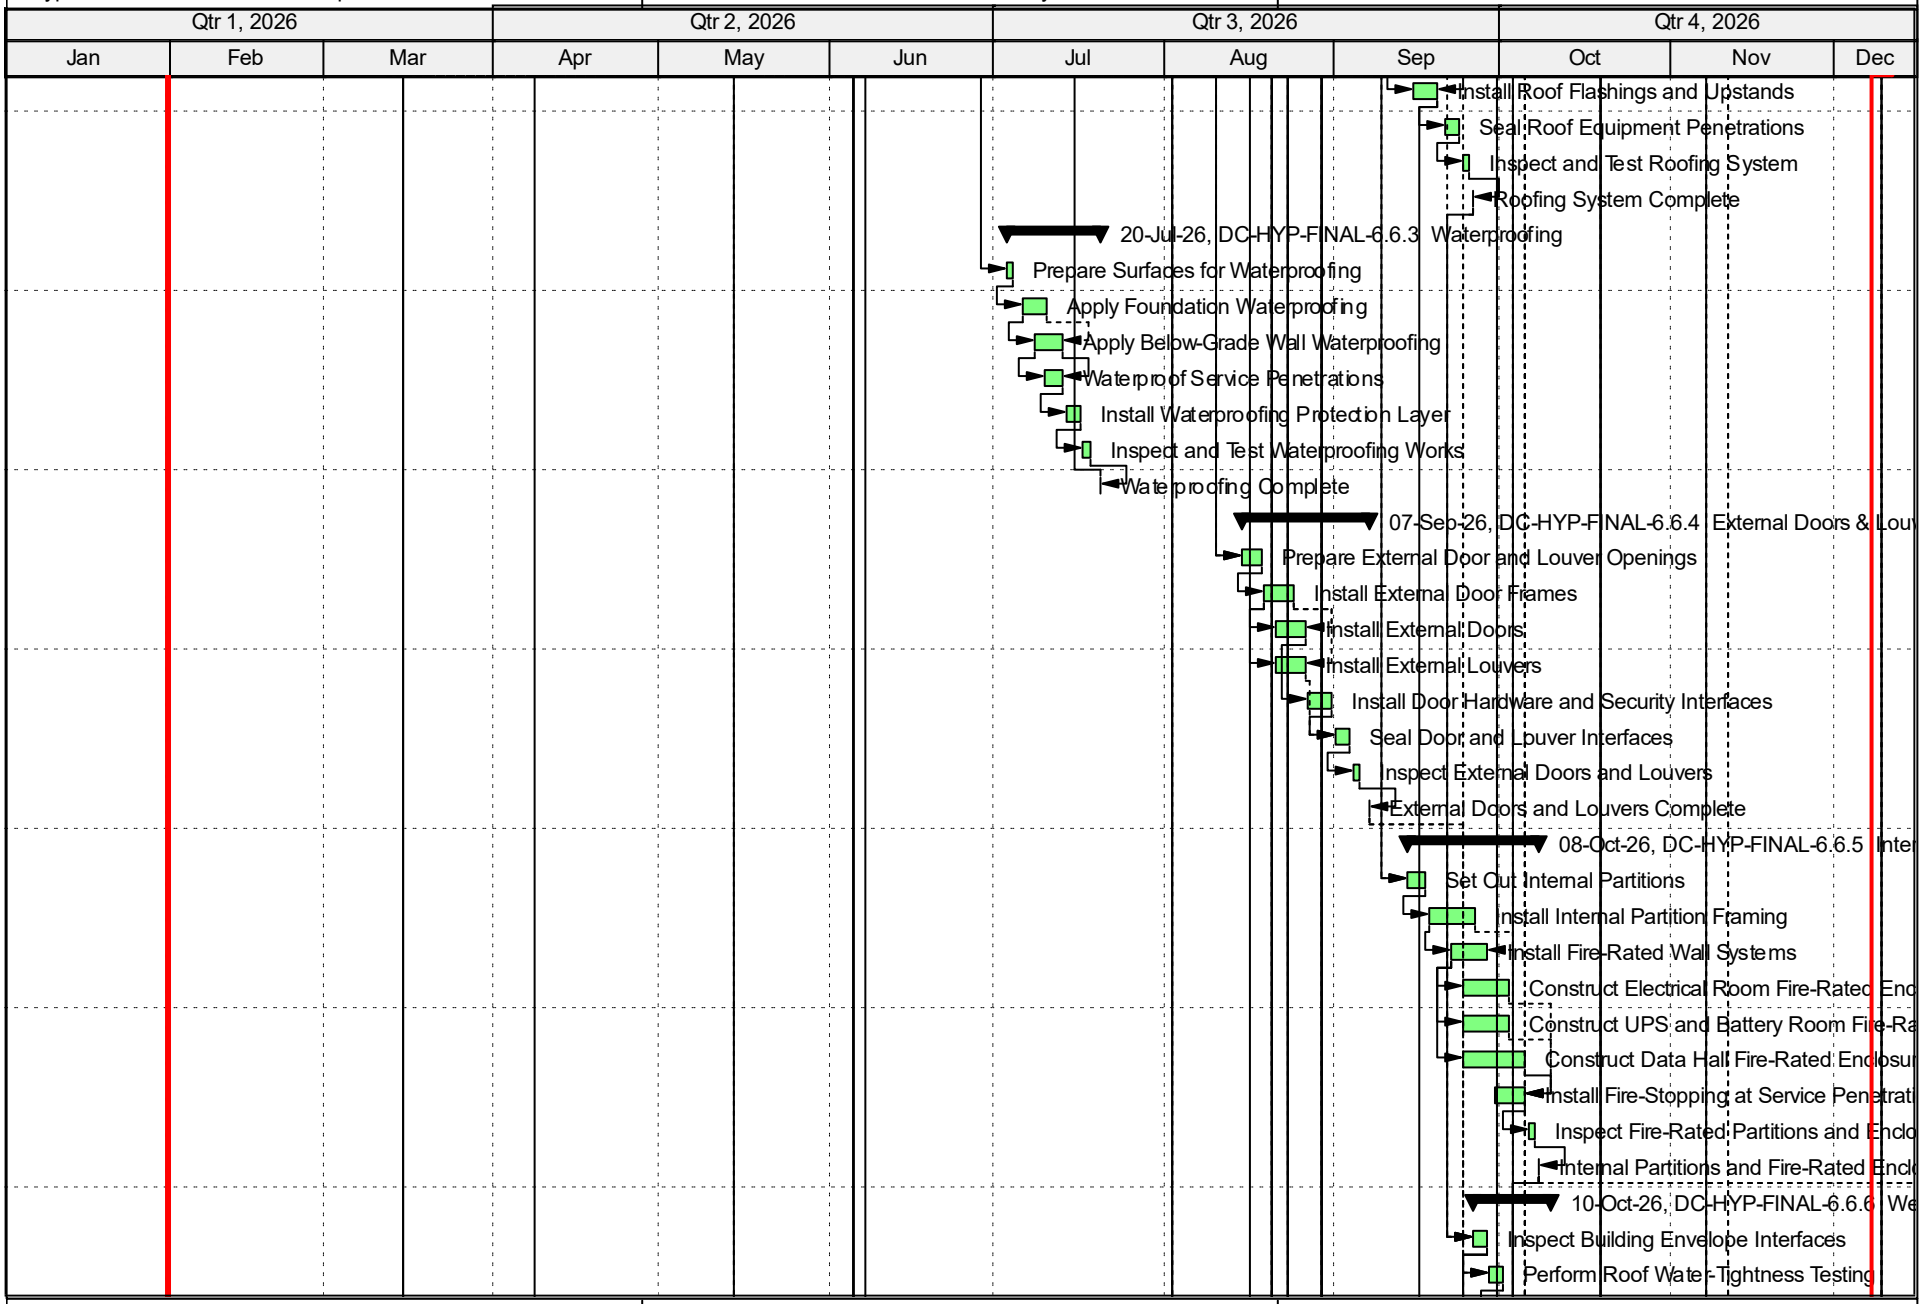


Actual Level of Effort | Remaining Work
Actual Work | Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
ENV-030	Perform External Wall Wate	3	3	0%	29-Sep-26	01-Oct-26	32		
ENV-040	Inspect Doors Louvers and	2	2	0%	29-Sep-26	30-Sep-26	33		
ENV-050	Rectify Building Envelope D	5	5	0%	02-Oct-26	07-Oct-26	32		
ENV-060	Complete Final Building En	2	2	0%	08-Oct-26	09-Oct-26	32		
ENV-070	Building Weather-Tight	0	0	0%	10-Oct-26	10-Oct-26	32		
DC-HYP-FINAL-6.7 Electrical Sy		246	246	0%	13-Apr-26	23-Jan-27	2		
DC-HYP-FINAL-6.7.1 Utility / MV Pow		35	35	0%	19-May-26	27-Jun-26	139		
MV-010	Set Out MV Power Infrastru	2	2	0%	19-May-26	20-May-26	139		
MV-020	Install MV Cable Duct Bank	15	15	0%	21-May-26	06-Jun-26	139		
MV-030	Install MV Cable Chambers	10	10	0%	27-May-26	06-Jun-26	139		
MV-040	Install Incoming MV Cables	10	10	0%	08-Jun-26	18-Jun-26	139		
MV-050	Terminate Incoming MV Ca	5	5	0%	19-Jun-26	24-Jun-26	139		
MV-060	Test Incoming MV Cable Sy	3	3	0%	25-Jun-26	27-Jun-26	139		
MV-070	MV Power Infrastructure Re	0	0	0%		27-Jun-26	139		
DC-HYP-FINAL-6.7.2 MV Switchgear		31	31	0%	10-Oct-26	14-Nov-26	26		
MVSG-01	Prepare MV Switchgear Ro	3	3	0%	10-Oct-26	13-Oct-26	37		
MVSG-02	Receive and Inspect MV Sv	2	2	0%	24-Oct-26	26-Oct-26	26		
MVSG-03	Position and Install MV Swi	5	5	0%	27-Oct-26	31-Oct-26	26		
MVSG-04	Assemble MV Switchgear S	5	5	0%	02-Nov-26	06-Nov-26	26		
MVSG-05	Install MV Switchgear Conti	5	5	0%	04-Nov-26	09-Nov-26	29		
MVSG-06	Terminate MV Power Cable	5	5	0%	07-Nov-26	12-Nov-26	26		
MVSG-07	Complete MV Switchgear In	2	2	0%	13-Nov-26	14-Nov-26	26		
MVSG-08	MV Switchgear Ready for F	0	0	0%		14-Nov-26	26		
DC-HYP-FINAL-6.7.3 Transformers		68	68	0%	08-Oct-26	25-Dec-26	0		
TRI-010	Prepare Transformer Areas	3	3	0%	08-Oct-26	10-Oct-26	55		
TRI-020	Receive and Inspect Transf	2	2	0%	12-Dec-26	14-Dec-26	0		
TRI-030	Position Transformers on Pl	3	3	0%	15-Dec-26	17-Dec-26	0		
TRI-040	Install Transformer Ancillary	5	5	0%	18-Dec-26	23-Dec-26	0		
TRI-050	Complete MV Transformer (	3	3	0%	18-Dec-26	21-Dec-26	2		
TRI-060	Complete LV Transformer C	3	3	0%	18-Dec-26	21-Dec-26	0		
TRI-070	Complete Transformer Insta	2	2	0%	24-Dec-26	25-Dec-26	0		
TRI-080	Transformers Ready for Pre	0	0	0%		25-Dec-26	0		
DC-HYP-FINAL-6.7.4 Standby Gener		113	113	0%	21-Aug-26	30-Dec-26	23		


© Oracle Corporation

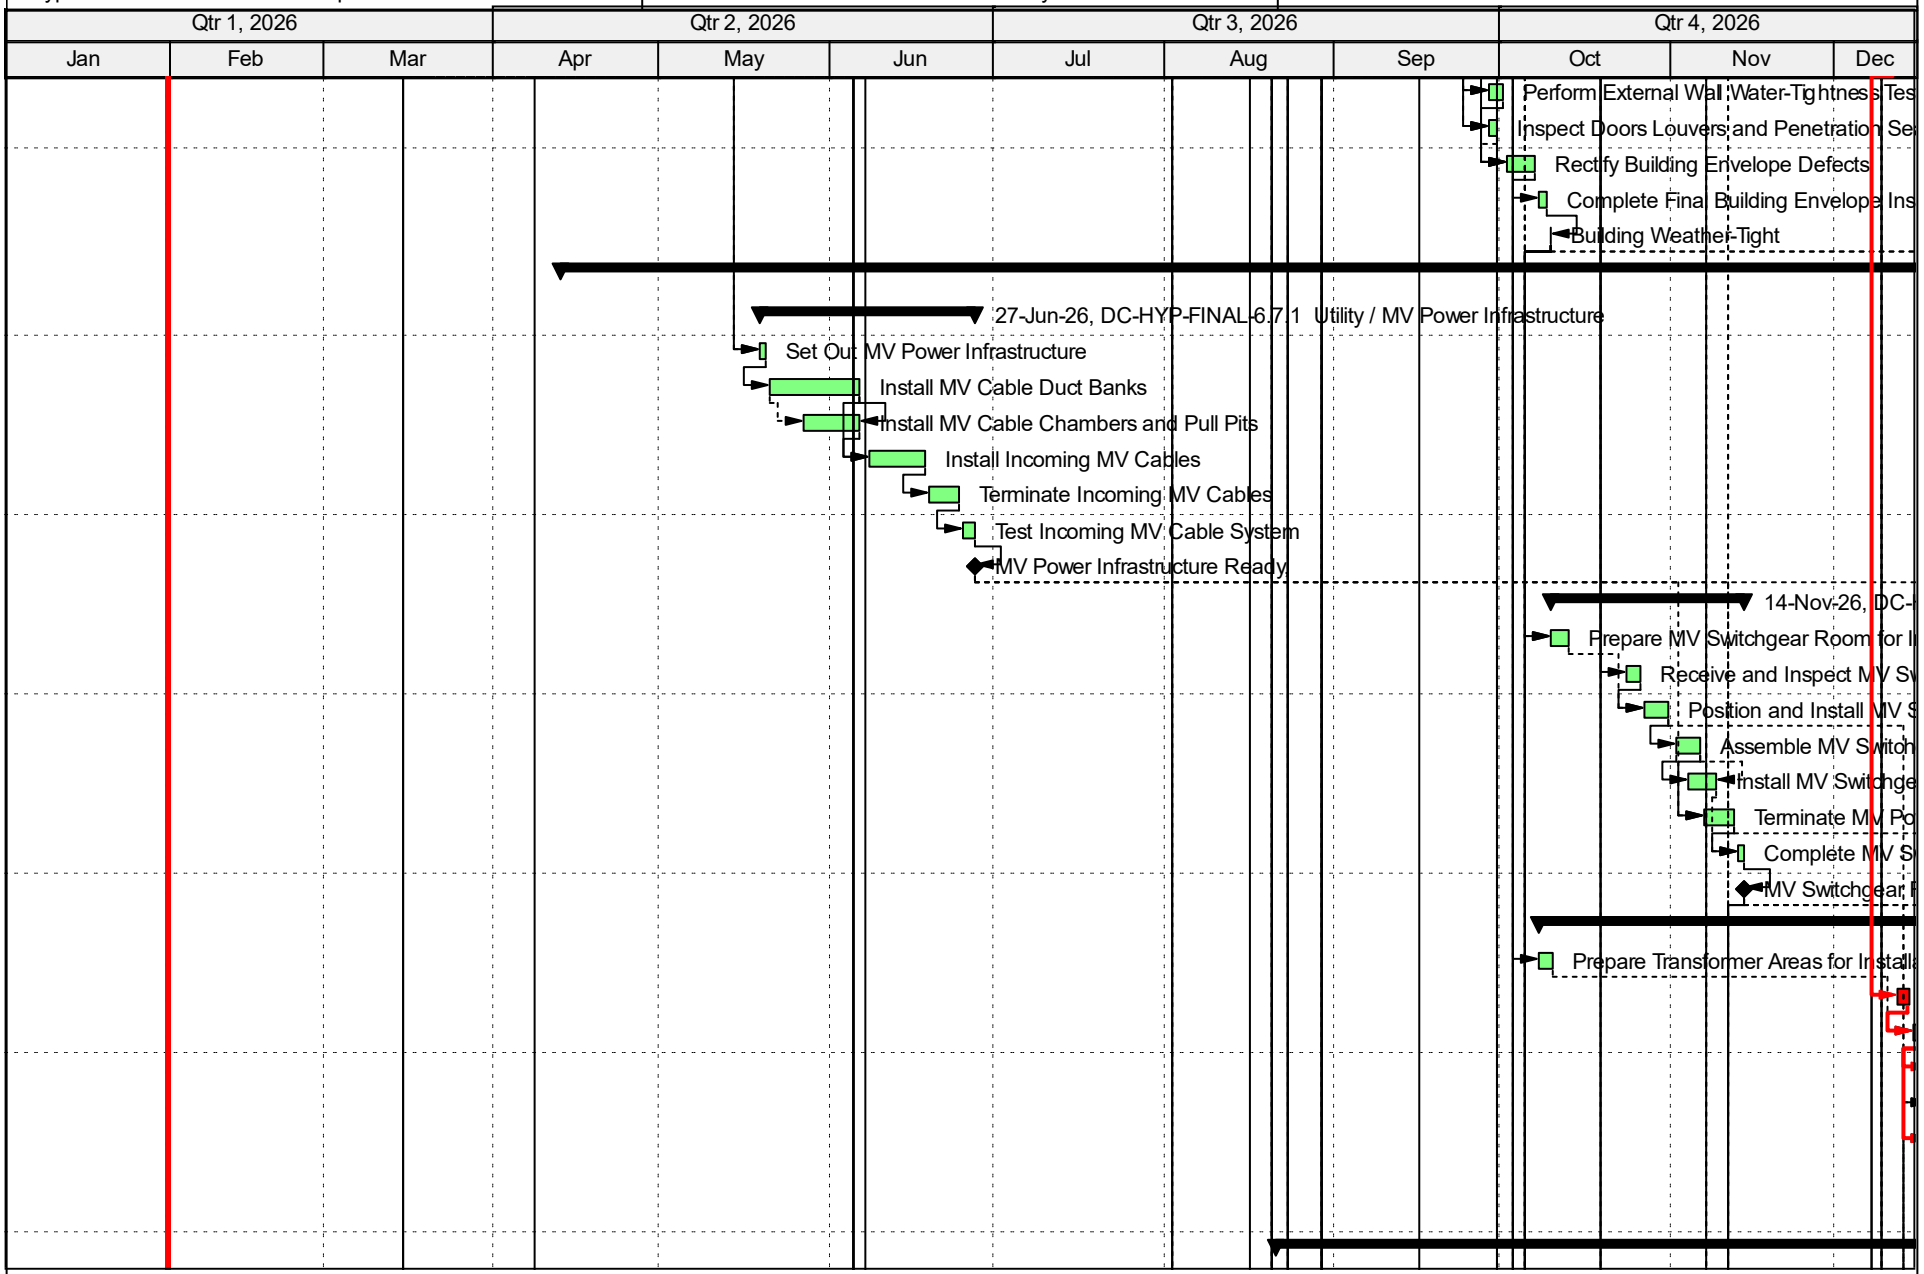

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
SGI-010	Prepare Generator Areas fo	3	3	0%	21-Aug-26	24-Aug-26	118		
SGI-020	Receive and Inspect Stand	2	2	0%	12-Dec-26	14-Dec-26	22		
SGI-030	Position Standby Generato	5	5	0%	15-Dec-26	19-Dec-26	22		
SGI-040	Install Generator Exhaust S	7	7	0%	21-Dec-26	28-Dec-26	23		
SGI-050	Install Generator Fuel Syste	7	7	0%	21-Dec-26	28-Dec-26	23		
SGI-060	Install Generator Power Co	5	5	0%	21-Dec-26	25-Dec-26	25		
SGI-070	Install Generator Control C	5	5	0%	21-Dec-26	25-Dec-26	25		
SGI-080	Complete Generator Install	2	2	0%	29-Dec-26	30-Dec-26	23		
SGI-090	Standby Generators Ready	0	0	0%		30-Dec-26	23		
DC-HYP-FINAL-6.7.5 LV Main Distrib		64	64	0%	10-Oct-26	23-Dec-26	0		
LV-010	Prepare LV Electrical Room	3	3	0%	10-Oct-26	13-Oct-26	42		
LV-020	Receive and Inspect LV Sw	2	2	0%	24-Oct-26	26-Oct-26	38		
LV-030	Position and Install LV Swit	5	5	0%	27-Oct-26	31-Oct-26	38		
LV-040	Install Main LV Cable Conta	8	8	0%	14-Oct-26	22-Oct-26	42		
LV-050	Install Main LV Power Cable	10	10	0%	16-Oct-26	27-Oct-26	42		
LV-060	Terminate Main LV Power C	5	5	0%	02-Nov-26	06-Nov-26	38		
LV-070	Install LV Control and Interl	5	5	0%	02-Nov-26	06-Nov-26	38		
LV-080	Complete LV Distribution In	2	2	0%	22-Dec-26	23-Dec-26	0		
LV-090	LV Main Distribution Ready	0	0	0%		23-Dec-26	0		
DC-HYP-FINAL-6.7.6 UPS Systems &		71	71	0%	10-Oct-26	31-Dec-26	0		
UPSI-010	Prepare UPS and Battery F	3	3	0%	10-Oct-26	13-Oct-26	54		
UPSI-020	Receive and Inspect UPS E	2	2	0%	24-Oct-26	26-Oct-26	45		
UPSI-030	Install UPS Units	5	5	0%	27-Oct-26	31-Oct-26	45		
UPSI-040	Install Battery Racks and C	5	5	0%	14-Oct-26	19-Oct-26	54		
UPSI-050	Install Battery Systems	7	7	0%	20-Oct-26	27-Oct-26	54		
UPSI-060	Install UPS Input and Outp	5	5	0%	24-Dec-26	29-Dec-26	0		
UPSI-070	Install UPS Control and Mo	5	5	0%	02-Nov-26	06-Nov-26	45		
UPSI-080	Complete UPS and Battery	2	2	0%	30-Dec-26	31-Dec-26	0		
UPSI-090	UPS and Battery Systems I	0	0	0%		31-Dec-26	0		
DC-HYP-FINAL-6.7.7 PDUs & Busway		110	110	0%	03-Sep-26	08-Jan-27	13		
BUS-010	Set Out PDU and Busway I	3	3	0%	03-Sep-26	05-Sep-26	72		
BUS-020	Install Busway Support Syst	10	10	0%	07-Sep-26	17-Sep-26	72		
BUS-030	Install Main Busway Distribu	15	15	0%	10-Sep-26	26-Sep-26	72		
BUS-040	Install Power Distribution Ur	7	7	0%	19-Sep-26	26-Sep-26	72		

© Oracle Corporation

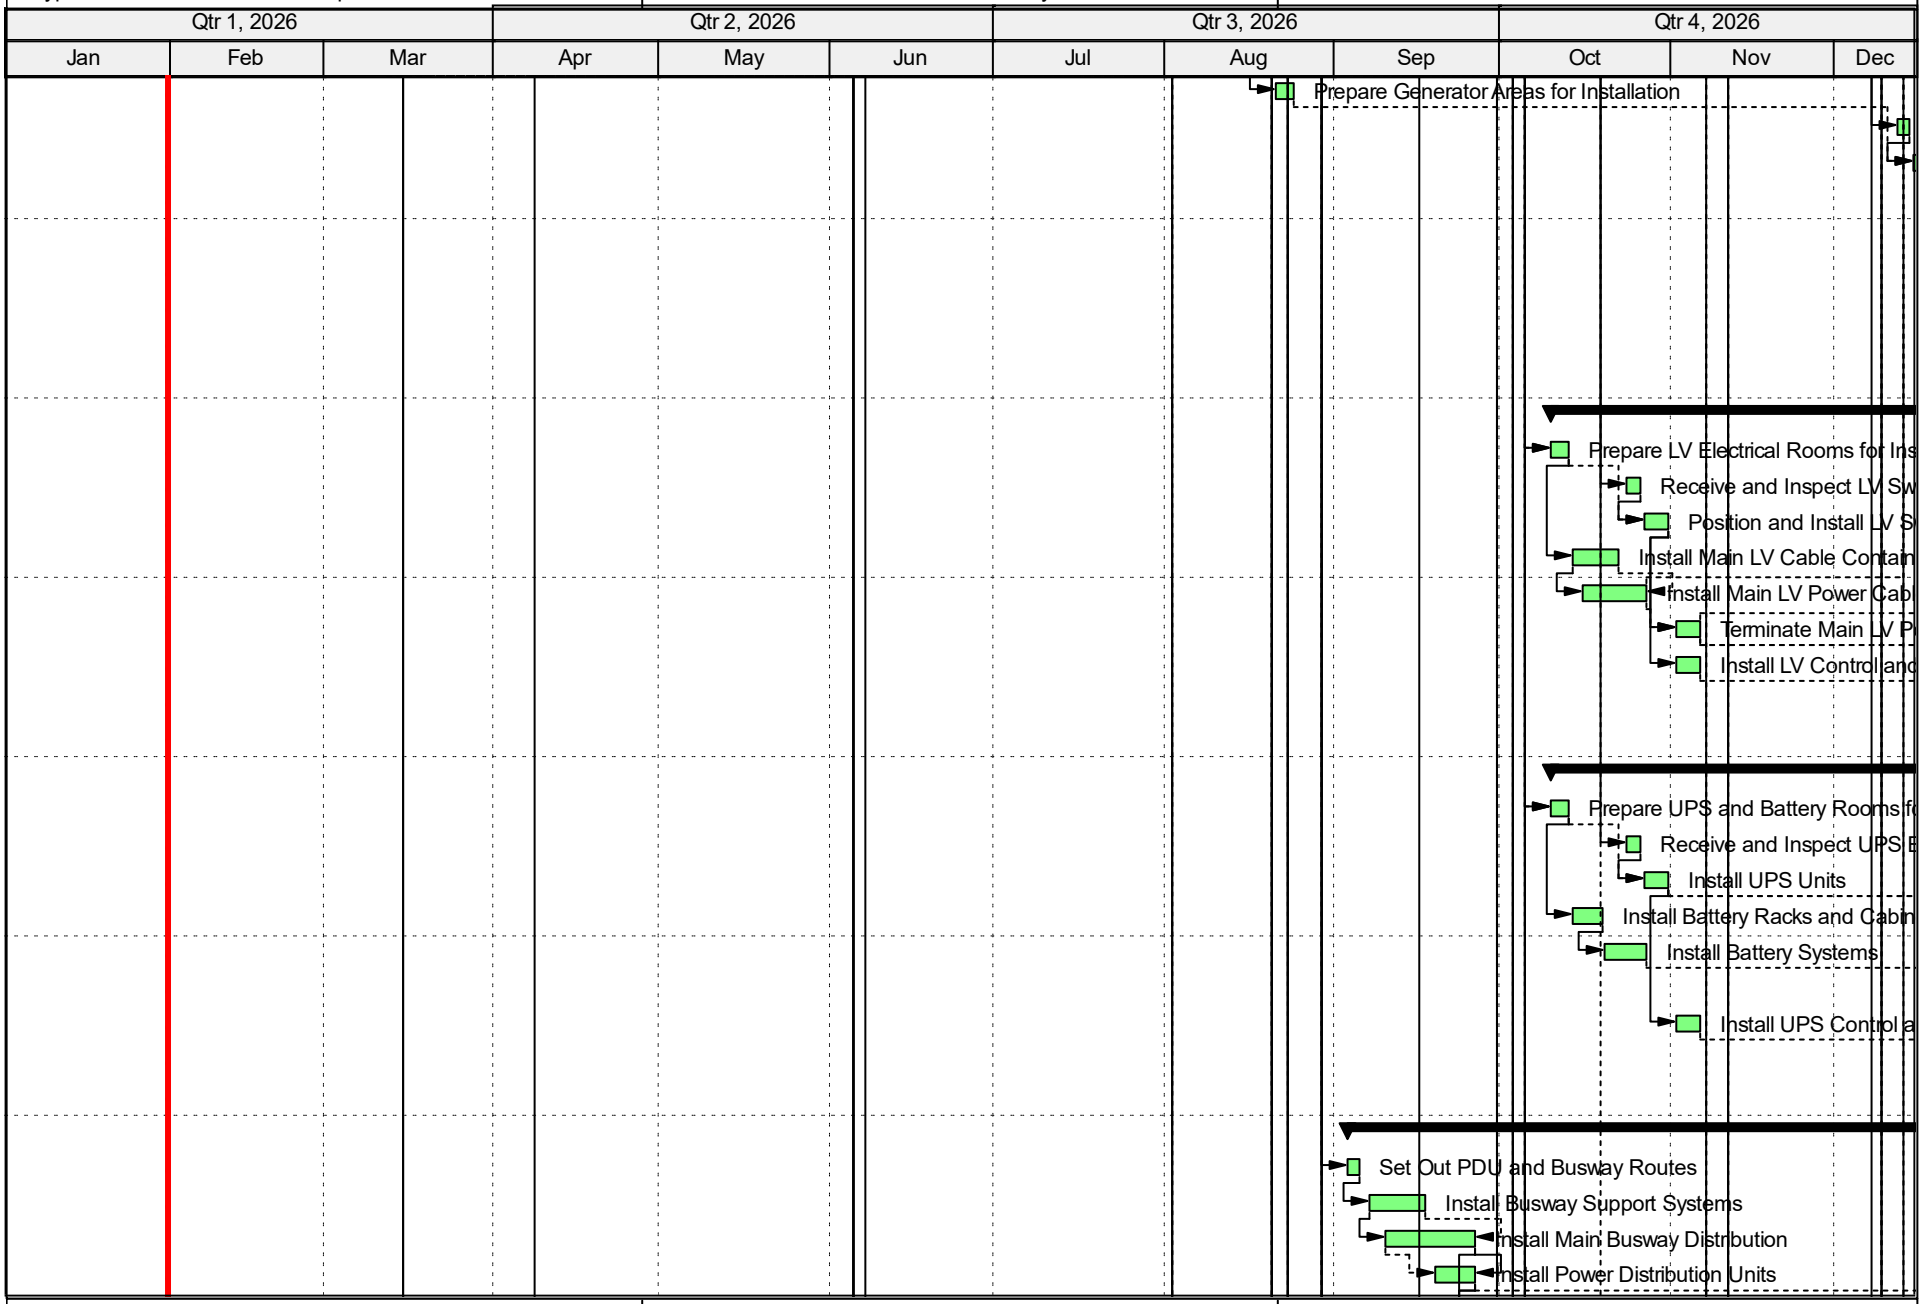


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
BUS-050	Install Busway Tap-Off Units	10	10	0%	28-Sep-26	08-Oct-26	72		
BUS-060	Complete Busway and PDU	5	5	0%	01-Jan-27	06-Jan-27	0		
BUS-070	Inspect PDU and Busway I	2	2	0%	07-Jan-27	08-Jan-27	13		
BUS-080	PDU and Busway Distributi	0	0	0%		08-Jan-27	13		
DC-HYP-FINAL-6.7.8 Data Hall Powe		123	123	0%	03-Sep-26	23-Jan-27	0		
DHP-010	Install Data Hall Cable Con	10	10	0%	03-Sep-26	14-Sep-26	90		
DHP-020	Install Data Hall Power Dist	15	15	0%	07-Sep-26	23-Sep-26	90		
DHP-030	Install Rack Power Distribut	10	10	0%	28-Sep-26	08-Oct-26	77		
DHP-040	Install Data Hall Power Mor	7	7	0%	15-Sep-26	22-Sep-26	101		
DHP-050	Terminate Data Hall Power	10	10	0%	07-Jan-27	18-Jan-27	0		
DHP-060	Test Data Hall Distribution (	5	5	0%	19-Jan-27	23-Jan-27	0		
DHP-070	Data Hall Power Distributior	0	0	0%		23-Jan-27	0		
DC-HYP-FINAL-6.7.9 Lightning Prote		12	12	0%	21-Sep-26	03-Oct-26	98		
LPS-010	Install Roof Lightning Prote	7	7	0%	21-Sep-26	28-Sep-26	98		
LPS-020	Install Lightning Protection I	5	5	0%	23-Sep-26	28-Sep-26	98		
LPS-030	Connect Lightning Protectic	3	3	0%	29-Sep-26	01-Oct-26	98		
LPS-040	Test Lightning Protection Sy	2	2	0%	02-Oct-26	03-Oct-26	98		
LPS-050	Lightning Protection Systen	0	0	0%		03-Oct-26	98		
DC-HYP-FINAL-6.7.10 Earthing & Bo		224	224	0%	13-Apr-26	29-Dec-26	22		
ERT-010	Install Main Site Earthing G	10	10	0%	13-Apr-26	23-Apr-26	215		
ERT-020	Install Building Earthing Net	10	10	0%	12-Jun-26	23-Jun-26	166		
ERT-030	Install Electrical Room Earth	5	5	0%	05-Oct-26	09-Oct-26	78		
ERT-040	Bond Transformers and Swi	5	5	0%	18-Dec-26	23-Dec-26	24		
ERT-050	Bond UPS and Generator E	5	5	0%	21-Dec-26	25-Dec-26	22		
ERT-060	Bond Mechanical and Data	10	10	0%	22-Oct-26	02-Nov-26	68		
ERT-070	Perform Earthing Resistanc	3	3	0%	26-Dec-26	29-Dec-26	22		
ERT-080	Earthing and Bonding Syste	0	0	0%		29-Dec-26	22		
DC-HYP-FINAL-6.7.11 Electrical Roor		81	81	0%	05-Oct-26	06-Jan-27	17		
ERA-010	Install Electrical Room Cabl	10	10	0%	05-Oct-26	15-Oct-26	86		
ERA-020	Install Electrical Room Light	7	7	0%	08-Oct-26	15-Oct-26	86		
ERA-030	Install Electrical Room Sma	7	7	0%	08-Oct-26	15-Oct-26	86		
ERA-040	Install Emergency Lighting	5	5	0%	10-Oct-26	15-Oct-26	86		
ERA-050	Install Electrical Room Iden	3	3	0%	01-Jan-27	04-Jan-27	17		
ERA-060	Complete Electrical Room I	5	5	0%	30-Dec-26	04-Jan-27	17		

© Oracle Corporation

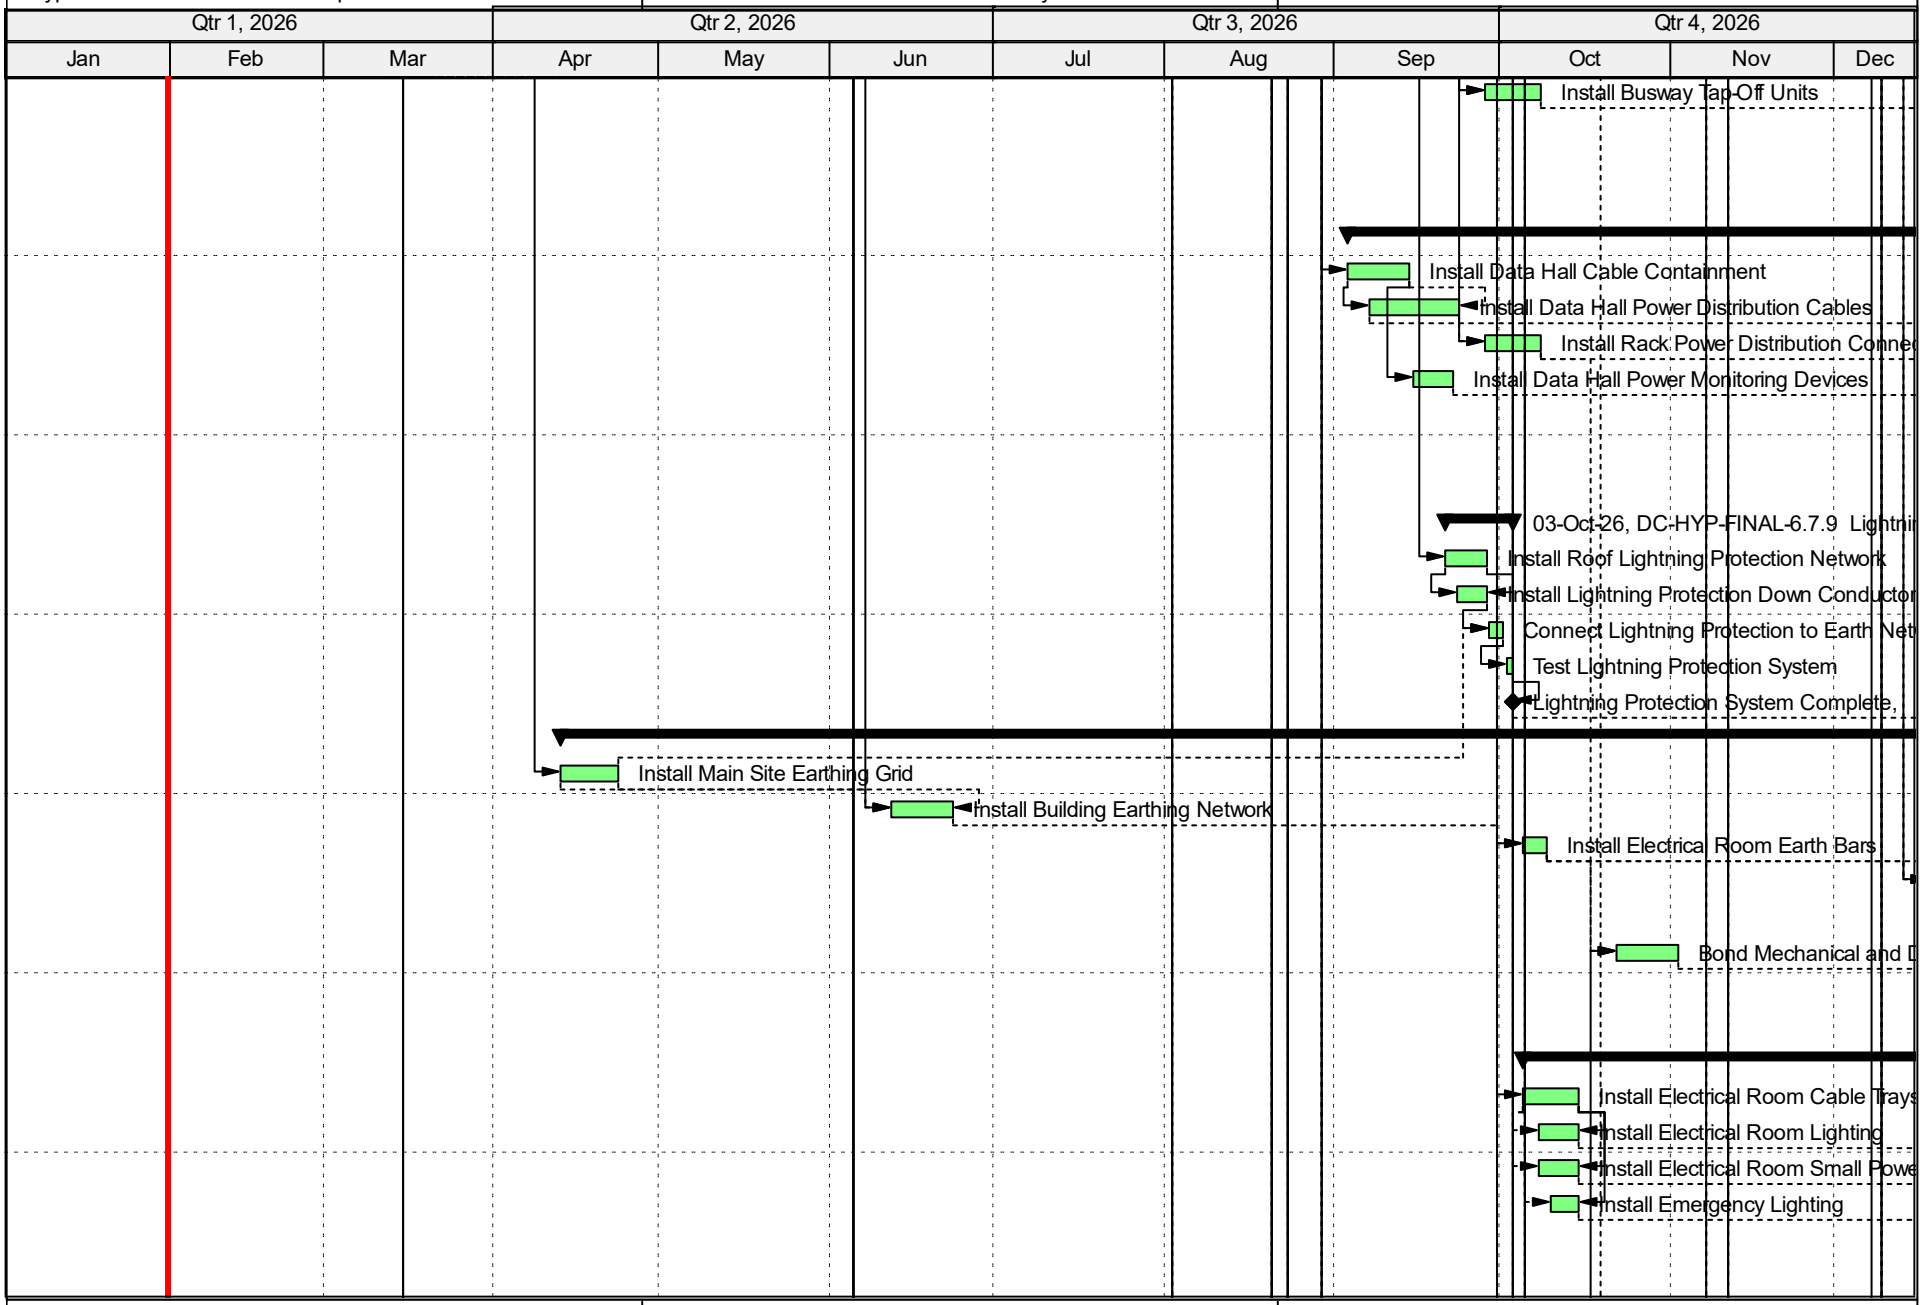


Actual Level of Effort | Remaining Work
Actual Work | Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
ERA-070	Complete Electrical Room I	2	2	0%	05-Jan-27	06-Jan-27	17		
ERA-080	Electrical Rooms Ready for	0	0	0%		06-Jan-27	17		
DC-HYP-FINAL-6.8 Mechanical		90	90	0%	25-Aug-26	07-Dec-26	43		
DC-HYP-FINAL-6.8.1 Cooling Plant		25	25	0%	25-Aug-26	22-Sep-26	108		
CLG-010	Prepare Cooling Plant Area	3	3	0%	25-Aug-26	27-Aug-26	108		
CLG-020	Install Cooling Plant Equipr	5	5	0%	28-Aug-26	02-Sep-26	108		
CLG-030	Install Cooling Plant Main H	10	10	0%	03-Sep-26	14-Sep-26	108		
CLG-040	Install Cooling Plant Valves	5	5	0%	15-Sep-26	19-Sep-26	108		
CLG-050	Install Cooling Plant Electric	5	5	0%	09-Sep-26	14-Sep-26	113		
CLG-060	Install Cooling Plant Contro	5	5	0%	09-Sep-26	14-Sep-26	113		
CLG-070	Inspect Cooling Plant Instal	2	2	0%	21-Sep-26	22-Sep-26	108		
CLG-080	Cooling Plant Ready for Pre	0	0	0%		22-Sep-26	108		
DC-HYP-FINAL-6.8.2 Chillers / Heat R		22	22	0%	28-Aug-26	22-Sep-26	96		
CHR-010	Prepare Chiller and Heat R	3	3	0%	28-Aug-26	31-Aug-26	47		
CHR-020	Receive and Inspect Chiller	2	2	0%	01-Sep-26	02-Sep-26	47		
CHR-030	Position Chillers on Equipm	5	5	0%	03-Sep-26	08-Sep-26	47		
CHR-040	Position Heat Rejection Eq	5	5	0%	03-Sep-26	08-Sep-26	99		
CHR-050	Install Chiller Mechanical C	10	10	0%	09-Sep-26	19-Sep-26	47		
CHR-060	Install Heat Rejection Equip	7	7	0%	09-Sep-26	16-Sep-26	99		
CHR-070	Install Electrical and Contro	7	7	0%	05-Sep-26	12-Sep-26	102		
CHR-080	Complete Chiller Installatior	2	2	0%	21-Sep-26	22-Sep-26	96		
CHR-090	Chillers and Heat Rejection	0	0	0%		22-Sep-26	96		
DC-HYP-FINAL-6.8.3 Pumps & Pump		19	19	0%	25-Aug-26	15-Sep-26	102		
PMP-010	Prepare Pump Bases for In	3	3	0%	25-Aug-26	27-Aug-26	53		
PMP-020	Receive and Inspect Pump	2	2	0%	28-Aug-26	29-Aug-26	53		
PMP-030	Install Primary Cooling Pum	5	5	0%	31-Aug-26	04-Sep-26	53		
PMP-040	Install Secondary Cooling F	5	5	0%	31-Aug-26	04-Sep-26	53		
PMP-050	Install Pump Suction and D	7	7	0%	05-Sep-26	12-Sep-26	53		
PMP-060	Install Pump Electrical Con	5	5	0%	02-Sep-26	07-Sep-26	107		
PMP-070	Install Pump Controls and I	5	5	0%	02-Sep-26	07-Sep-26	107		
PMP-080	Inspect Pumping System In	2	2	0%	14-Sep-26	15-Sep-26	102		
PMP-090	Pumping Systems Ready fo	0	0	0%		15-Sep-26	102		
DC-HYP-FINAL-6.8.5 CRAH / CRAC S		54	54	0%	03-Sep-26	04-Nov-26	59		


© Oracle Corporation

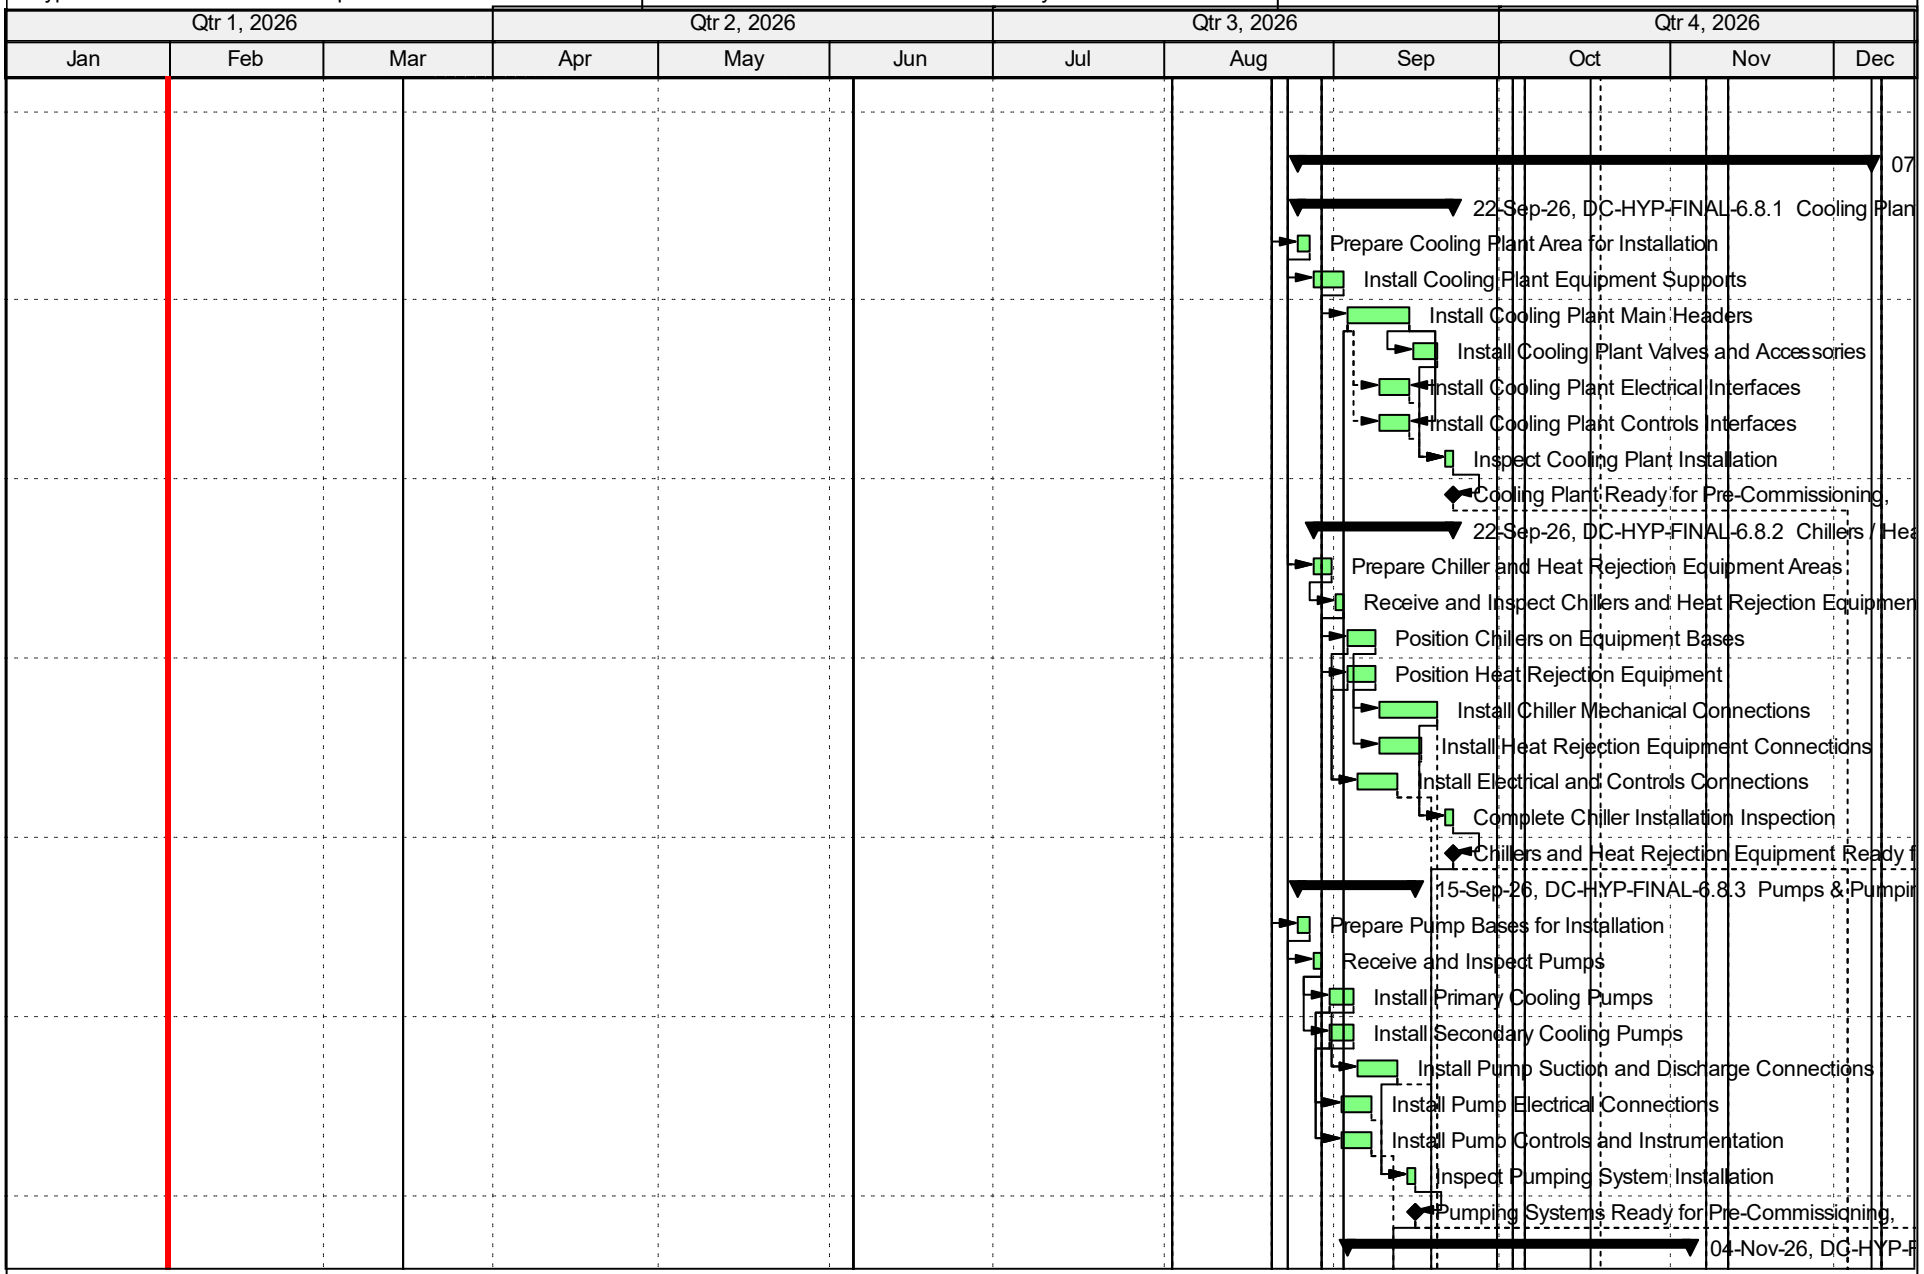

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
CRAC-010	Prepare CRAH/CRAC Insta	3	3	0%	03-Sep-26	05-Sep-26	59		
CRAC-020	Receive and Inspect CRAH	2	2	0%	07-Sep-26	08-Sep-26	59		
CRAC-030	Position and Install CRAH/(	10	10	0%	10-Oct-26	21-Oct-26	32		
CRAC-040	Install CRAH/CRAC Chillec	10	10	0%	22-Oct-26	02-Nov-26	32		
CRAC-050	Install CRAH/CRAC Conde	7	7	0%	22-Oct-26	29-Oct-26	62		
CRAC-060	Install CRAH/CRAC Electri	7	7	0%	22-Oct-26	29-Oct-26	62		
CRAC-070	Install CRAH/CRAC Contro	7	7	0%	22-Oct-26	29-Oct-26	62		
CRAC-080	Complete CRAH/CRAC Ins	2	2	0%	03-Nov-26	04-Nov-26	59		
CRAC-090	CRAH/CRAC Systems Rea	0	0	0%		04-Nov-26	59		
DC-HYP-FINAL-6.8.6 Data Hall Coolir		64	64	0%	03-Sep-26	16-Nov-26	49		
DHC-010	Set Out Data Hall Cooling I	3	3	0%	03-Sep-26	05-Sep-26	70		
DHC-020	Install Data Hall Cooling Pi	7	7	0%	07-Sep-26	14-Sep-26	70		
DHC-030	Install Data Hall Cooling Di	15	15	0%	10-Sep-26	26-Sep-26	70		
DHC-040	Install Data Hall Cooling Va	7	7	0%	19-Sep-26	26-Sep-26	70		
DHC-050	Connect Cooling Distributio	10	10	0%	22-Oct-26	02-Nov-26	49		
DHC-060	Pressure Test Data Hall Co	5	5	0%	03-Nov-26	07-Nov-26	49		
DHC-070	Flush Data Hall Cooling Dis	5	5	0%	09-Nov-26	13-Nov-26	51		
DHC-080	Insulate Data Hall Cooling I	10	10	0%	05-Nov-26	16-Nov-26	49		
DHC-090	Data Hall Cooling Distributi	0	0	0%		16-Nov-26	49		
DC-HYP-FINAL-6.8.7 Ventilation & E		21	21	0%	05-Oct-26	28-Oct-26	77		
VEN-010	Install Ventilation Ductwork	7	7	0%	05-Oct-26	12-Oct-26	77		
VEN-020	Install Ventilation and Exha	15	15	0%	07-Oct-26	23-Oct-26	77		
VEN-030	Install Ventilation Fans	7	7	0%	07-Oct-26	14-Oct-26	80		
VEN-040	Install Dampers and Air Cor	7	7	0%	10-Oct-26	17-Oct-26	77		
VEN-050	Install Louvers Grilles and T	7	7	0%	10-Oct-26	17-Oct-26	77		
VEN-060	Install Ventilation Controls (	7	7	0%	19-Oct-26	26-Oct-26	77		
VEN-070	Inspect Ventilation and Exh	2	2	0%	27-Oct-26	28-Oct-26	77		
VEN-080	Ventilation and Exhaust Sys	0	0	0%		28-Oct-26	77		
DC-HYP-FINAL-6.8.8 Mechanical Cor		40	40	0%	22-Oct-26	07-Dec-26	32		
MCI-010	Install Mechanical Control F	5	5	0%	22-Oct-26	27-Oct-26	40		
MCI-020	Install Temperature Sensors	7	7	0%	24-Oct-26	31-Oct-26	43		
MCI-030	Install Pressure Sensors	7	7	0%	24-Oct-26	31-Oct-26	43		
MCI-040	Install Flow Measurement D	7	7	0%	24-Oct-26	31-Oct-26	43		
MCI-050	Install Control Valves and A	10	10	0%	03-Nov-26	13-Nov-26	32		

© Oracle Corporation

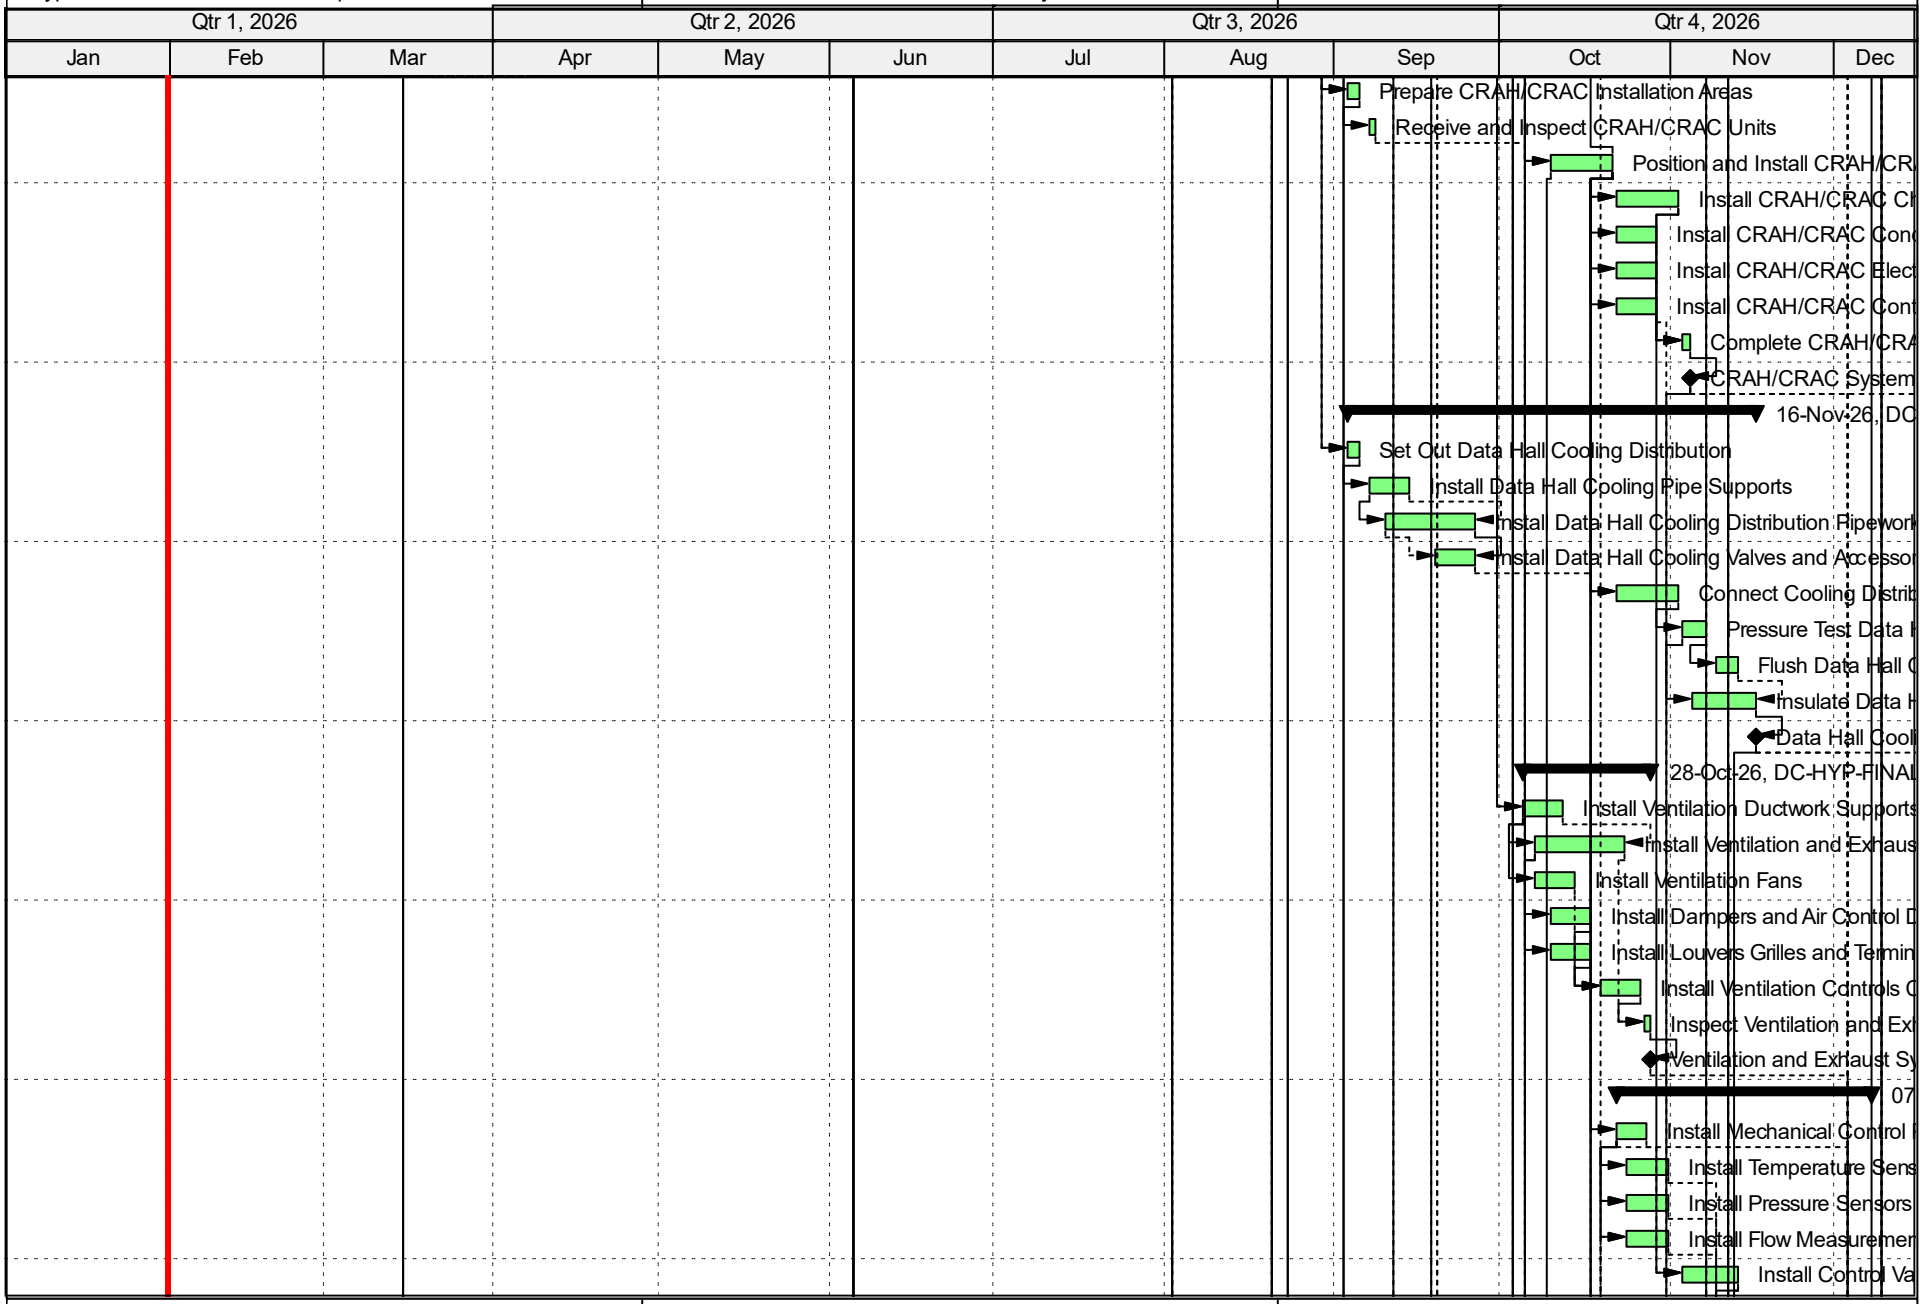


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
MCI-060	Complete Mechanical Cont	10	10	0%	14-Nov-26	25-Nov-26	32		
MCI-070	Complete BMS Interface C	7	7	0%	26-Nov-26	03-Dec-26	32		
MCI-080	Inspect Mechanical Control	3	3	0%	04-Dec-26	07-Dec-26	32		
MCI-090	Mechanical Controls Ready	0	0	0%		07-Dec-26	32		
DC-HYP-FINAL-6.8.9 Water Treatmen		20	20	0%	25-Aug-26	16-Sep-26	113		
WTM-010	Prepare Water Treatment E	3	3	0%	25-Aug-26	27-Aug-26	113		
WTM-020	Install Water Treatment Equ	5	5	0%	28-Aug-26	02-Sep-26	113		
WTM-030	Install Chemical Dosing Sys	5	5	0%	03-Sep-26	08-Sep-26	113		
WTM-040	Install Cooling System Mak	5	5	0%	03-Sep-26	08-Sep-26	113		
WTM-050	Install Water Treatment Inst	5	5	0%	31-Aug-26	04-Sep-26	116		
WTM-060	Complete Electrical and Co	5	5	0%	09-Sep-26	14-Sep-26	113		
WTM-070	Inspect Water Treatment ar	2	2	0%	15-Sep-26	16-Sep-26	113		
WTM-080	Water Treatment and Make	0	0	0%		16-Sep-26	113		
DC-HYP-FINAL-6.8.10 Mechanical An		49	49	0%	07-Sep-26	02-Nov-26	73		
MCA-010	Install Mechanical Equipme	7	7	0%	22-Oct-26	29-Oct-26	73		
MCA-020	Install Condensate Drainag	7	7	0%	22-Oct-26	29-Oct-26	73		
MCA-030	Install Mechanical Equipme	5	5	0%	07-Sep-26	11-Sep-26	114		
MCA-040	Complete Mechanical Equi	5	5	0%	14-Oct-26	19-Oct-26	82		
MCA-050	Complete Mechanical Plant	5	5	0%	07-Sep-26	11-Sep-26	114		
MCA-060	Complete Mechanical Insta	3	3	0%	30-Oct-26	02-Nov-26	73		
MCA-070	Mechanical Systems Install	0	0	0%		02-Nov-26	73		
DC-HYP-FINAL-6.8.4 Chilled Water D		38	38	0%	25-Aug-26	07-Oct-26	95		
CHW-010	Set Out Chilled Water Pipe	3	3	0%	25-Aug-26	27-Aug-26	44		
CHW-020	Install Chilled Water Pipe S	10	10	0%	28-Aug-26	08-Sep-26	44		
CHW-030	Install Main Chilled Water F	15	15	0%	01-Sep-26	17-Sep-26	44		
CHW-040	Install Chilled Water Branch	15	15	0%	07-Sep-26	23-Sep-26	44		
CHW-050	Install Chilled Water Valves	7	7	0%	16-Sep-26	23-Sep-26	44		
CHW-060	Pressure Test Chilled Water	7	7	0%	24-Sep-26	01-Oct-26	44		
CHW-070	Flush and Clean Chilled Wa	5	5	0%	02-Oct-26	07-Oct-26	44		
CHW-080	Install Chilled Water Pipe In	10	10	0%	26-Sep-26	07-Oct-26	95		
CHW-090	Chilled Water Distribution R	0	0	0%		07-Oct-26	95		
DC-HYP-FINAL-6.9 Fire & Life S		219	219	0%	10-Jun-26	19-Feb-27	63		
DC-HYP-FINAL-6.9.1 Fire Detection &		117	117	0%	10-Jun-26	23-Oct-26	67		

© Oracle Corporation

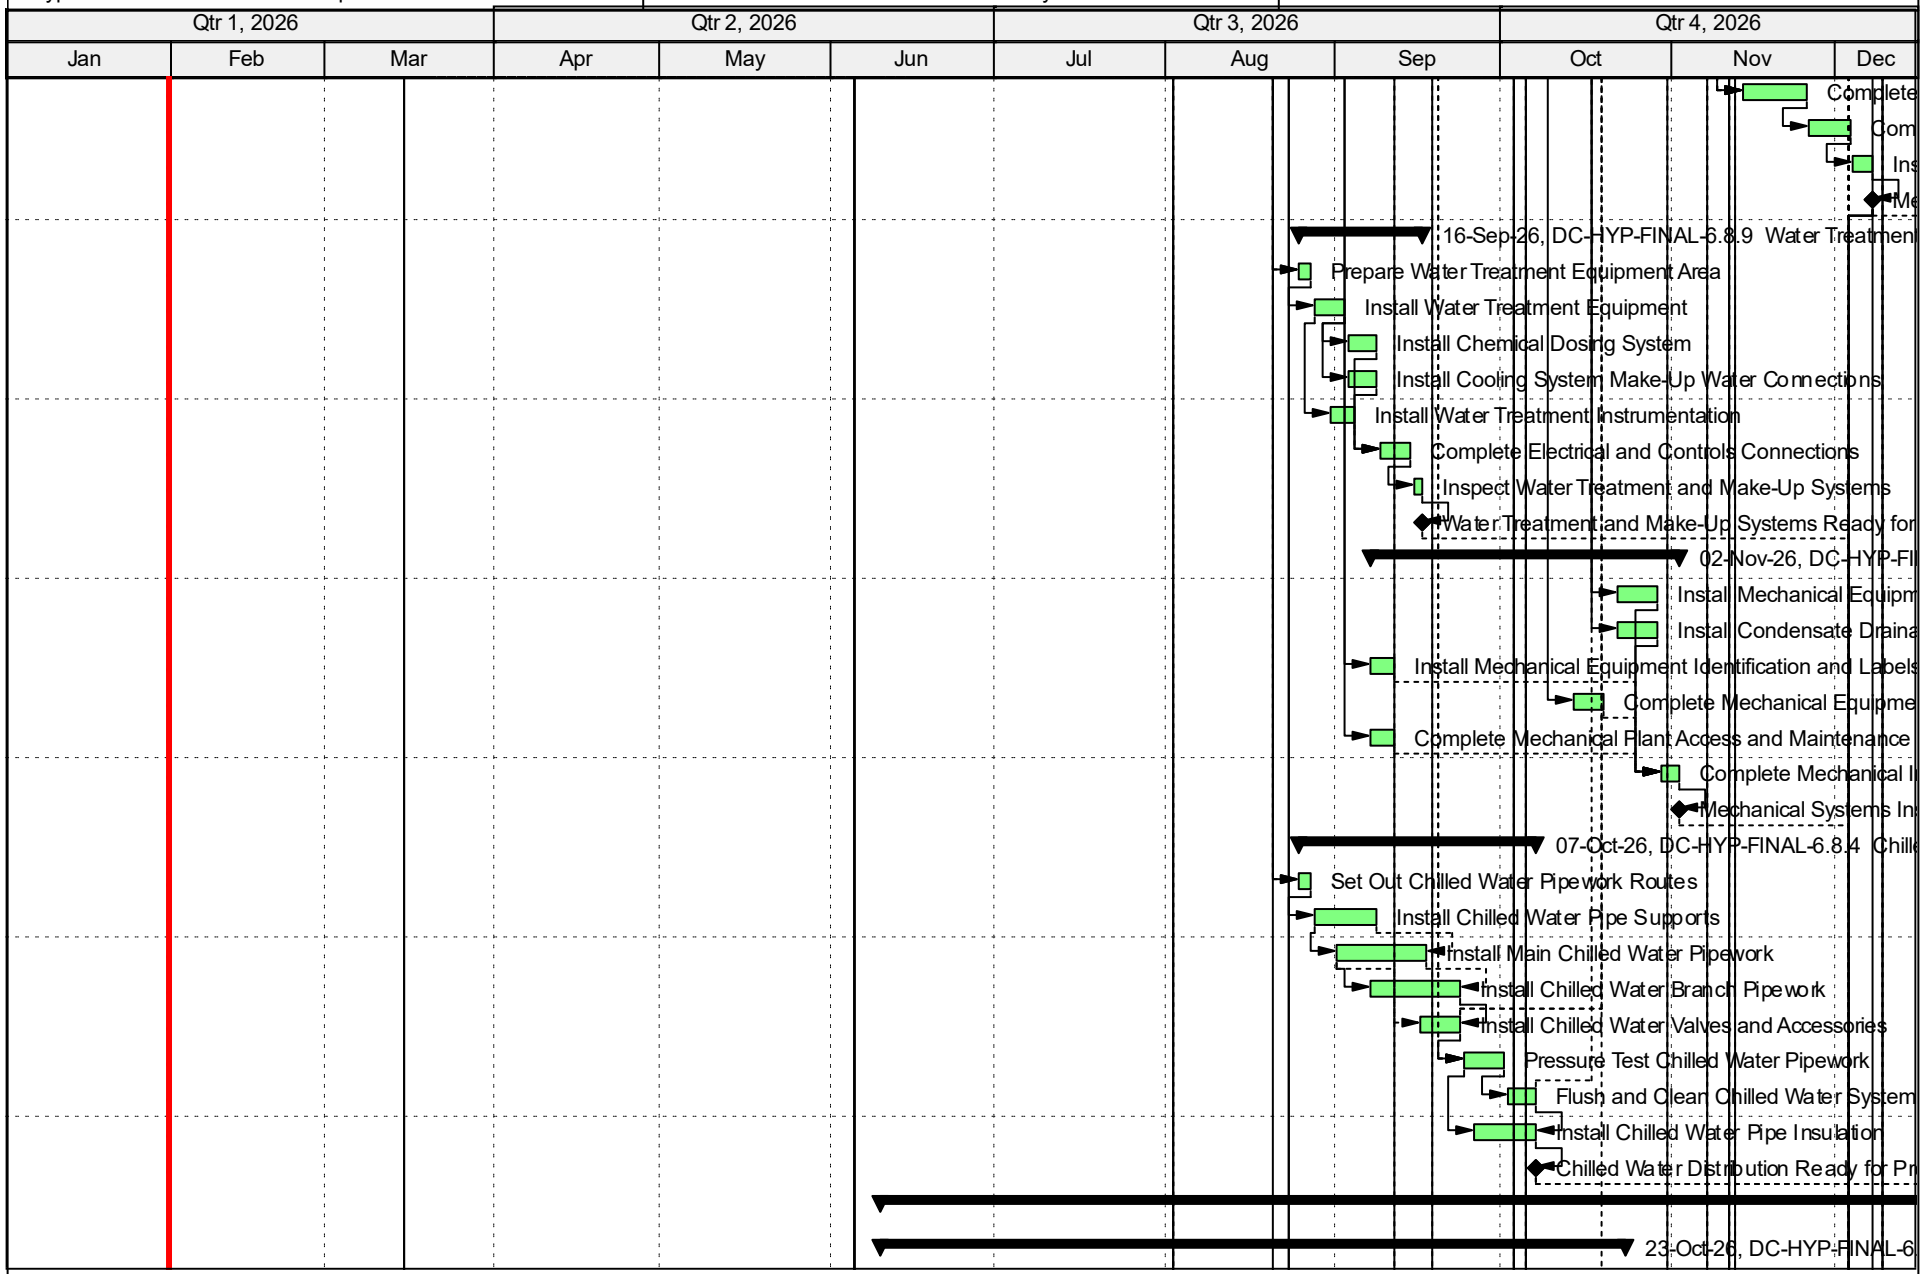


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
FAD-010	Install Fire Alarm Control Pa	5	5	0%	10-Jun-26	15-Jun-26	175		
FAD-020	Install Fire Alarm Cabling	10	10	0%	08-Oct-26	19-Oct-26	67		
FAD-030	Install Smoke and Heat De	8	8	0%	10-Oct-26	19-Oct-26	67		
FAD-040	Install Manual Call Points	4	4	0%	10-Oct-26	14-Oct-26	71		
FAD-050	Install Notification Devices	6	6	0%	10-Oct-26	16-Oct-26	69		
FAD-060	Complete Fire Alarm Device	2	2	0%	20-Oct-26	21-Oct-26	67		
FAD-070	Inspect Fire Detection and /	2	2	0%	22-Oct-26	23-Oct-26	67		
FAD-080	Fire Detection and Alarm R	0	0	0%		23-Oct-26	67		
DC-HYP-FINAL-6.9.2 Sprinkler Syste		24	24	0%	08-Oct-26	04-Nov-26	71		
SPR-010	Install Sprinkler Main Pipew	10	10	0%	08-Oct-26	19-Oct-26	71		
SPR-020	Install Sprinkler Branch Pipe	10	10	0%	12-Oct-26	22-Oct-26	71		
SPR-030	Install Sprinkler Heads	8	8	0%	15-Oct-26	23-Oct-26	71		
SPR-040	Install Zone Control Assemb	5	5	0%	10-Oct-26	15-Oct-26	78		
SPR-050	Pressure Test Sprinkler Syst	3	3	0%	24-Oct-26	27-Oct-26	71		
SPR-060	Flush Sprinkler System	5	5	0%	28-Oct-26	02-Nov-26	71		
SPR-070	Inspect Sprinkler Installatior	2	2	0%	03-Nov-26	04-Nov-26	71		
SPR-080	Sprinkler System Ready for	0	0	0%		04-Nov-26	71		
DC-HYP-FINAL-6.9.3 Clean Agent Fir		22	22	0%	08-Oct-26	02-Nov-26	73		
CAF-010	Prepare Clean Agent Protec	5	5	0%	08-Oct-26	13-Oct-26	73		
CAF-020	Install Clean Agent Cylinder	5	5	0%	14-Oct-26	19-Oct-26	76		
CAF-030	Install Clean Agent Distribut	8	8	0%	14-Oct-26	22-Oct-26	73		
CAF-040	Install Clean Agent Dischar	5	5	0%	23-Oct-26	28-Oct-26	73		
CAF-050	Install Release and Control	5	5	0%	22-Oct-26	27-Oct-26	74		
CAF-060	Complete Room Integrity P	2	2	0%	29-Oct-26	30-Oct-26	73		
CAF-070	Inspect Clean Agent Suppr	2	2	0%	31-Oct-26	02-Nov-26	73		
CAF-080	Clean Agent Suppression F	0	0	0%		02-Nov-26	73		
DC-HYP-FINAL-6.9.4 Fire Pump & Wa		122	122	0%	10-Jun-26	29-Oct-26	76		
FPW-010	Prepare Fire Pump Room	5	5	0%	10-Jun-26	15-Jun-26	178		
FPW-020	Install Fire Water Tank Conr	5	5	0%	16-Jun-26	20-Jun-26	178		
FPW-030	Install Main Fire Pumps	5	5	0%	16-Jun-26	20-Jun-26	178		
FPW-040	Install Jockey Pump	5	5	0%	16-Jun-26	20-Jun-26	178		
FPW-050	Install Fire Pump Pipework a	8	8	0%	22-Jun-26	30-Jun-26	178		
FPW-060	Install Fire Pump Electrical (	5	5	0%	22-Jun-26	26-Jun-26	181		
FPW-070	Install Fire Pump Controls	5	5	0%	22-Oct-26	27-Oct-26	76		

© Oracle Corporation

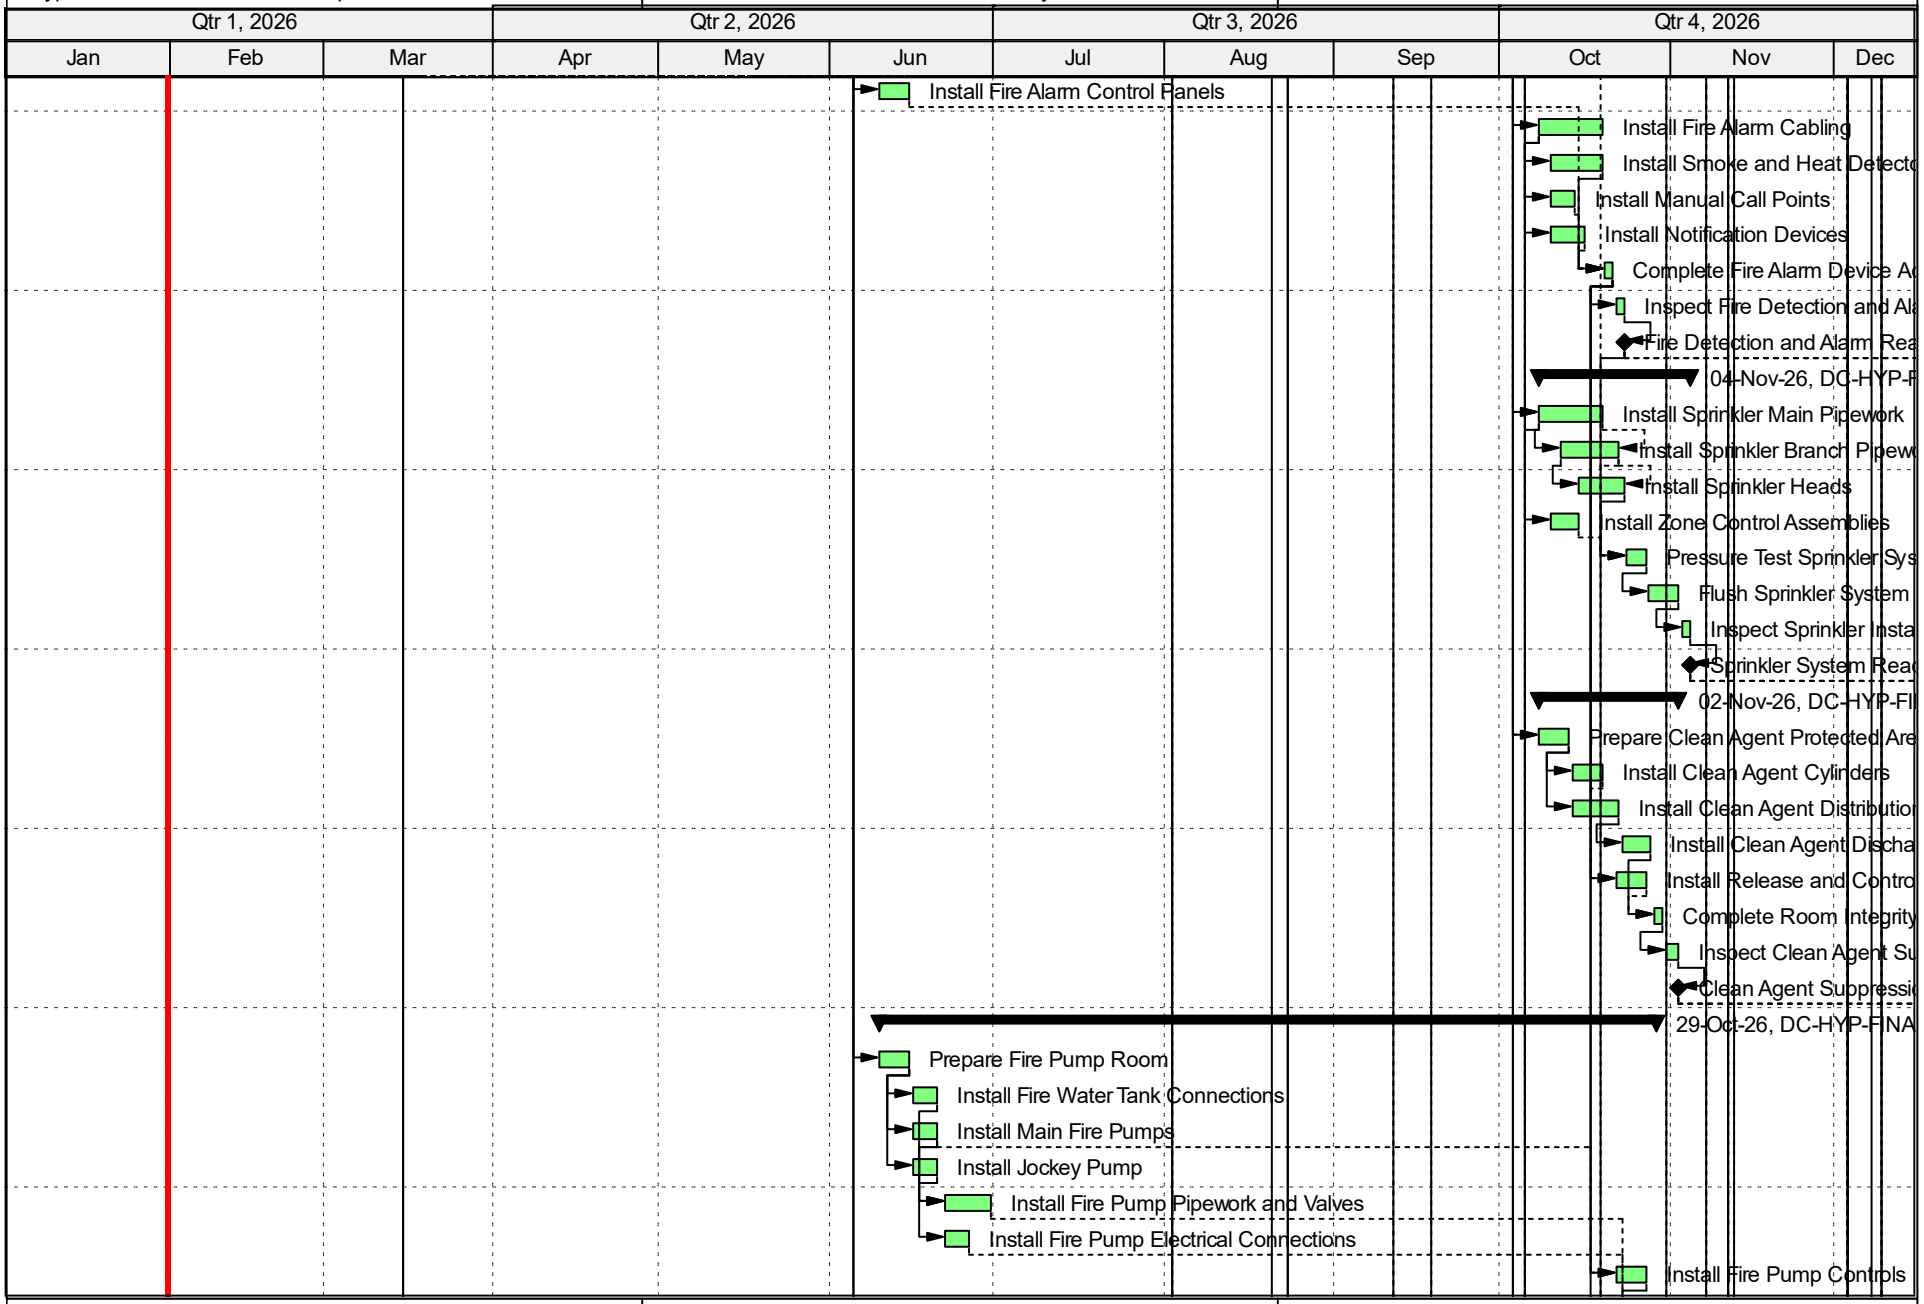


Actual Level of Effort | Remaining Work
Actual Work | Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
FPW-080	Inspect Fire Pump and Wat	2	2	0%	28-Oct-26	29-Oct-26	76		
FPW-090	Fire Pump and Water Supp	0	0	0%		29-Oct-26	76		
DC-HYP-FINAL-6.9.5 Smoke Detectic		119	119	0%	10-Jun-26	26-Oct-26	79		
VES-010	Install VESDA Control Units	5	5	0%	10-Jun-26	15-Jun-26	187		
VES-020	Install VESDA Sampling Pip	8	8	0%	08-Oct-26	16-Oct-26	81		
VES-030	Install VESDA Sampling Po	5	5	0%	12-Oct-26	16-Oct-26	81		
VES-040	Complete VESDA Electrical	2	2	0%	17-Oct-26	19-Oct-26	81		
VES-050	Complete VESDA Fire Alarr	2	2	0%	22-Oct-26	23-Oct-26	79		
VES-060	Inspect VESDA Installation	2	2	0%	24-Oct-26	26-Oct-26	79		
VES-070	VESDA System Ready for I	0	0	0%		26-Oct-26	79		
DC-HYP-FINAL-6.9.6 Emergency Ligl		12	12	0%	24-Dec-26	06-Jan-27	17		
EML-010	Install Emergency Lighting I	5	5	0%	25-Dec-26	30-Dec-26	21		
EML-020	Install Exit Signage	5	5	0%	25-Dec-26	30-Dec-26	21		
EML-030	Install Emergency Lighting (	5	5	0%	24-Dec-26	29-Dec-26	17		
EML-040	Install Emergency Lighting (	5	5	0%	30-Dec-26	04-Jan-27	17		
EML-050	Inspect Emergency Lighting	2	2	0%	05-Jan-27	06-Jan-27	17		
EML-060	Emergency Lighting and Ex	0	0	0%		06-Jan-27	17		
DC-HYP-FINAL-6.9.7 Fire System Inte		65	65	0%	24-Oct-26	07-Jan-27	16		
FSI-010	Install Fire Alarm Interface M	5	5	0%	24-Oct-26	29-Oct-26	67		
FSI-020	Connect Fire Alarm to Mech	5	5	0%	08-Dec-26	12-Dec-26	34		
FSI-030	Connect Fire Alarm to Elect	5	5	0%	24-Dec-26	29-Dec-26	20		
FSI-040	Connect Fire Alarm to Acce	5	5	0%	30-Oct-26	04-Nov-26	67		
FSI-050	Connect Fire Alarm to BMS	5	5	0%	29-Dec-26	02-Jan-27	16		
FSI-060	Complete Fire Cause and E	2	2	0%	04-Jan-27	05-Jan-27	16		
FSI-070	Inspect Fire System Interfac	2	2	0%	06-Jan-27	07-Jan-27	16		
FSI-080	Fire System Interfaces Rea	0	0	0%		07-Jan-27	16		
DC-HYP-FINAL-6.9.8 Life Safety Con		116	116	0%	08-Oct-26	19-Feb-27	63		
LSC-010	Conduct Internal Fire and L	2	2	0%	08-Feb-27	09-Feb-27	63		
LSC-020	Conduct Fire-Stopping Insp	2	2	0%	08-Oct-26	09-Oct-26	168		
LSC-030	Conduct Emergency Egress	2	2	0%	08-Oct-26	09-Oct-26	168		
LSC-040	Conduct Fire System Comp	5	5	0%	10-Feb-27	15-Feb-27	63		
LSC-050	Rectify Fire and Life Safety	2	2	0%	16-Feb-27	17-Feb-27	63		
LSC-060	Prepare Authority Inspectior	2	2	0%	18-Feb-27	19-Feb-27	63		
LSC-070	Fire and Life Safety System	0	0	0%		19-Feb-27	63		


© Oracle Corporation

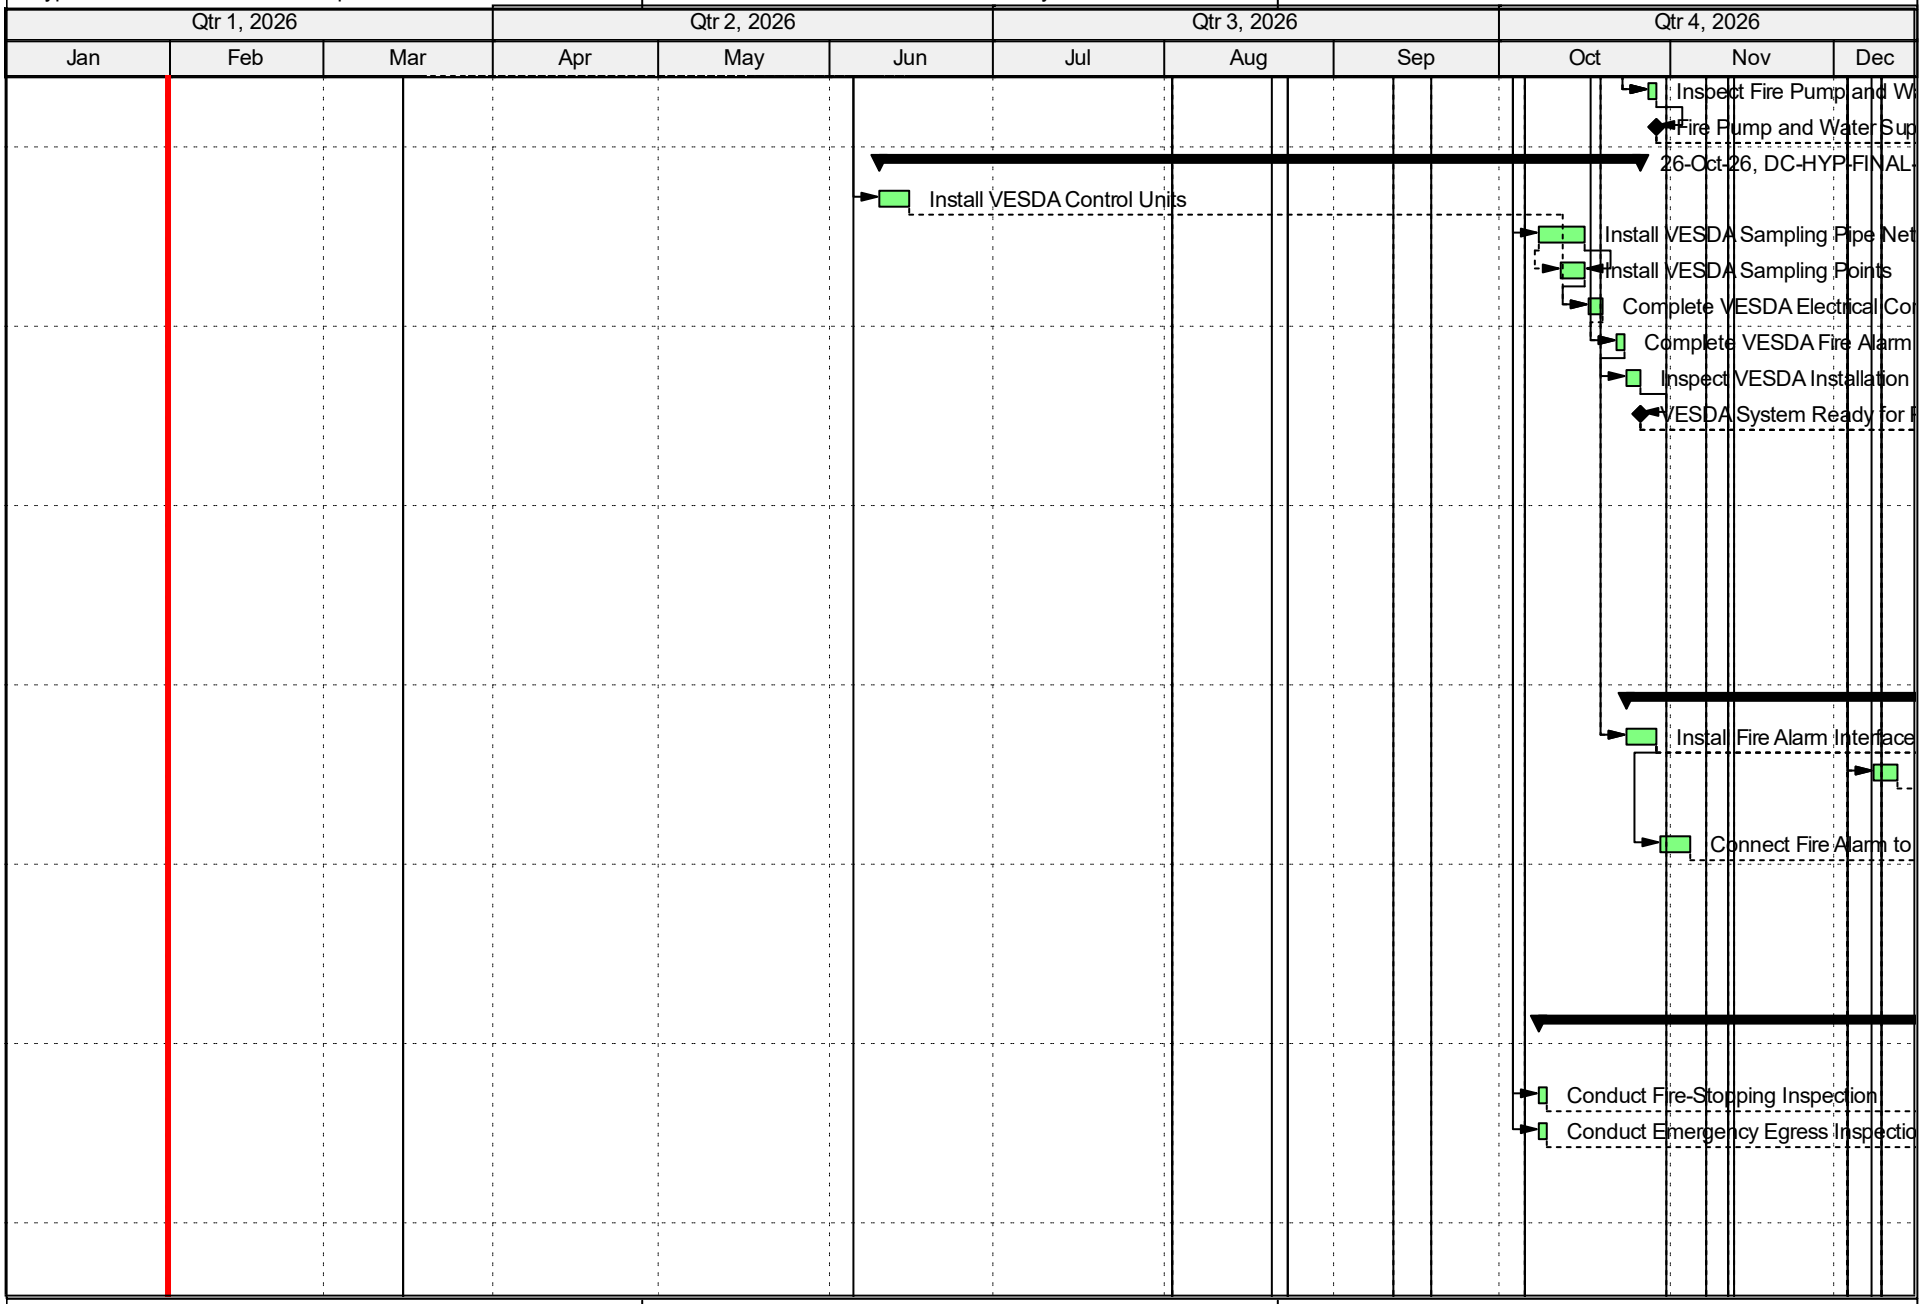

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.10	**Controls, I**	144	144	0%	07-Aug-26	21-Jan-27	28		
DC-HYP-FINAL-6.10.1	**BMS Infrastru**	68	68	0%	10-Oct-26	28-Dec-26	16		
BMSI-010	Prepare BMS Installation Ar	5	5	0%	10-Oct-26	15-Oct-26	44		
BMSI-020	Install BMS Control Panels	5	5	0%	16-Oct-26	21-Oct-26	65		
BMSI-030	Install BMS Network Infrastr	8	8	0%	16-Oct-26	24-Oct-26	44		
BMSI-040	Install BMS Field Cabling	10	10	0%	19-Oct-26	29-Oct-26	65		
BMSI-050	Complete BMS Panel Powe	2	2	0%	24-Dec-26	25-Dec-26	16		
BMSI-060	Inspect BMS Infrastructure	2	2	0%	26-Dec-26	28-Dec-26	16		
BMSI-070	BMS Infrastructure Ready f	0	0	0%		28-Dec-26	16		
DC-HYP-FINAL-6.10.2	**Electrical Mon**	47	47	0%	16-Nov-26	08-Jan-27	10		
EMC-010	Install Electrical Monitoring I	5	5	0%	16-Nov-26	20-Nov-26	50		
EMC-020	Install Power Metering Devi	5	5	0%	24-Dec-26	29-Dec-26	17		
EMC-030	Install Switchgear Monitorin	6	6	0%	16-Nov-26	21-Nov-26	49		
EMC-040	Install UPS Monitoring Inter	5	5	0%	01-Jan-27	06-Jan-27	10		
EMC-050	Install Generator Monitoring	6	6	0%	12-Dec-26	18-Dec-26	26		
EMC-060	Complete Monitoring Comr	2	2	0%	07-Jan-27	08-Jan-27	10		
EMC-070	Electrical Monitoring Ready	0	0	0%		08-Jan-27	10		
DC-HYP-FINAL-6.10.3	**Mechanical Mo**	77	77	0%	16-Sep-26	14-Dec-26	32		
MMC-010	Install Mechanical Monitorir	4	4	0%	08-Dec-26	11-Dec-26	32		
MMC-020	Connect Chiller Monitoring	5	5	0%	23-Sep-26	28-Sep-26	96		
MMC-030	Connect Pump Monitoring I	5	5	0%	16-Sep-26	21-Sep-26	102		
MMC-040	Connect CRAH CRAC Mor	5	5	0%	05-Nov-26	10-Nov-26	59		
MMC-050	Connect Cooling Sensors t	5	5	0%	17-Nov-26	21-Nov-26	49		
MMC-060	Verify Mechanical Control W	2	2	0%	12-Dec-26	14-Dec-26	32		
MMC-070	Mechanical Monitoring Rea	0	0	0%		14-Dec-26	32		
DC-HYP-FINAL-6.10.4	**DCIM Platform**	55	55	0%	12-Nov-26	14-Jan-27	10		
DCIM-010	Install DCIM Server Infrastr	5	5	0%	12-Nov-26	17-Nov-26	44		
DCIM-020	Configure DCIM Platform	8	8	0%	18-Nov-26	26-Nov-26	44		
DCIM-030	Configure Data Hall Asset I	8	8	0%	27-Nov-26	05-Dec-26	44		
DCIM-040	Configure Power Monitoring	5	5	0%	09-Jan-27	14-Jan-27	10		
DCIM-050	Configure Cooling Monitori	5	5	0%	15-Dec-26	19-Dec-26	32		
DCIM-060	Configure Alarm and Event	5	5	0%	27-Nov-26	02-Dec-26	47		
DCIM-070	DCIM Platform Ready for F	0	0	0%		14-Jan-27	10		


© Oracle Corporation

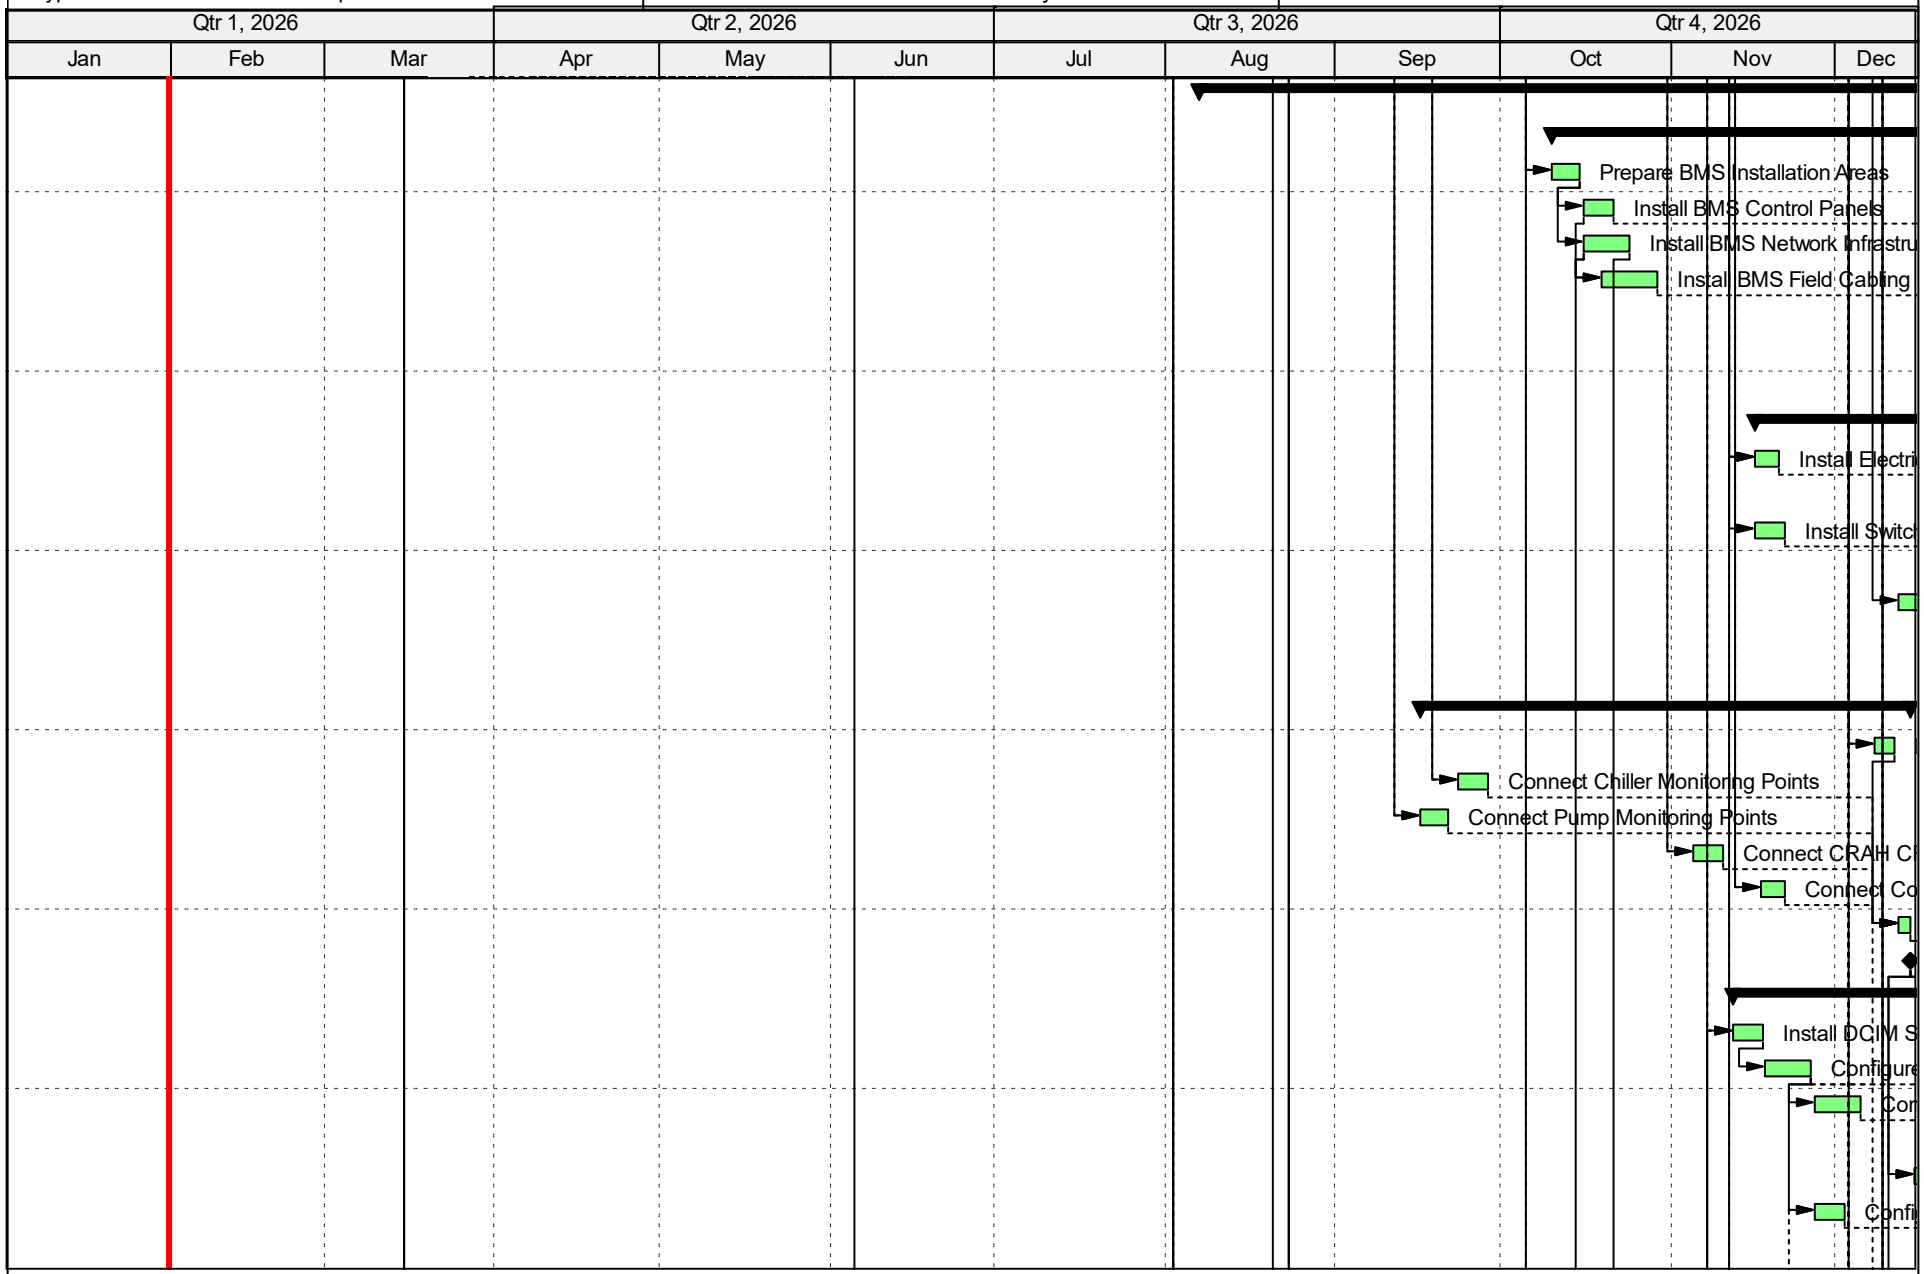

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.10.5	**Sensors & Fiel**	36	36	0%	10-Oct-26	20-Nov-26	57		
SFD-010	Install Environmental Sensc	5	5	0%	10-Oct-26	15-Oct-26	79		
SFD-020	Install Temperature and Hu	5	5	0%	12-Oct-26	16-Oct-26	79		
SFD-030	Install Differential Pressure	5	5	0%	12-Oct-26	16-Oct-26	79		
SFD-040	Install Leak Detection Sens	5	5	0%	12-Oct-26	16-Oct-26	79		
SFD-050	Install Energy Metering Dev	5	5	0%	12-Oct-26	16-Oct-26	79		
SFD-060	Terminate Sensor and Field	8	8	0%	12-Nov-26	20-Nov-26	57		
SFD-070	Sensors and Field Devices	0	0	0%		20-Nov-26	57		
DC-HYP-FINAL-6.10.6	**Controls Netw**	21	21	0%	19-Oct-26	11-Nov-26	44		
CNW-010	Install Controls Network Sw	5	5	0%	26-Oct-26	30-Oct-26	44		
CNW-020	Install Controls Network Ca	8	8	0%	19-Oct-26	27-Oct-26	47		
CNW-030	Configure Controls Network	4	4	0%	31-Oct-26	04-Nov-26	44		
CNW-040	Configure Network Segmer	3	3	0%	05-Nov-26	07-Nov-26	44		
CNW-050	Perform Controls Network C	3	3	0%	09-Nov-26	11-Nov-26	44		
CNW-060	Controls Network Ready	0	0	0%		11-Nov-26	44		
DC-HYP-FINAL-6.10.7	**System Integra**	21	21	0%	29-Dec-26	21-Jan-27	28		
CSI-010	Integrate BMS with Electrica	4	4	0%	09-Jan-27	13-Jan-27	33		
CSI-020	Integrate BMS with Mechar	4	4	0%	29-Dec-26	01-Jan-27	43		
CSI-030	Integrate BMS with Fire Alai	3	3	0%	08-Jan-27	11-Jan-27	35		
CSI-040	Integrate BMS with UPS ar	4	4	0%	09-Jan-27	13-Jan-27	33		
CSI-050	Integrate DCIM with Power	4	4	0%	15-Jan-27	19-Jan-27	28		
CSI-060	Integrate DCIM with Coolin	4	4	0%	15-Jan-27	19-Jan-27	28		
CSI-070	Verify System Integration In	2	2	0%	20-Jan-27	21-Jan-27	28		
CSI-080	Controls Integration Ready	0	0	0%		21-Jan-27	28		
DC-HYP-FINAL-6.10.8	**Graphics, Con**	13	13	0%	07-Aug-26	21-Aug-26	130		
GCP-010	Develop BMS Control Logic	8	8	0%	07-Aug-26	15-Aug-26	130		
GCP-020	Configure BMS Alarm Logic	5	5	0%	10-Aug-26	14-Aug-26	133		
GCP-030	Develop BMS Graphics	8	8	0%	10-Aug-26	18-Aug-26	130		
GCP-040	Configure DCIM Dashboar	5	5	0%	10-Aug-26	14-Aug-26	133		
GCP-050	Configure Trend Logging ar	4	4	0%	10-Aug-26	13-Aug-26	134		
GCP-060	Complete Controls Softwar	3	3	0%	19-Aug-26	21-Aug-26	130		
GCP-070	BMS and DCIM Configurat	0	0	0%		21-Aug-26	130		
DC-HYP-FINAL-6.11	**Utility Con**	229	229	0%	20-Mar-26	03-Feb-27	0		

© Oracle Corporation

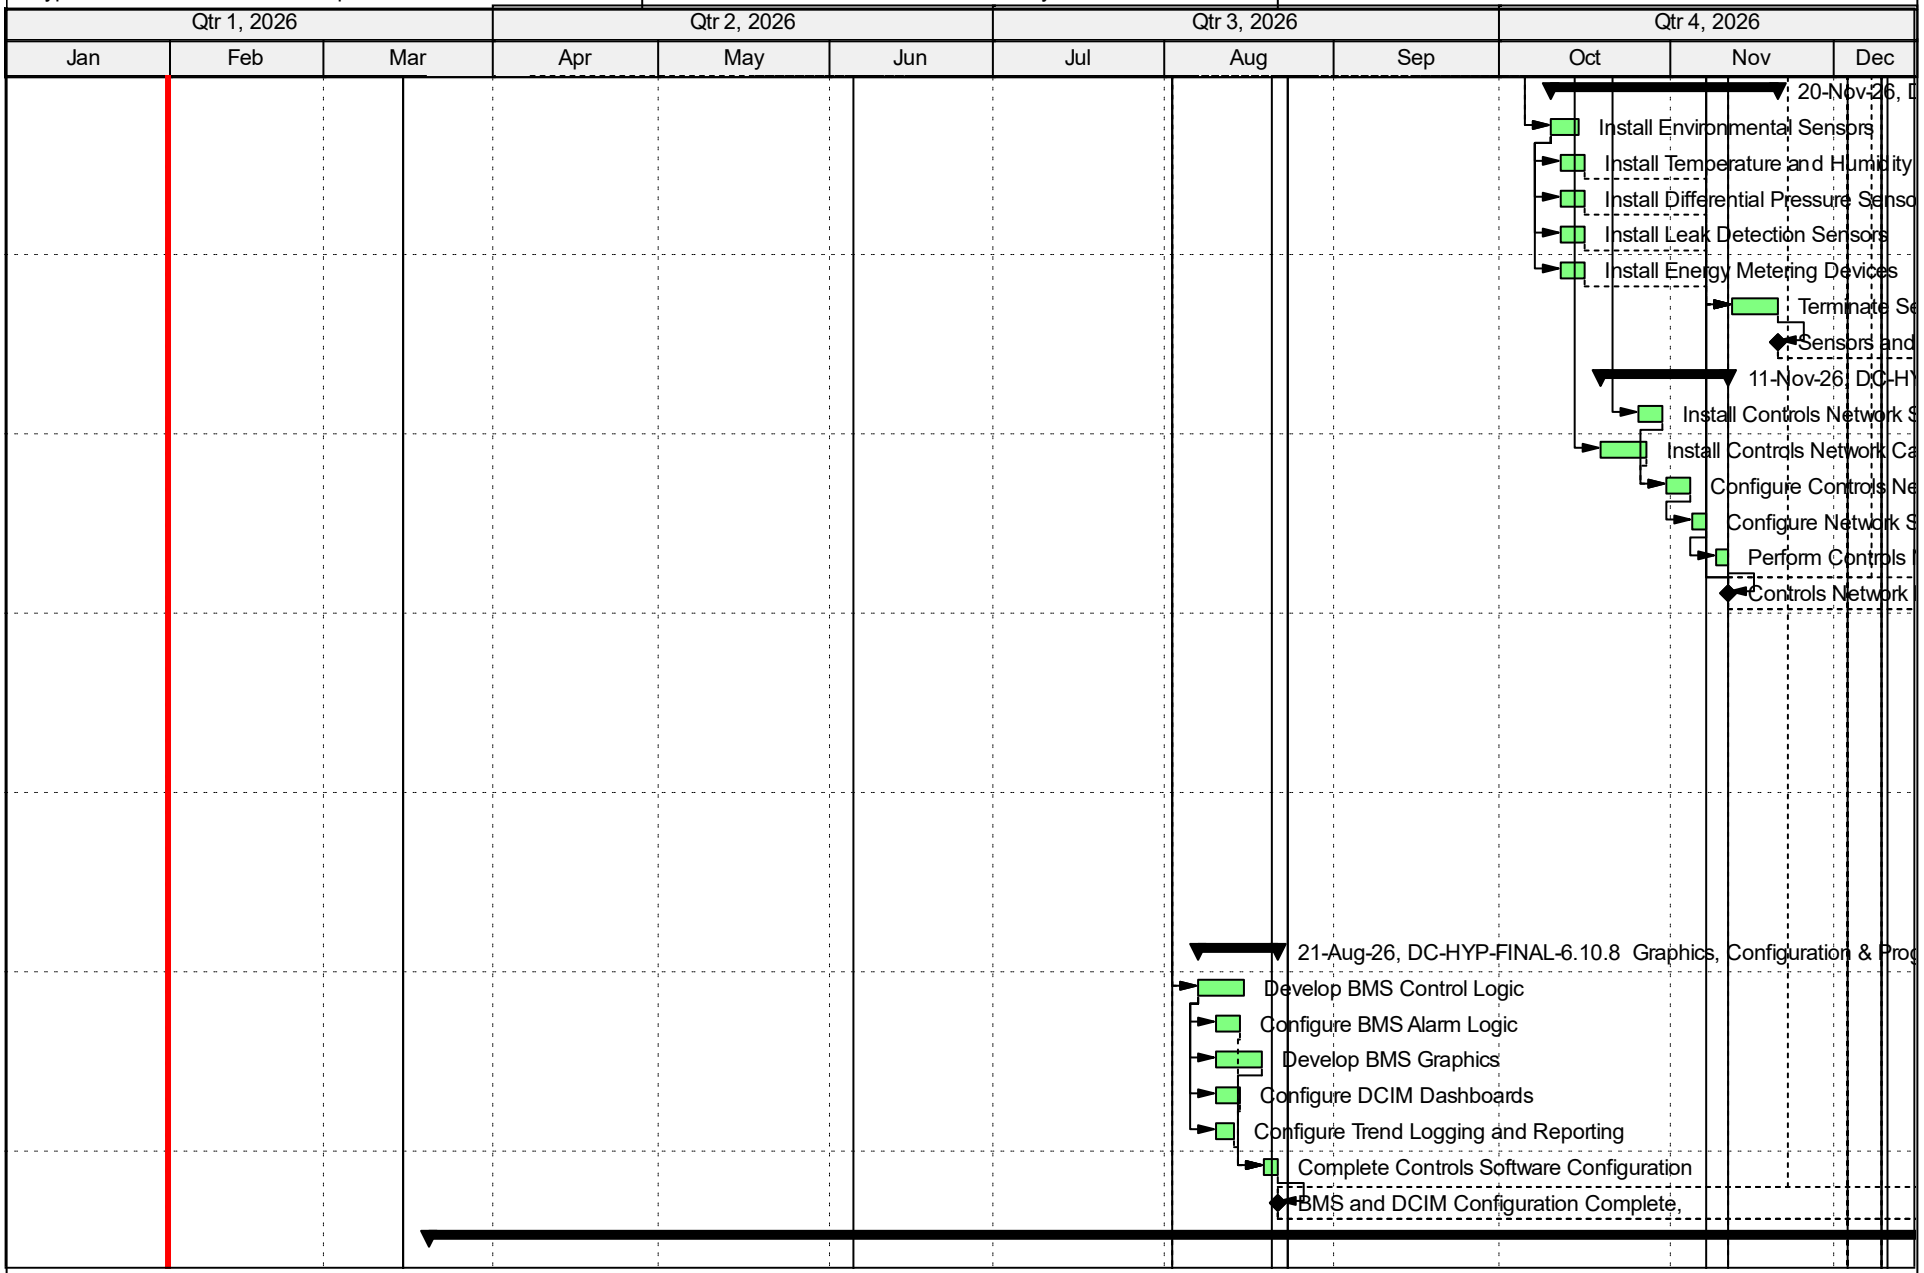


Actual Level of Effort
Actual Work
Remaining Work
Critical Remainin...

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
DC-HYP-FINAL-6.11.1	**Utility Coordin**	25	25	0%	20-Mar-26	17-Apr-26	177		
UTL-010	Submit Utility Connection A	5	5	0%	20-Mar-26	25-Mar-26	177		
UTL-020	Coordinate Utility Technical	10	10	0%	26-Mar-26	06-Apr-26	177		
UTL-030	Submit Utility Protection Stu	10	10	0%	26-Mar-26	06-Apr-26	177		
UTL-040	Resolve Utility Review Com	10	10	0%	07-Apr-26	17-Apr-26	177		
UTL-050	Obtain Utility Connection Ap	0	0	0%		17-Apr-26	177		
DC-HYP-FINAL-6.11.2	**Incoming Utilit**	20	20	0%	18-Apr-26	11-May-26	177		
UCMV-01	Complete Incoming Utility M	15	15	0%	18-Apr-26	05-May-26	177		
UCMV-02	Install Utility Metering Equip	5	5	0%	22-Apr-26	27-Apr-26	189		
UCMV-03	Complete Utility MV Cable	5	5	0%	06-May-26	11-May-26	177		
UCMV-04	Complete Utility Protection	5	5	0%	24-Apr-26	29-Apr-26	187		
UCMV-05	Incoming Utility Connection	0	0	0%		11-May-26	177		
DC-HYP-FINAL-6.11.3	**Utility Substati**	10	10	0%	12-May-26	22-May-26	177		
SUB-010	Inspect Utility Substation In	2	2	0%	12-May-26	13-May-26	177		
SUB-020	Complete Substation Prote	3	3	0%	14-May-26	16-May-26	177		
SUB-030	Complete Substation Meter	3	3	0%	14-May-26	16-May-26	177		
SUB-040	Close Utility Substation Pur	5	5	0%	18-May-26	22-May-26	177		
SUB-050	Utility Substation Ready for	0	0	0%		22-May-26	177		
DC-HYP-FINAL-6.11.4	**MV System En**	9	9	0%	16-Nov-26	25-Nov-26	26		
MVE-010	Complete MV Pre-Energiza	2	2	0%	16-Nov-26	17-Nov-26	26		
MVE-020	Verify MV Protection Setting	2	2	0%	18-Nov-26	19-Nov-26	26		
MVE-030	Obtain MV Energization Pe	2	2	0%	20-Nov-26	21-Nov-26	26		
MVE-040	Energize Incoming MV Syst	1	1	0%	23-Nov-26	23-Nov-26	26		
MVE-050	Verify MV System Operation	2	2	0%	24-Nov-26	25-Nov-26	26		
MVE-060	MV System Energized	0	0	0%		25-Nov-26	26		
DC-HYP-FINAL-6.11.6	**LV System En**	6	6	0%	26-Dec-26	01-Jan-27	0		
TRE-010	Complete Transformer Pre-I	1	1	0%	26-Dec-26	26-Dec-26	0		
TRE-020	Verify Transformer Protectio	2	2	0%	28-Dec-26	29-Dec-26	0		
TRE-030	Energize Transformers	1	1	0%	30-Dec-26	30-Dec-26	0		
TRE-040	Perform Transformer Opera	2	2	0%	31-Dec-26	01-Jan-27	0		
TRE-050	Transformers Energized	0	0	0%		01-Jan-27	0		
DC-HYP-FINAL-6.11.7	**UPS & Critical**	9	9	0%	02-Jan-27	12-Jan-27	0		
LVE-010	Complete LV Pre-Energizat	1	1	0%	02-Jan-27	02-Jan-27	0		
LVE-020	Verify LV Protection Setting	2	2	0%	04-Jan-27	05-Jan-27	0		


© Oracle Corporation

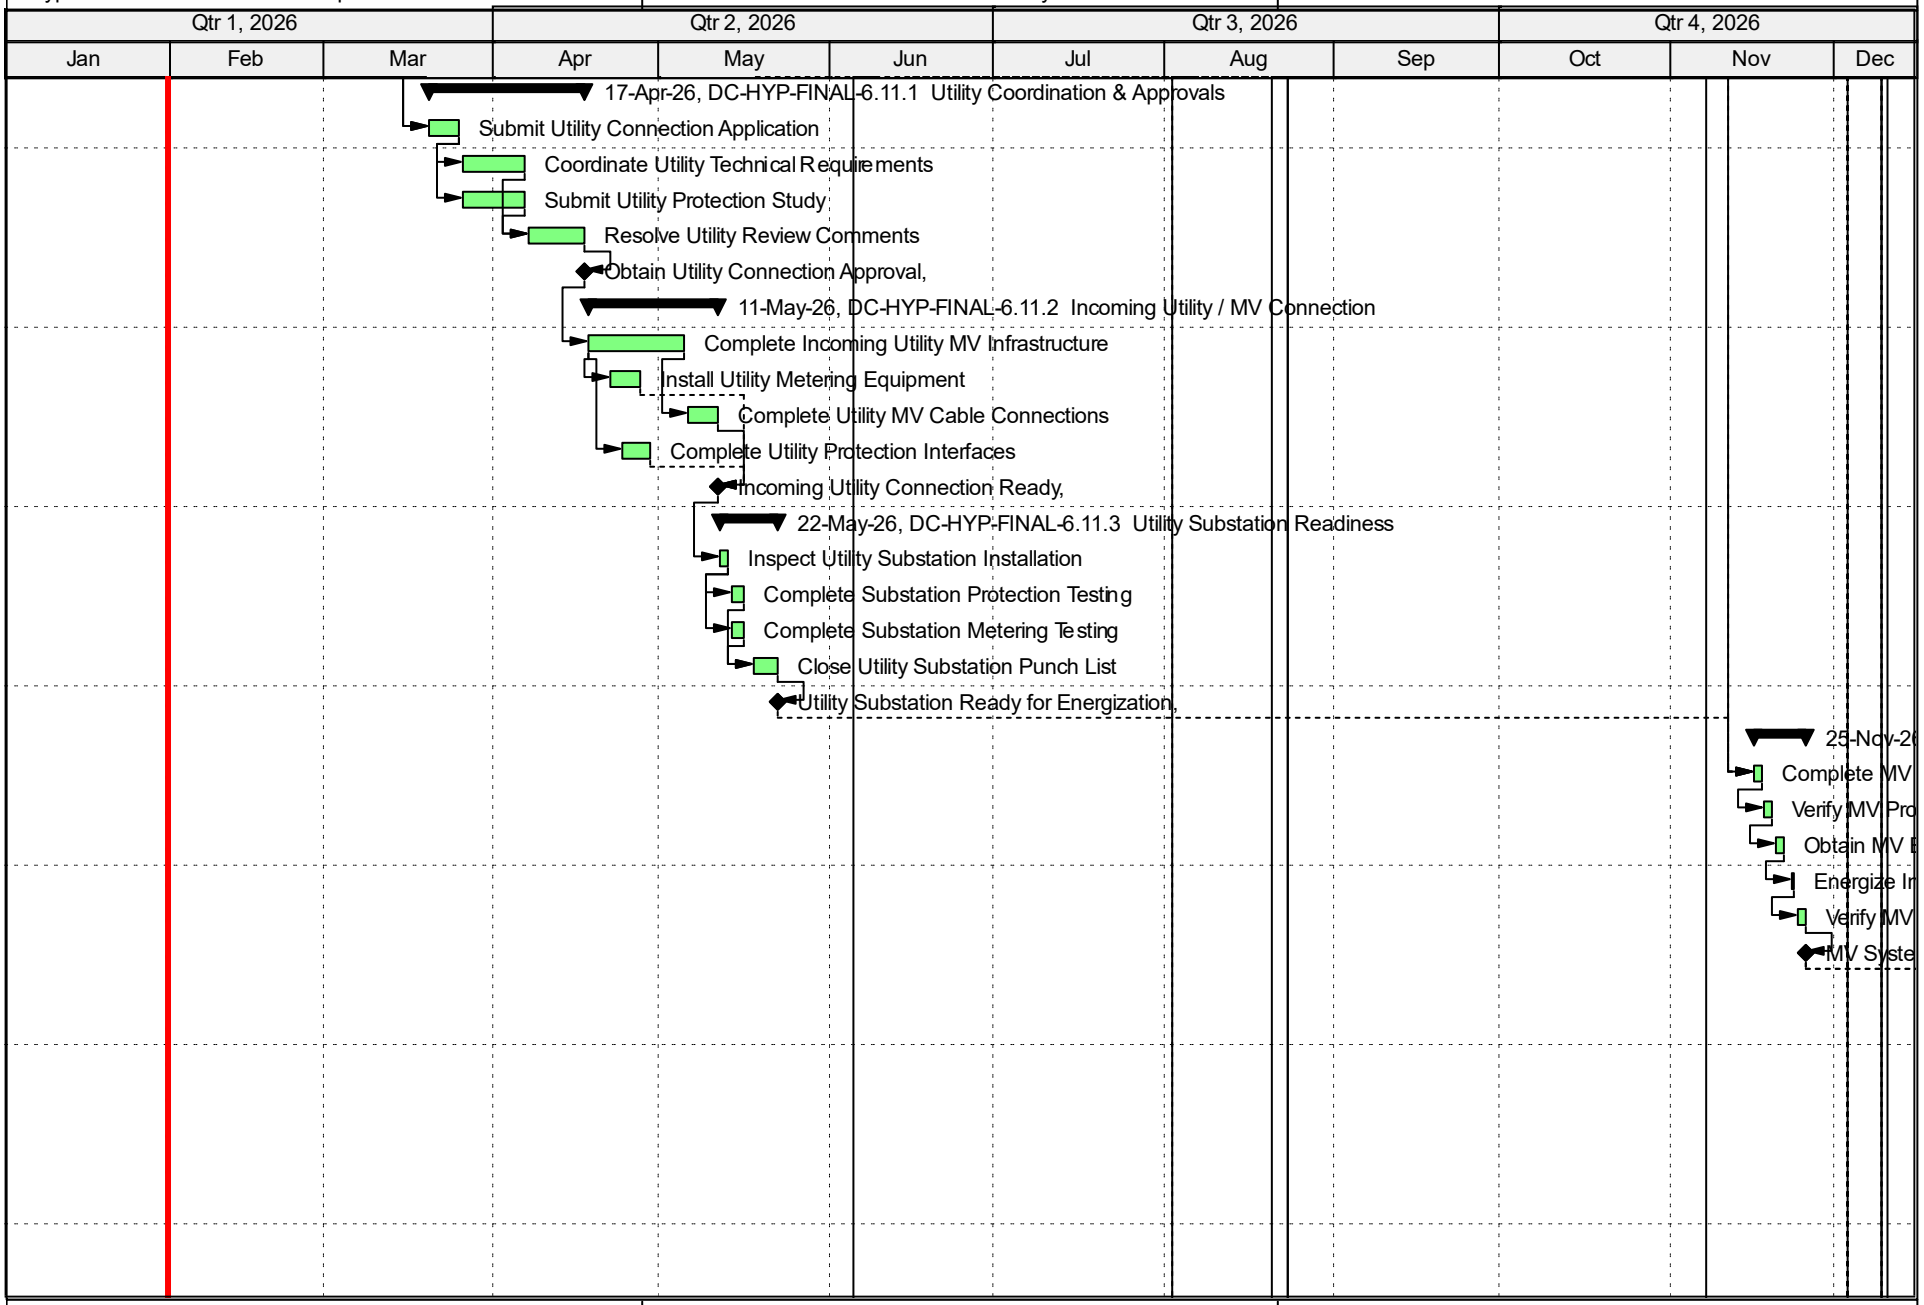

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
LVE-030	Energize Main LV Switchge	1	1	0%	06-Jan-27	06-Jan-27	0		
LVE-040	Energize LV Distribution Bo	3	3	0%	07-Jan-27	09-Jan-27	0		
LVE-050	Verify LV System Operation	2	2	0%	11-Jan-27	12-Jan-27	0		
LVE-060	LV System Energized	0	0	0%		12-Jan-27	0		
DC-HYP-FINAL-6.11.8 Generator & Ba		10	10	0%	13-Jan-27	23-Jan-27	0		
UPE-010	Complete UPS Pre-Energiz	1	1	0%	13-Jan-27	13-Jan-27	0		
UPE-020	Energize UPS Input Supply	1	1	0%	14-Jan-27	14-Jan-27	0		
UPE-030	Start and Configure UPS S	3	3	0%	15-Jan-27	18-Jan-27	0		
UPE-040	Energize UPS Output Distri	3	3	0%	19-Jan-27	21-Jan-27	0		
UPE-050	Verify Battery System Opera	2	2	0%	22-Jan-27	23-Jan-27	0		
UPE-060	Critical Power System Ener	0	0	0%		23-Jan-27	0		
DC-HYP-FINAL-6.11.9 Data Hall Powe		31	31	0%	30-Dec-26	03-Feb-27	0		
DPO-010	Verify Data Hall Electrical In	2	2	0%	25-Jan-27	26-Jan-27	0		
DPO-020	Verify UPS and PDU Availa	2	2	0%	25-Jan-27	26-Jan-27	0		
DPO-030	Verify Data Hall Earthing ar	2	2	0%	30-Dec-26	31-Dec-26	22		
DPO-040	Energize Data Hall Busway	2	2	0%	27-Jan-27	28-Jan-27	0		
DPO-050	Energize Data Hall Power D	3	3	0%	29-Jan-27	01-Feb-27	0		
DPO-060	Verify Data Hall Power Avai	2	2	0%	02-Feb-27	03-Feb-27	0		
DPO-070	Data Hall Power-On Compl	0	0	0%		03-Feb-27	0		
GBP-010	Complete Generator Pre-St	1	1	0%	31-Dec-26	31-Dec-26	23		
GBP-020	Complete Generator Fuel S	1	1	0%	31-Dec-26	31-Dec-26	23		
GBP-030	Start Standby Generators	2	2	0%	01-Jan-27	02-Jan-27	23		
GBP-040	Verify Generator Controls a	2	2	0%	04-Jan-27	05-Jan-27	23		
GBP-050	Verify Generator Automatic	2	2	0%	13-Jan-27	14-Jan-27	17		
GBP-060	Backup Power System Rea	0	0	0%		14-Jan-27	17		
DC-HYP-FINAL-6.11.5 Transformer E		0	0	0%			0		
DC-HYP-FINAL-6.12 Testing & (		409	386	0%	06-Jan-26	27-Apr-27	0		
DC-HYP-FINAL-6.12.1 Commissionin		15	0	0%	06-Jan-26	22-Jan-26			
CXP-010	Develop Commissioning Ma	5	0	100%	06-Jan-26	10-Jan-26			
CXP-020	Develop Commissioning Sc	5	0	100%	12-Jan-26	16-Jan-26			
CXP-030	Develop Commissioning Pr	5	0	100%	12-Jan-26	16-Jan-26			
CXP-040	Develop Systems Completi	5	0	100%	12-Jan-26	16-Jan-26			
CXP-050	Establish Commissioning D	10	0	100%	12-Jan-26	22-Jan-26			


© Oracle Corporation

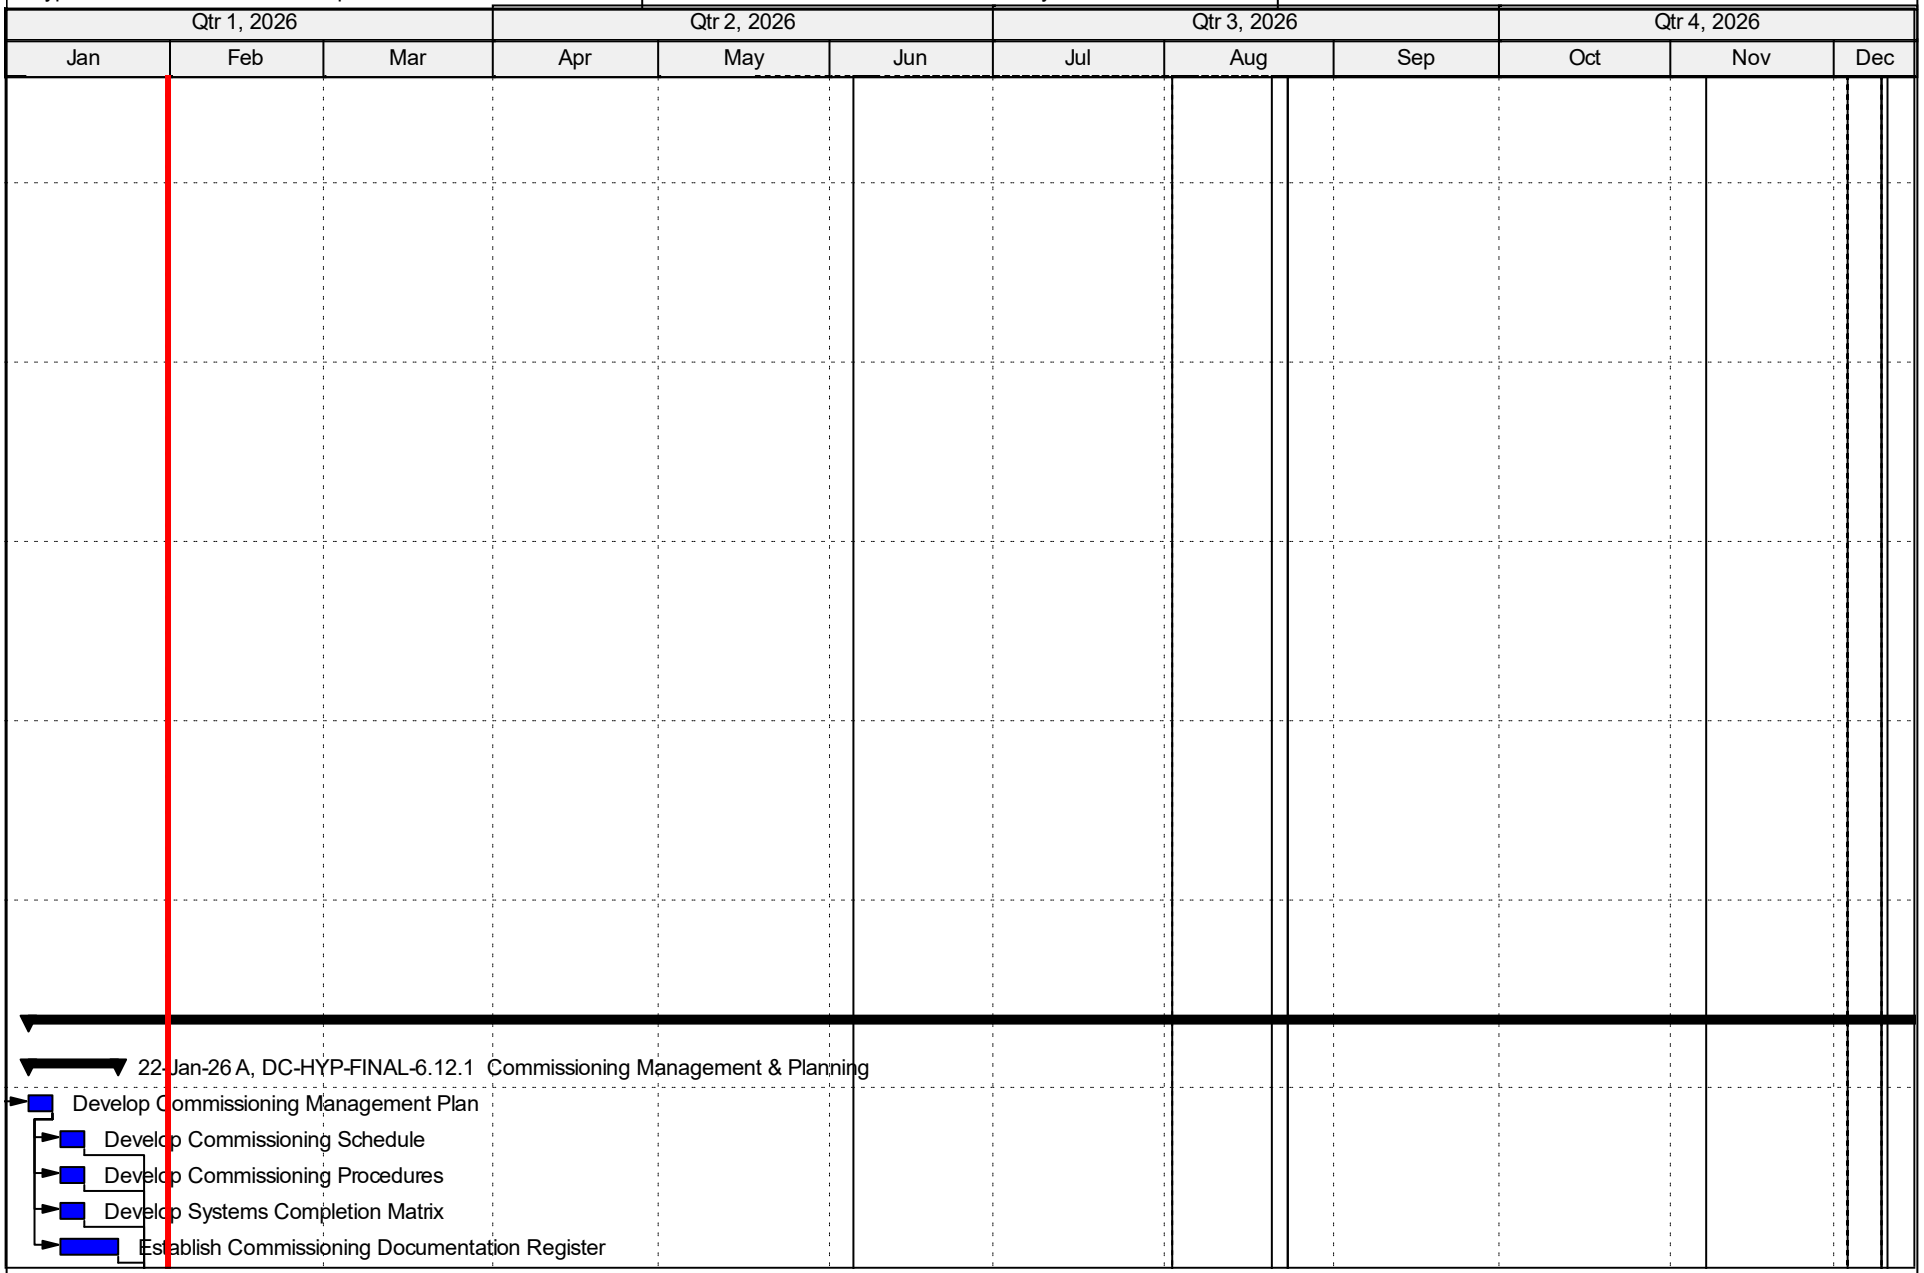

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
CXP-060	Commissioning Plan Appro	0	0	100%		22-Jan-26			
DC-HYP-FINAL-6.12.2 Pre-Commissi		46	46	0%	08-Dec-26	29-Jan-27	2		
PRE-010	Complete Electrical Pre-Co	2	2	0%	25-Jan-27	26-Jan-27	2		
PRE-020	Complete Mechanical Pre-(	2	2	0%	08-Dec-26	09-Dec-26	43		
PRE-030	Complete Fire System Pre-	2	2	0%	08-Jan-27	09-Jan-27	16		
PRE-040	Complete BMS and Contro	2	2	0%	15-Jan-27	16-Jan-27	10		
PRE-050	Complete Pre-Commissioni	3	3	0%	27-Jan-27	29-Jan-27	2		
PRE-060	Systems Ready for Functio	0	0	0%		29-Jan-27	2		
DC-HYP-FINAL-6.12.3 Electrical Syst		14	14	0%	30-Jan-27	15-Feb-27	0		
ELC-CX-(	Commission MV Switchgea	5	5	0%	04-Feb-27	09-Feb-27	5		
ELC-CX-(	Commission Transformers	5	5	0%	30-Jan-27	04-Feb-27	9		
ELC-CX-(	Commission LV Switchgear	5	5	0%	30-Jan-27	04-Feb-27	9		
ELC-CX-(	Commission UPS Systems	5	5	0%	30-Jan-27	04-Feb-27	9		
ELC-CX-(	Commission Battery Syster	5	5	0%	30-Jan-27	04-Feb-27	9		
ELC-CX-(	Commission Standby Gene	5	5	0%	30-Jan-27	04-Feb-27	9		
ELC-CX-(	Commission PDU and Bus	10	10	0%	04-Feb-27	15-Feb-27	0		
ELC-CX-(	Electrical Systems Function	0	0	0%		15-Feb-27	0		
DC-HYP-FINAL-6.12.4 Mechanical & (		12	12	0%	30-Jan-27	12-Feb-27	2		
MEC-CX-	Commission Chillers and H	5	5	0%	30-Jan-27	04-Feb-27	2		
MEC-CX-	Commission Cooling Pump	5	5	0%	30-Jan-27	04-Feb-27	2		
MEC-CX-	Commission Chilled Water	5	5	0%	30-Jan-27	04-Feb-27	2		
MEC-CX-	Commission CRAH CRAC	5	5	0%	30-Jan-27	04-Feb-27	2		
MEC-CX-	Perform Air and Water Bala	5	5	0%	05-Feb-27	10-Feb-27	2		
MEC-CX-	Verify Cooling System Cont	2	2	0%	11-Feb-27	12-Feb-27	2		
MEC-CX-	Mechanical Systems Functi	0	0	0%		12-Feb-27	2		
DC-HYP-FINAL-6.12.5 Fire & Life Saf		7	7	0%	30-Jan-27	06-Feb-27	10		
FLS-CX-(	Commission Fire Detection	5	5	0%	30-Jan-27	04-Feb-27	10		
FLS-CX-(	Commission Sprinkler Syste	5	5	0%	30-Jan-27	04-Feb-27	10		
FLS-CX-(	Commission Clean Agent F	5	5	0%	30-Jan-27	04-Feb-27	10		
FLS-CX-(	Commission Fire Pumps	5	5	0%	30-Jan-27	04-Feb-27	10		
FLS-CX-(	Commission VESDA Syster	5	5	0%	30-Jan-27	04-Feb-27	10		
FLS-CX-(	Verify Fire Cause and Effec	2	2	0%	05-Feb-27	06-Feb-27	10		
FLS-CX-(	Fire and Life Safety Commi	0	0	0%		06-Feb-27	10		
DC-HYP-FINAL-6.12.6 BMS & DCIM (		16	16	0%	30-Jan-27	17-Feb-27	1		

© Oracle Corporation

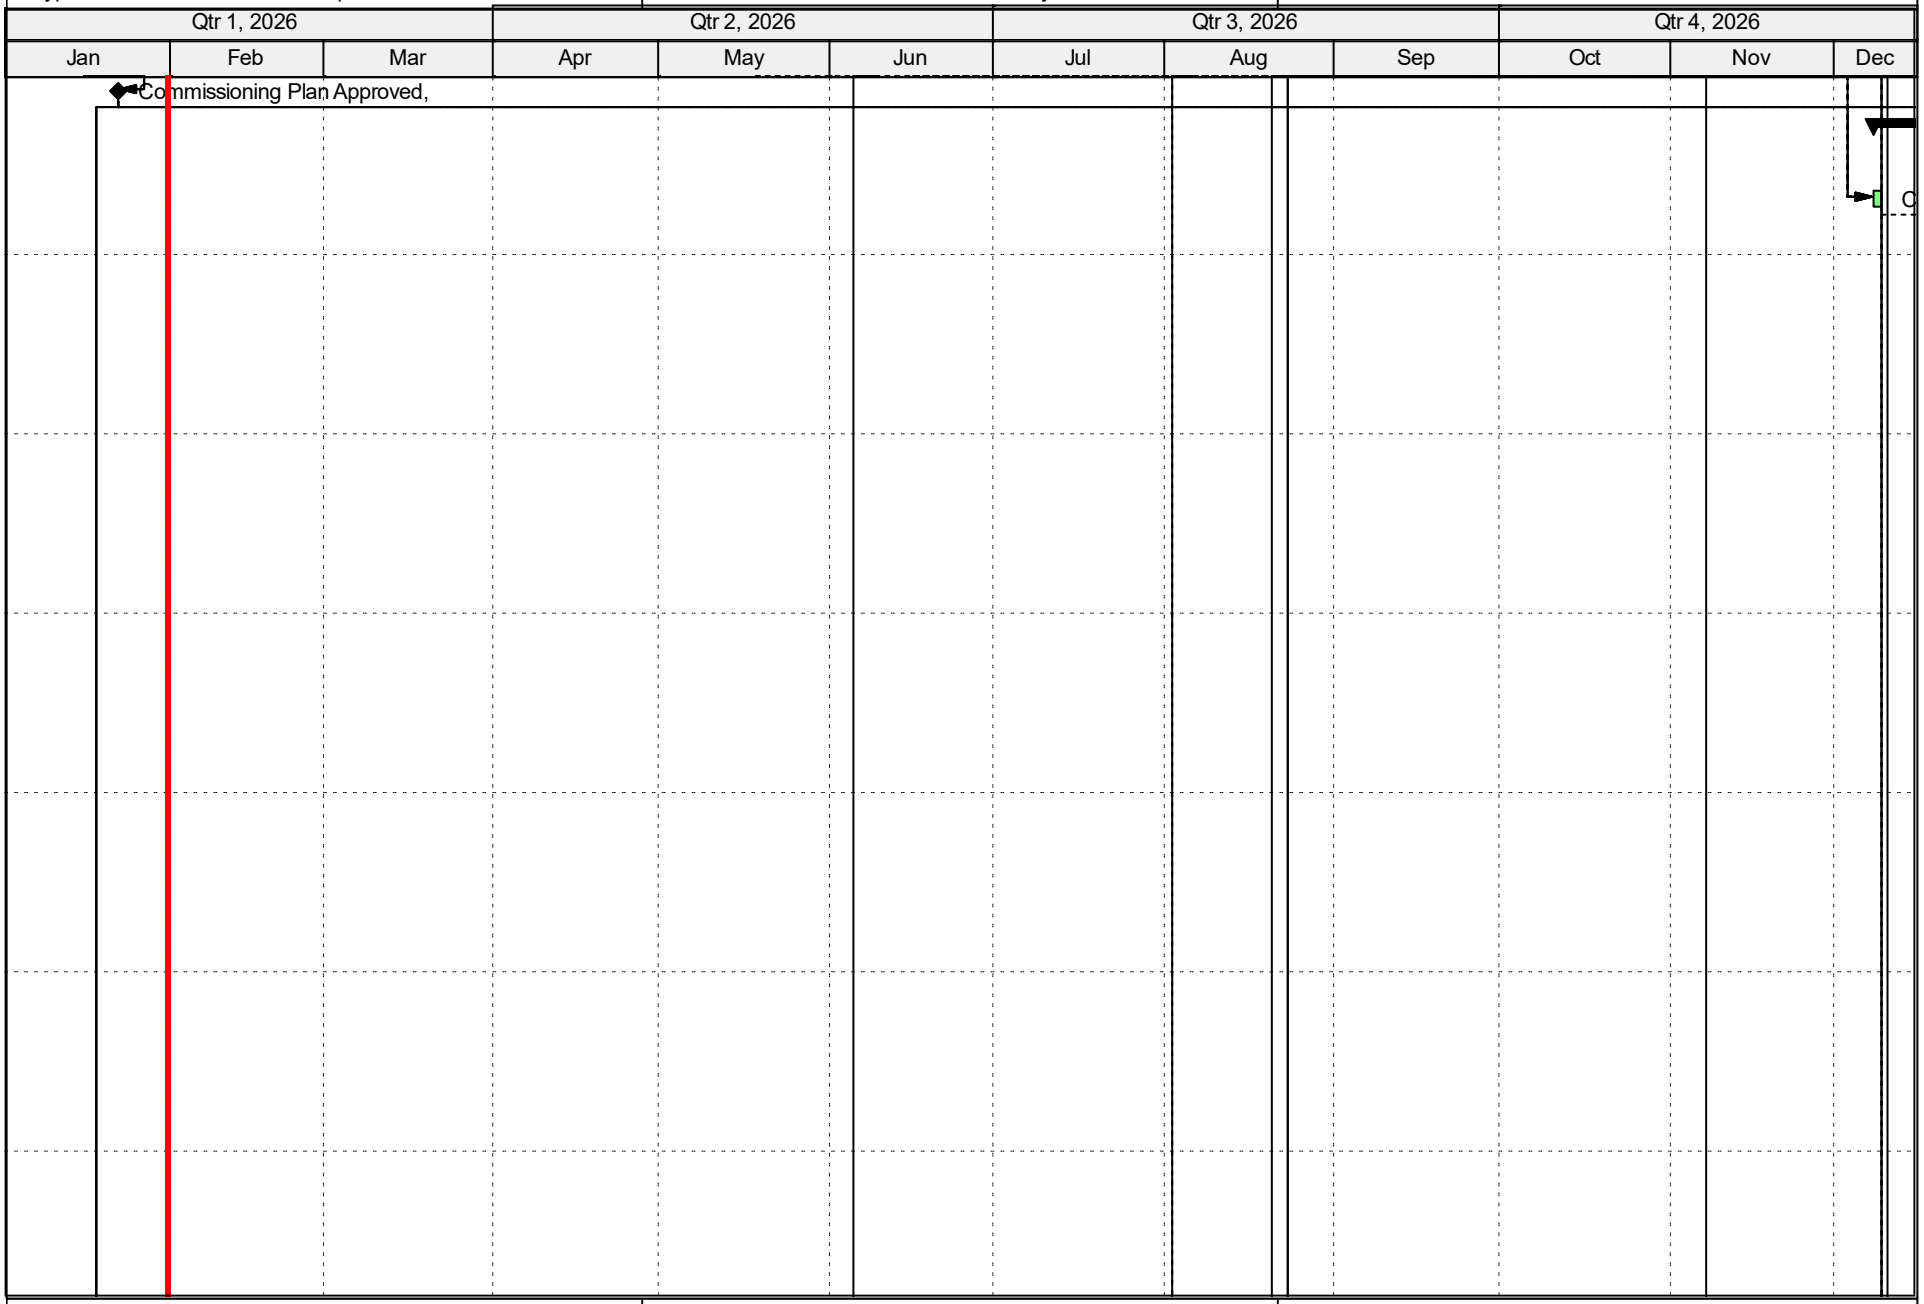

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
BMS-CX-	Commission BMS Infrastruc	5	5	0%	30-Jan-27	04-Feb-27	5		
BMS-CX-	Verify BMS Field Points	2	2	0%	05-Feb-27	06-Feb-27	5		
BMS-CX-	Commission BMS Graphics	5	5	0%	08-Feb-27	12-Feb-27	5		
BMS-CX-	Commission DCIM Platform	5	5	0%	30-Jan-27	04-Feb-27	10		
BMS-CX-	Verify DCIM Power Monitori	2	2	0%	16-Feb-27	17-Feb-27	1		
BMS-CX-	Verify DCIM Cooling Monitc	2	2	0%	13-Feb-27	15-Feb-27	3		
BMS-CX-	BMS and DCIM Commissic	0	0	0%		17-Feb-27	1		
DC-HYP-FINAL-6.12.7 Controls & Sy		4	4	0%	18-Feb-27	22-Feb-27	1		
INT-CX-0	Verify Electrical to BMS Inte	2	2	0%	18-Feb-27	19-Feb-27	1		
INT-CX-0	Verify Mechanical to BMS I	2	2	0%	18-Feb-27	19-Feb-27	1		
INT-CX-0	Verify Fire System Integratic	2	2	0%	18-Feb-27	19-Feb-27	1		
INT-CX-0	Verify UPS and Generator (	2	2	0%	18-Feb-27	19-Feb-27	1		
INT-CX-0	Complete Integrated Contr	2	2	0%	20-Feb-27	22-Feb-27	1		
INT-CX-0	Systems Integration Compl	0	0	0%		22-Feb-27	1		
DC-HYP-FINAL-6.12.8 Integrated Sys		355	347	0%	23-Jan-26	12-Mar-27	0		
IST-010	Prepare Integrated System	10	4	80%	23-Jan-26	05-Feb-26	328		
IST-020	Conduct Utility Power Failur	5	5	0%	24-Feb-27	01-Mar-27	0		
IST-030	Conduct Generator Transfe	5	5	0%	24-Feb-27	01-Mar-27	0		
IST-040	Conduct UPS Battery Ride-	5	5	0%	24-Feb-27	01-Mar-27	0		
IST-050	Conduct Cooling Failure Sc	5	5	0%	24-Feb-27	01-Mar-27	0		
IST-060	Conduct Fire Alarm Integrat	5	5	0%	24-Feb-27	01-Mar-27	0		
IST-070	Conduct BMS DCIM Alarm	3	3	0%	24-Feb-27	26-Feb-27	2		
IST-080	Resolve IST Deficiencies	10	10	0%	02-Mar-27	12-Mar-27	0		
IST-090	Integrated Systems Testing	0	0	0%		12-Mar-27	0		
DC-HYP-FINAL-6.12.9 Load Bank & F		17	17	0%	04-Feb-27	23-Feb-27	0		
LBT-010	Mobilize Load Bank Equipn	5	5	0%	04-Feb-27	09-Feb-27	0		
LBT-020	Connect Load Bank Equipr	5	5	0%	10-Feb-27	15-Feb-27	0		
LBT-030	Perform UPS Load Bank Te	5	5	0%	16-Feb-27	20-Feb-27	0		
LBT-040	Perform Generator Load Ba	5	5	0%	16-Feb-27	20-Feb-27	0		
LBT-050	Perform Cooling Performan	5	5	0%	16-Feb-27	20-Feb-27	0		
LBT-060	Verify Data Hall Environmer	2	2	0%	22-Feb-27	23-Feb-27	0		
LBT-070	Load Bank and Performanc	0	0	0%		23-Feb-27	0		
DC-HYP-FINAL-6.12.10 Reliability / R		367	359	0%	23-Jan-26	26-Mar-27	0		
RRT-010	Develop Reliability Test Pla	10	4	80%	23-Jan-26	05-Feb-26	343		


© Oracle Corporation



© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
RRT-020	Perform Utility Loss Resilier	10	10	0%	13-Mar-27	24-Mar-27	0		
RRT-030	Perform Generator Failure S	5	5	0%	13-Mar-27	18-Mar-27	5		
RRT-040	Perform UPS Failure Simula	5	5	0%	13-Mar-27	18-Mar-27	5		
RRT-050	Perform Cooling Failure Sin	5	5	0%	13-Mar-27	18-Mar-27	5		
RRT-060	Complete Reliability Demor	2	2	0%	25-Mar-27	26-Mar-27	0		
RRT-070	Reliability Testing Complete	0	0	0%		26-Mar-27	0		
DC-HYP-FINAL-6.12.11 Commissioni		27	27	0%	27-Mar-27	27-Apr-27	0		
CXC-010	Compile Commissioning De	10	10	0%	27-Mar-27	07-Apr-27	0		
CXC-020	Rectify Electrical Commissi	5	5	0%	08-Apr-27	13-Apr-27	2		
CXC-030	Rectify Mechanical Commis	5	5	0%	08-Apr-27	13-Apr-27	2		
CXC-040	Rectify Controls and BMS D	7	7	0%	08-Apr-27	15-Apr-27	0		
CXC-050	Rectify Fire System Defects	7	7	0%	08-Apr-27	15-Apr-27	0		
CXC-060	Close Commissioning Punc	10	10	0%	16-Apr-27	27-Apr-27	0		
CXC-070	Commissioning Complete	0	0	0%		27-Apr-27	0		
DC-HYP-FINAL-6.13 Client Acc		387	289	0%	23-Jan-26	19-Jul-27	0		
DC-HYP-FINAL-6.13.1 Punch List / S		24	24	0%	28-Apr-27	31-May-27	0		
HND-010	Conduct Client Pre-Handov	2	2	0%	28-Apr-27	29-Apr-27	0		
HND-020	Prepare Final Punch List	10	10	0%	30-Apr-27	13-May-27	0		
HND-030	Rectify Final Punch List Iter	10	10	0%	14-May-27	27-May-27	0		
HND-040	Verify Punch List Closure	2	2	0%	28-May-27	31-May-27	0		
DC-HYP-FINAL-6.13.2 As-Built Docur		119	119	0%	25-Aug-26	05-Feb-27	73		
ASB-010	Compile Civil and Architectu	10	10	0%	25-Aug-26	07-Sep-26	172		
ASB-020	Compile Electrical As-Built D	10	10	0%	11-Jan-27	22-Jan-27	73		
ASB-030	Compile Mechanical As-Bui	10	10	0%	15-Dec-26	28-Dec-26	92		
ASB-040	Compile Controls and Fire A	10	10	0%	08-Jan-27	21-Jan-27	74		
ASB-050	Submit Final As-Built Docun	10	10	0%	25-Jan-27	05-Feb-27	73		
DC-HYP-FINAL-6.13.3 O&M Manuals		153	153	0%	10-Jun-26	08-Jan-27	93		
OMM-010	Compile Electrical O&M Ma	10	10	0%	14-Dec-26	25-Dec-26	93		
OMM-020	Compile Mechanical O&M I	10	10	0%	28-Aug-26	10-Sep-26	169		
OMM-030	Compile Fire and Life Safet	10	10	0%	10-Jun-26	23-Jun-26	226		
OMM-040	Compile BMS and DCIM C	10	10	0%	07-Aug-26	20-Aug-26	184		
OMM-050	Submit Final O&M Manuals	10	10	0%	28-Dec-26	08-Jan-27	93		
DC-HYP-FINAL-6.13.4 Training & Knc		284	13	0%	23-Jan-26	24-Feb-27	70		


© Oracle Corporation

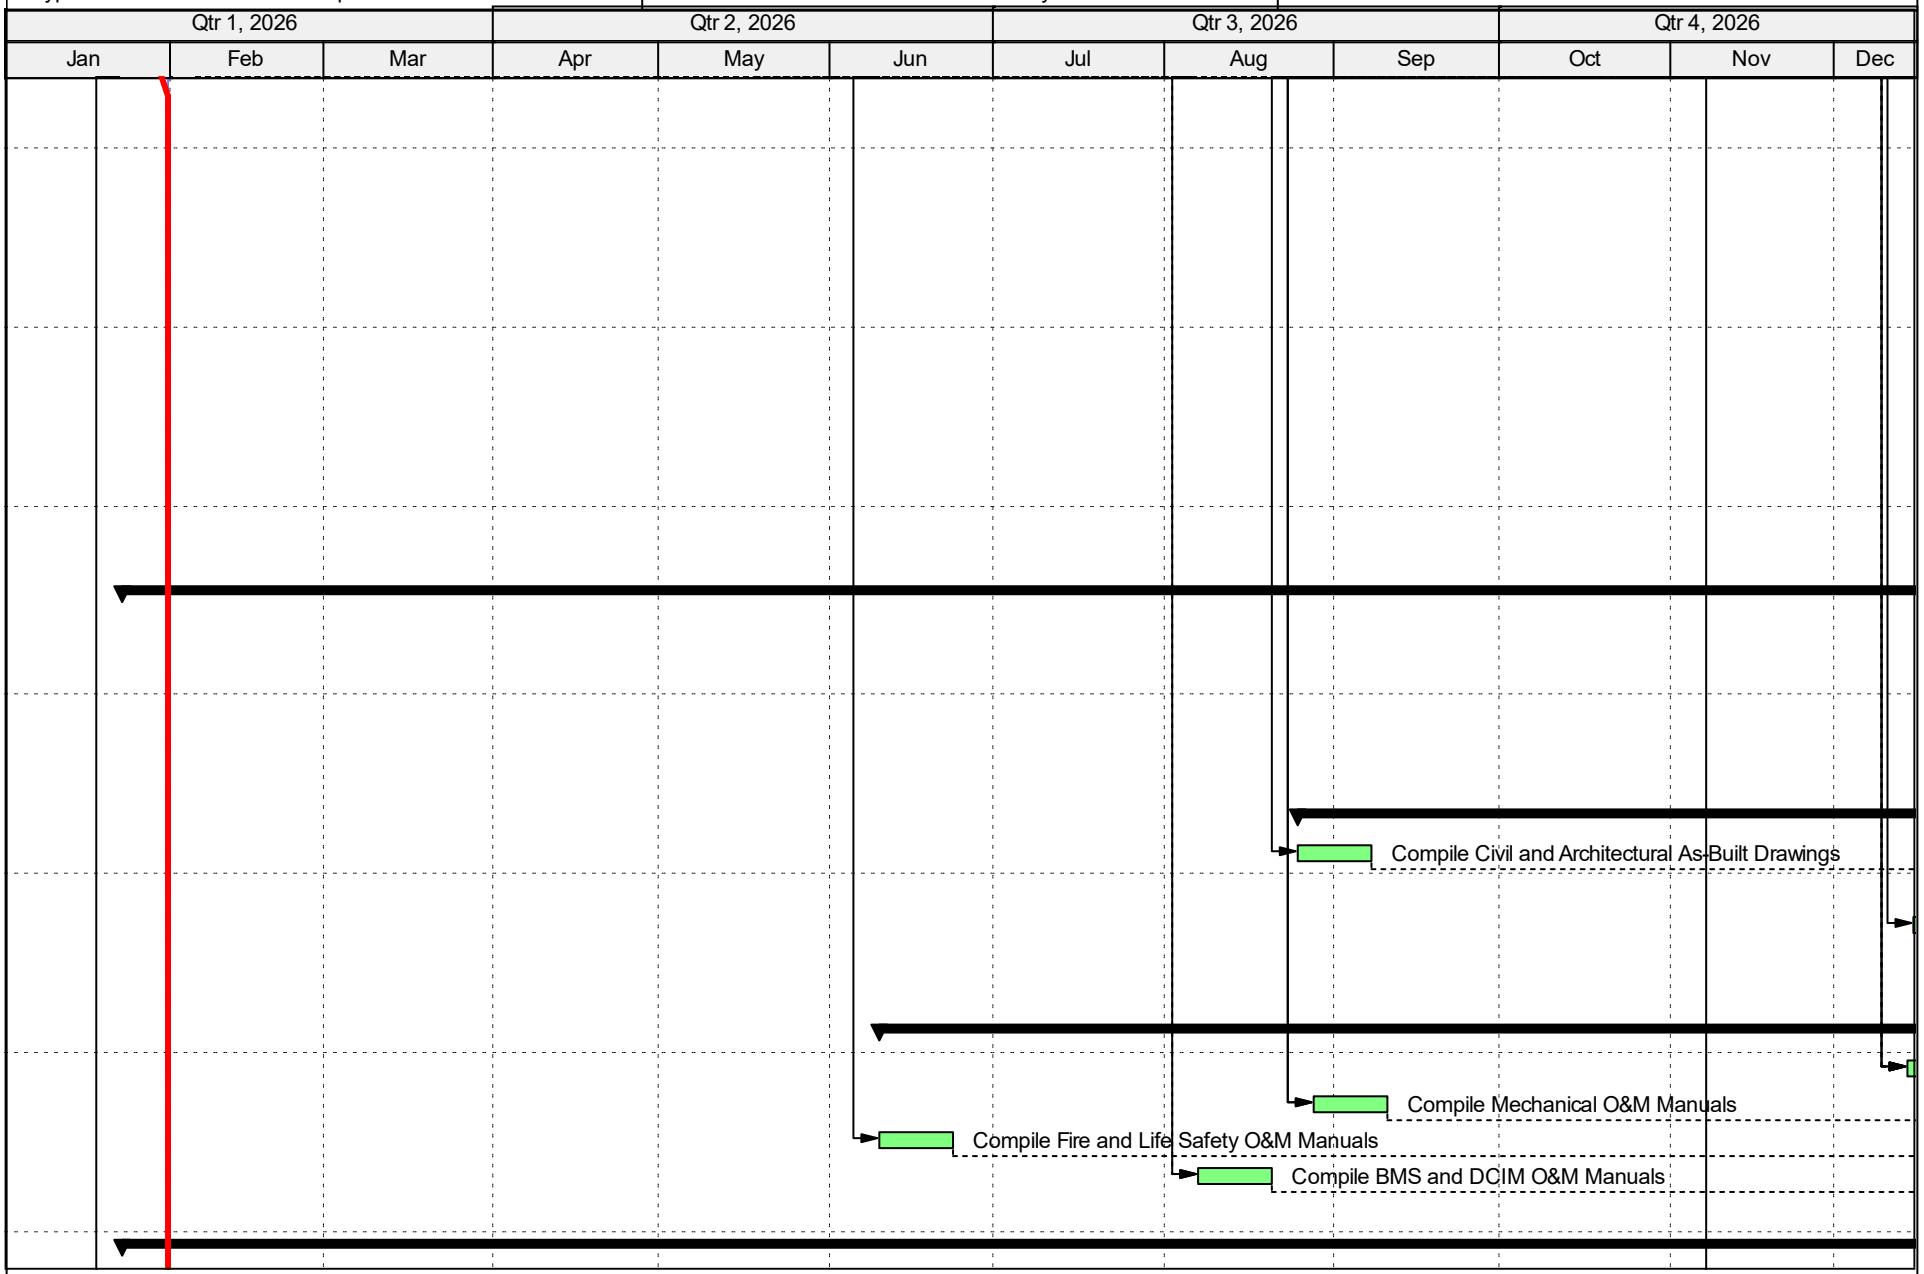

© Oracle Corporation

Activity ID	Activity Name	Planned Duration	Remaining Duration	Schedule % Complete	Start	Finish	Total Float	Qtr 4, 2025 Nov	Qtr 4, 2025 Dec
TRN-010	Develop Operations Training	5	0	100%	23-Jan-26	29-Jan-26			
TRN-020	Conduct Electrical Systems	5	5	0%	16-Feb-27	22-Feb-27	72		
TRN-030	Conduct Mechanical Syster	5	5	0%	15-Feb-27	19-Feb-27	73		
TRN-040	Conduct Fire and Life Safet	5	5	0%	08-Feb-27	12-Feb-27	78		
TRN-050	Conduct BMS and DCIM Ti	5	5	0%	18-Feb-27	24-Feb-27	70		
TRN-060	Operations Training Comple	0	0	0%		24-Feb-27	70		
DC-HYP-FINAL-6.13.5 Authority / Reg		13	13	0%	22-Feb-27	10-Mar-27	52		
AUT-010	Submit Final Authority Inspe	2	2	0%	22-Feb-27	23-Feb-27	52		
AUT-020	Conduct Fire Authority Insp	2	2	0%	24-Feb-27	25-Feb-27	52		
AUT-030	Conduct Electrical Authority	2	2	0%	24-Feb-27	25-Feb-27	52		
AUT-040	Resolve Authority Inspectio	2	2	0%	26-Feb-27	01-Mar-27	52		
AUT-050	Obtain Final Authority Appro	7	7	0%	02-Mar-27	10-Mar-27	52		
DC-HYP-FINAL-6.13.7 Final Documer		19	19	0%	16-Jun-27	12-Jul-27	0		
DFC-010	Compile Outstanding Defec	10	10	0%	16-Jun-27	29-Jun-27	0		
DFC-020	Rectify Outstanding Constr	7	7	0%	30-Jun-27	08-Jul-27	0		
DFC-030	Rectify Outstanding Systerr	7	7	0%	30-Jun-27	08-Jul-27	0		
DFC-040	Verify Outstanding Defects	2	2	0%	09-Jul-27	12-Jul-27	0		
DC-HYP-FINAL-6.13.8 Ready for Serv		129	129	0%	12-Nov-26	11-May-27	16		
FDT-010	Compile Final Handover Dc	5	5	0%	08-Feb-27	12-Feb-27	73		
FDT-020	Submit Commissioning Rec	5	5	0%	28-Apr-27	04-May-27	16		
FDT-030	Submit Testing Certificates	3	3	0%	29-Mar-27	31-Mar-27	40		
FDT-040	Submit Equipment Warrant	5	5	0%	12-Nov-26	18-Nov-26	135		
FDT-050	Final Handover Documenta	5	5	0%	05-May-27	11-May-27	16		
DC-HYP-FINAL-6.13.9 Final Acceptar		49	49	0%	11-May-27	19-Jul-27	0		
RFS-010	Confirm Operational Readir	5	5	0%	13-Jul-27	19-Jul-27	0		
RFS-020	Confirm Systems Acceptan	5	5	0%	16-Jun-27	22-Jun-27	19		
RFS-030	Confirm Documentation an	0	0	0%		11-May-27	49		
RFS-040	Ready for Service	0	0	0%		19-Jul-27	0		
DC-HYP-FINAL-6.13.6 Client Final Ins		11	11	0%	01-Jun-27	15-Jun-27	0		
CFI-010	Conduct Client Final Techni	2	2	0%	01-Jun-27	02-Jun-27	0		
CFI-020	Conduct Client Operations	5	5	0%	03-Jun-27	09-Jun-27	0		
CFI-030	Resolve Client Final Inspec	2	2	0%	10-Jun-27	11-Jun-27	0		
CFI-040	Client Final Inspection Acce	2	2	0%	14-Jun-27	15-Jun-27	0		

© Oracle Corporation

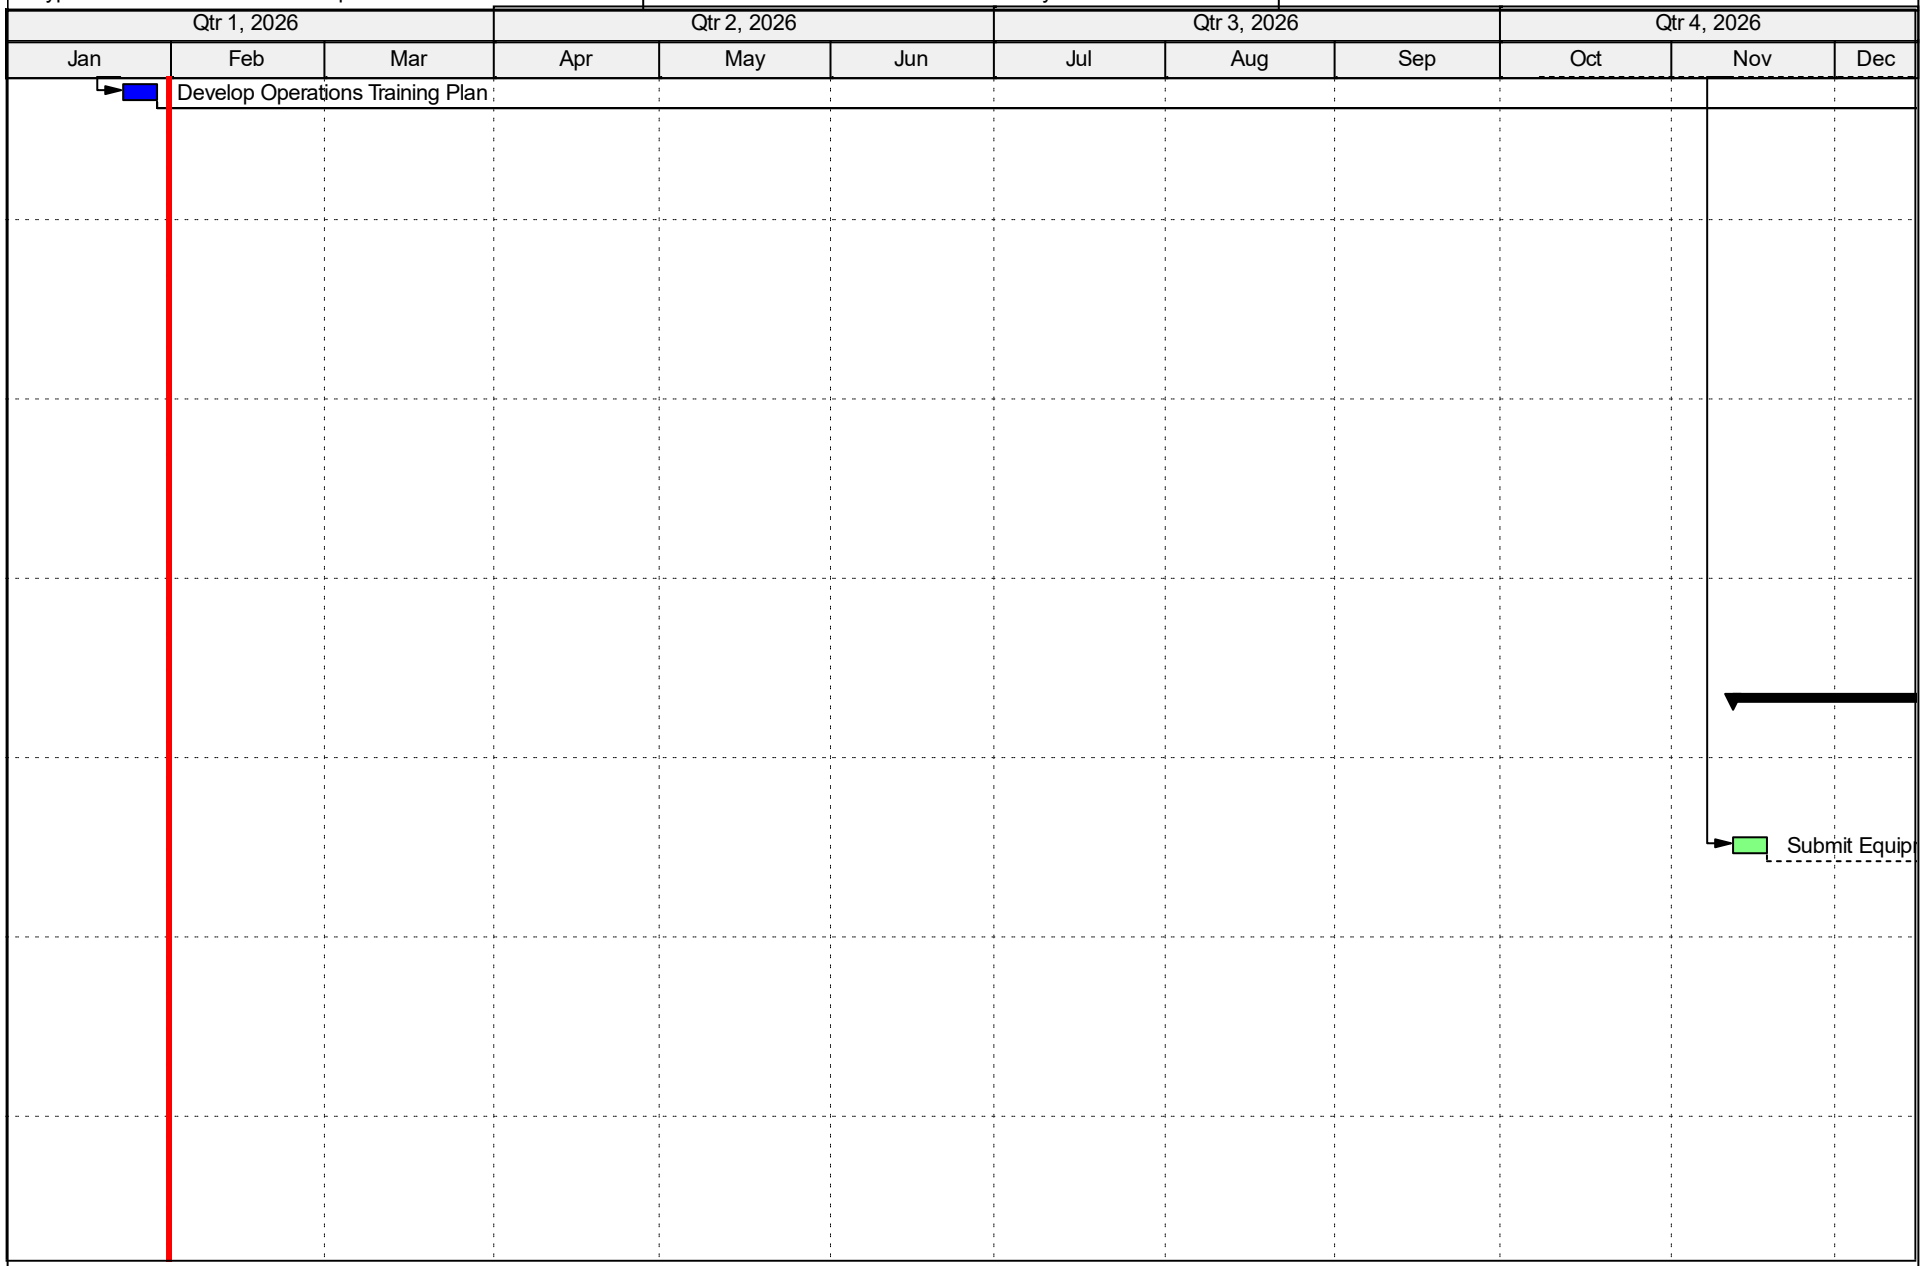

© Oracle Corporation
